

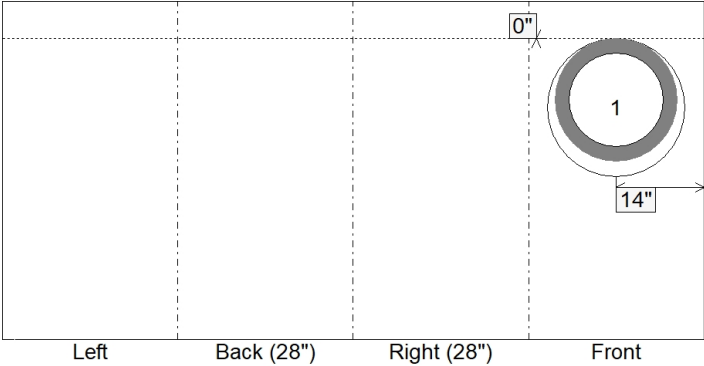


Job Name: 26-1057 - The Courtside Enclave Final SP Job Location: Antioch, TN Contractor: Hayes Pipe Supply					Plant: 100 9/8/2026 9:08:37 AM		Tech: J. Horsley PC: E. Bradley				
Structure ID: ST5 (7)											
P1		BX2828-06BA48		BOX BASE 6inW, 6inF F/n							
P2) 28" x 28" - CASTING HEIGHT - 6" P1) 28" x 28" - BOX BASE 6inW, 6inF F/n - 48" 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 22"					0 lb 3901 lb 0 lb 0 lb ----- 3901 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,00 PSI AT 28 DAYS. 3. CASTING (JBS 4310 F/G) SUPPLIED BY CONTRACTOR. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 583.97' Rim to Invert: 4.45' Slack: 1.656' Sump: 2.256' Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	579.52'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)  Invert: 1 Degree: 0° Horz: 14" Hole: 22" Up(): 0"  Invert: 1 Degree: 0° Horz: 14" Hole: 22" Up(): 0" INSIDE WALL DIMENSIONS  Left Back (28") Right (28") Front EXT											
