

Contractor: Connhurst, LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 4.58'


Floor Height: 0"

Slack: 0.96"

- RISER/WALLS (As .12)



0 | b

Structure Total: 4676 lb

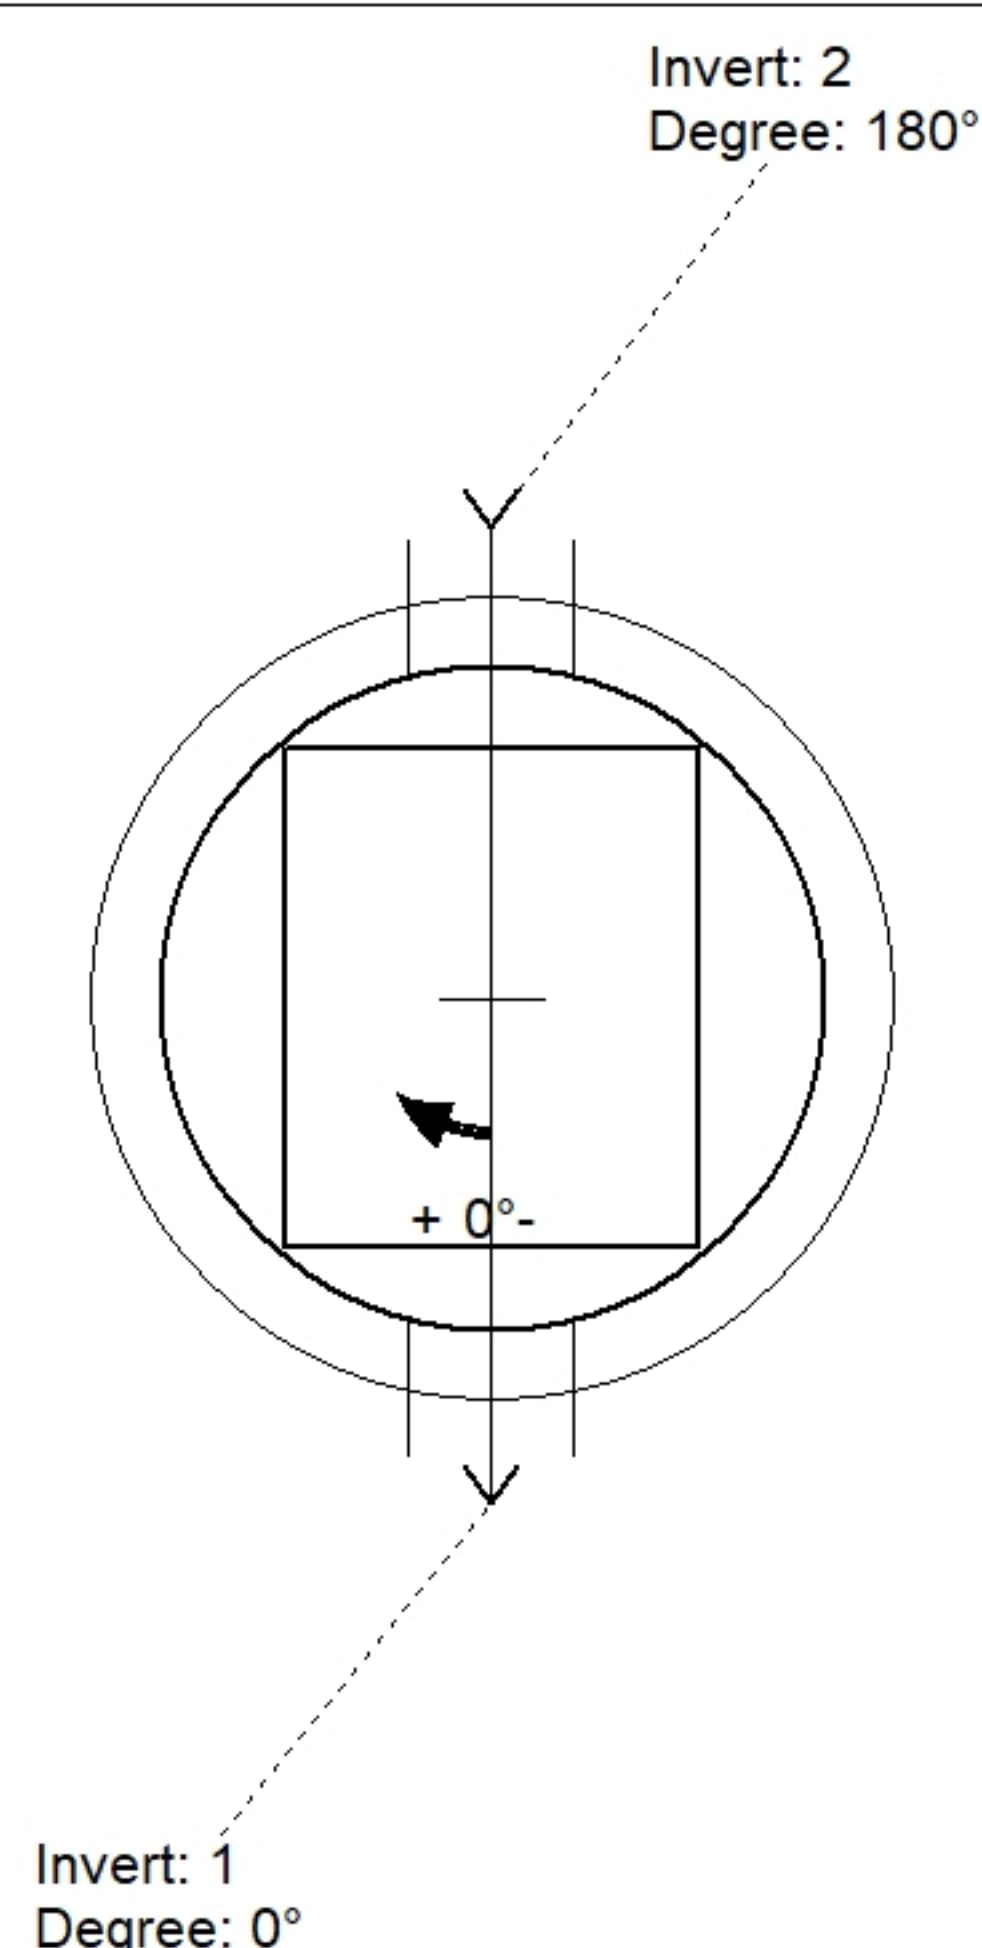

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	608.25'							
Reducer								
Invert 1	603.67'	0°	8" PVC C900	9.05"	12" x 12"	DOGHOUSE 12"x12"	4"	P2
Invert 2	603.67'	180°	8" PVC C900	9.05"	12" x 12"	DOGHOUSE 12"x12"	4"	P2
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

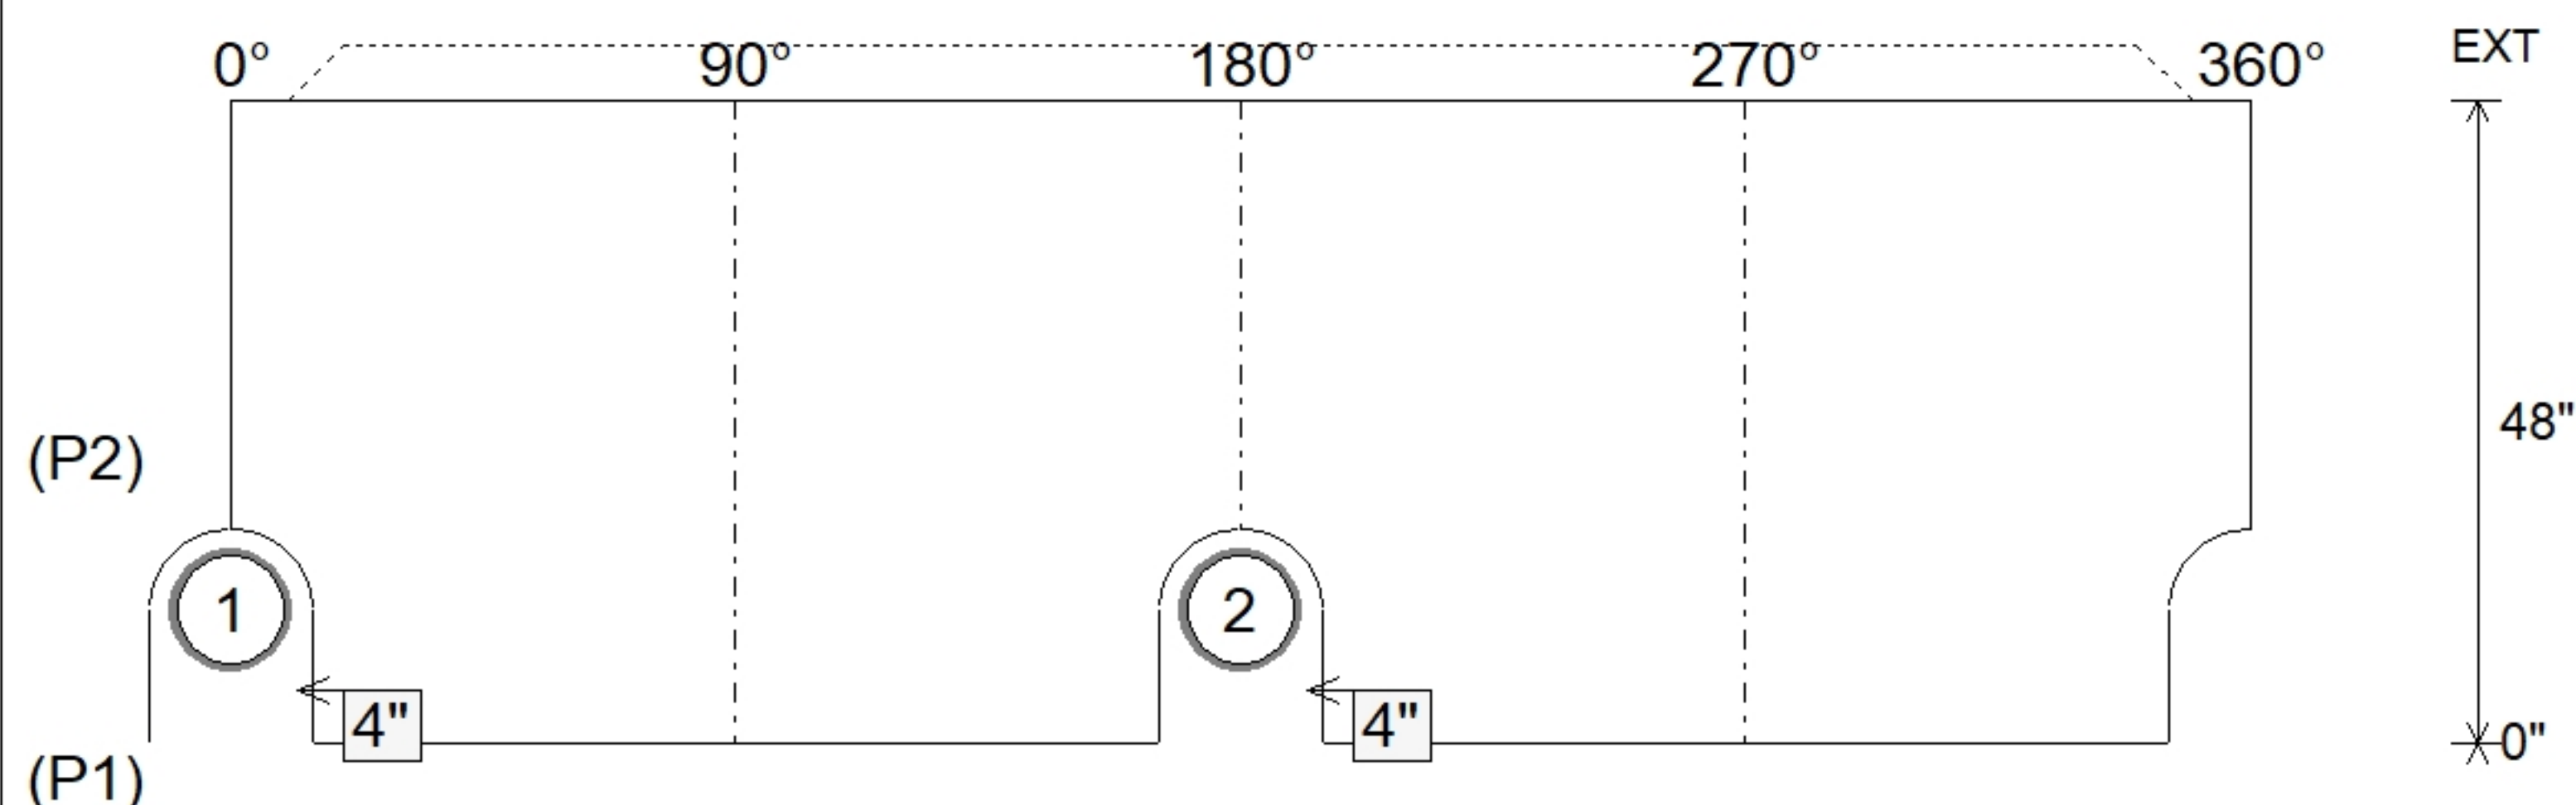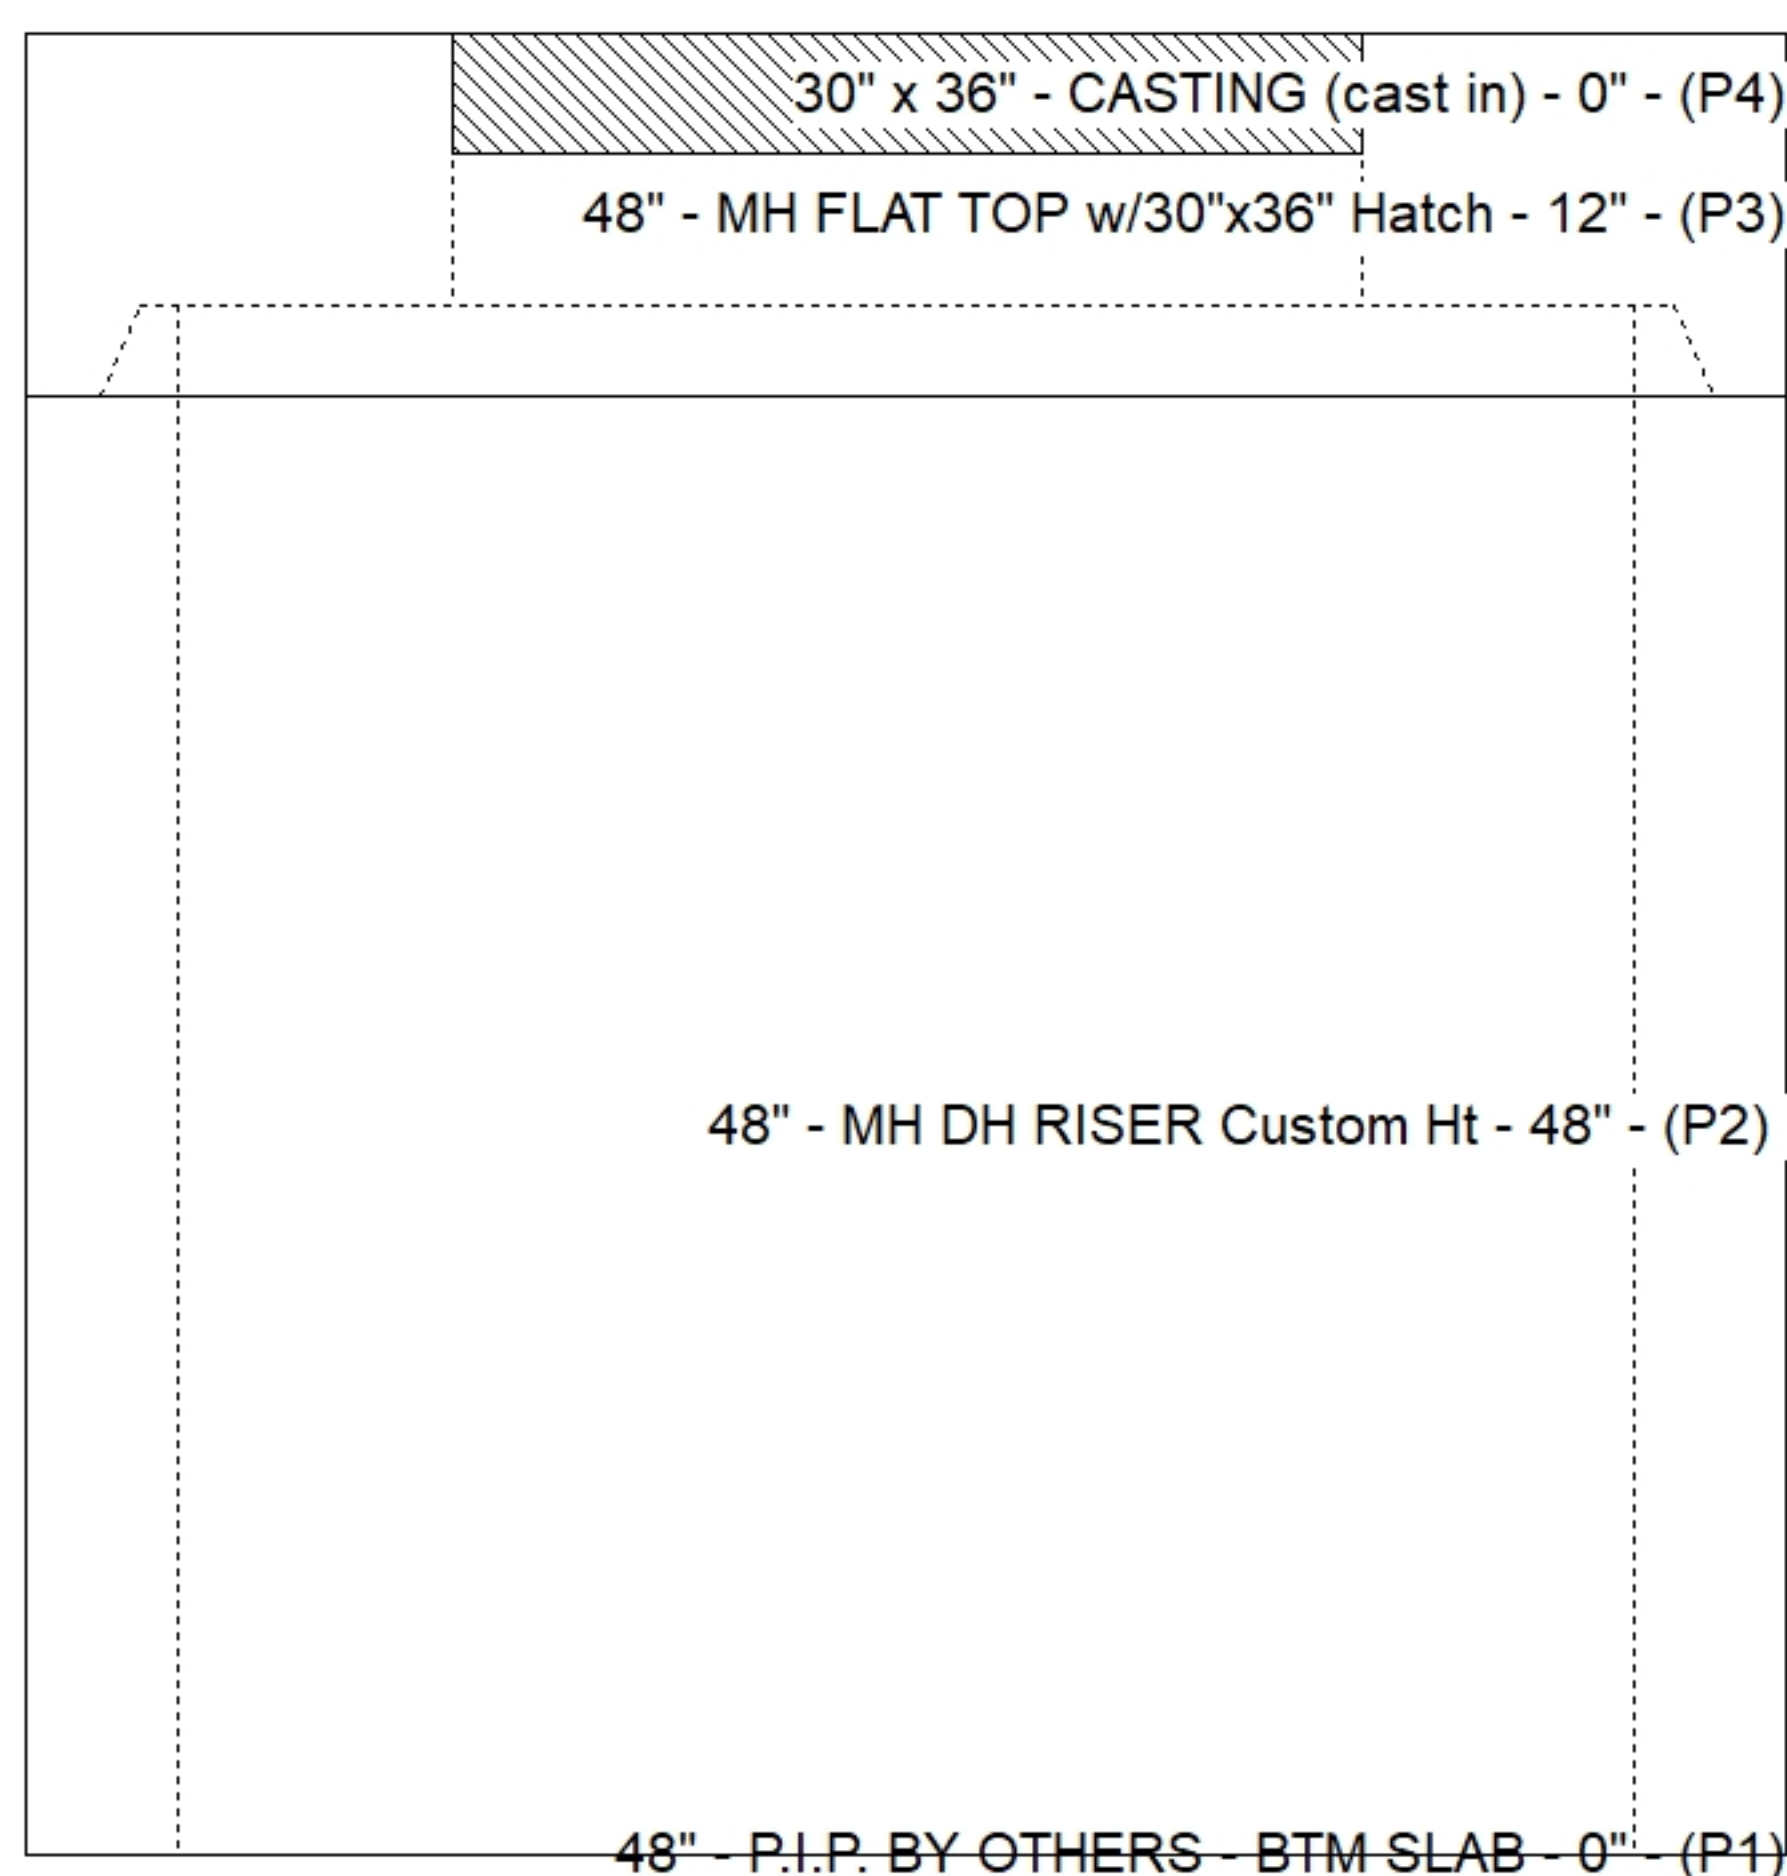

Submittal Drawing
7/17/2026 11:24:41 AM

SUBMITTAL
APPROVED BY:
