

Contractor: Connhurst, LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 11.44'

Floor Height: 6"


Slack: 0.28"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) PSX - 16M DD


16 lb

Structure Total: 11902 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	553.34'							
Reducer								
Invert 1	541.9'	0°	12" DI	13.2"	16"	PSX 16M DD	0.32"	P1
Invert 2	542'	173°	12" PVC SDR35	12.5"	16"	PSX 16M DD	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

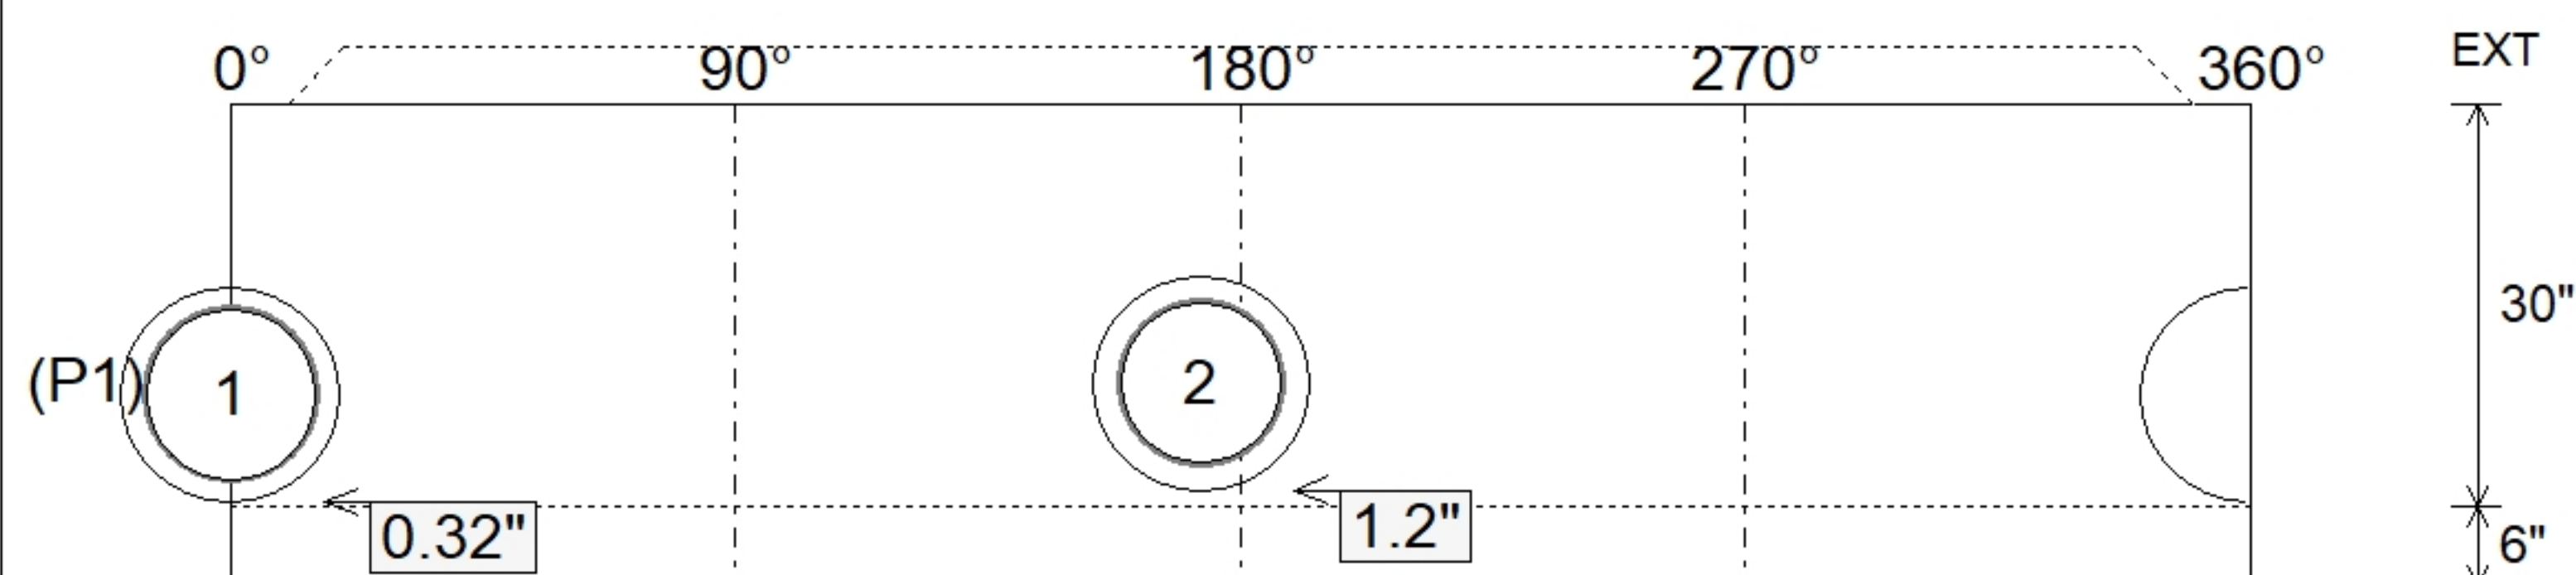

48" - MH BASE - 30" - (P1)

SUBMITTAL
APPROVED BY:
