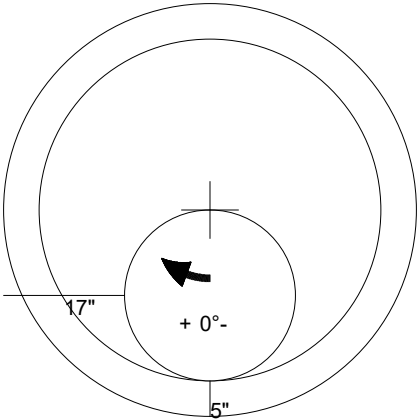



Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC		Plant: 100 6/2/2026 10:56:11 AM	Tech: Jared - F PC: E. Bradley	
Structure ID: A2 (6)		P3 MH048CN36-S		
ECC CONE w/ 24" HOLE F/G				
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 16M DD		0 lb 3000 lb 4192 lb 3255 lb 1440 lb 0 lb 0 lb 16 lb ----- Structure Total: 11902 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. ALL PIPE CONNECTORS TO INCLUDE DOUBLE PIPE BANDS. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 36" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
