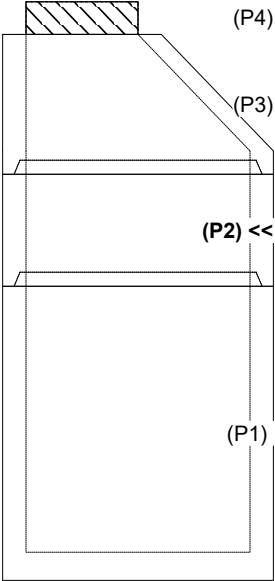




Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC					Plant: 100 6/2/2026 10:56:53 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A3 (7)											
P2 MH048RS24S MH RISER T/G											
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 24" P1) 48" - MH BASE Custom Ht T/n - 57" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 2) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 16M DD 1) Drop Tee - 12" PVC 1) Drop Elbow - 12" PVC						0 lb 2050 lb 1677 lb 5122 lb 1440 lb 0 lb 0 lb 8 lb 0 lb 0 lb Structure Total: 10297 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. EXTERIOR DROP ASSEMBLY PROVIDED BY ICAST. 6. ALL PIPE CONNECTORS TO INCLUDE DOUBLE PIPE BANDS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 552.77' Rim to Invert: 9.68' Slack: 0.16" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 1677 lb Volume (Net): 0.43cu.yd		
