

Contractor: Connhurst, LLC

Plant: 100



Size: 48"

Rim to Invert: 9.68'


Floor Height: 6"

Slack: 0.16"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


0 lb

Structure Total: 13012 lb

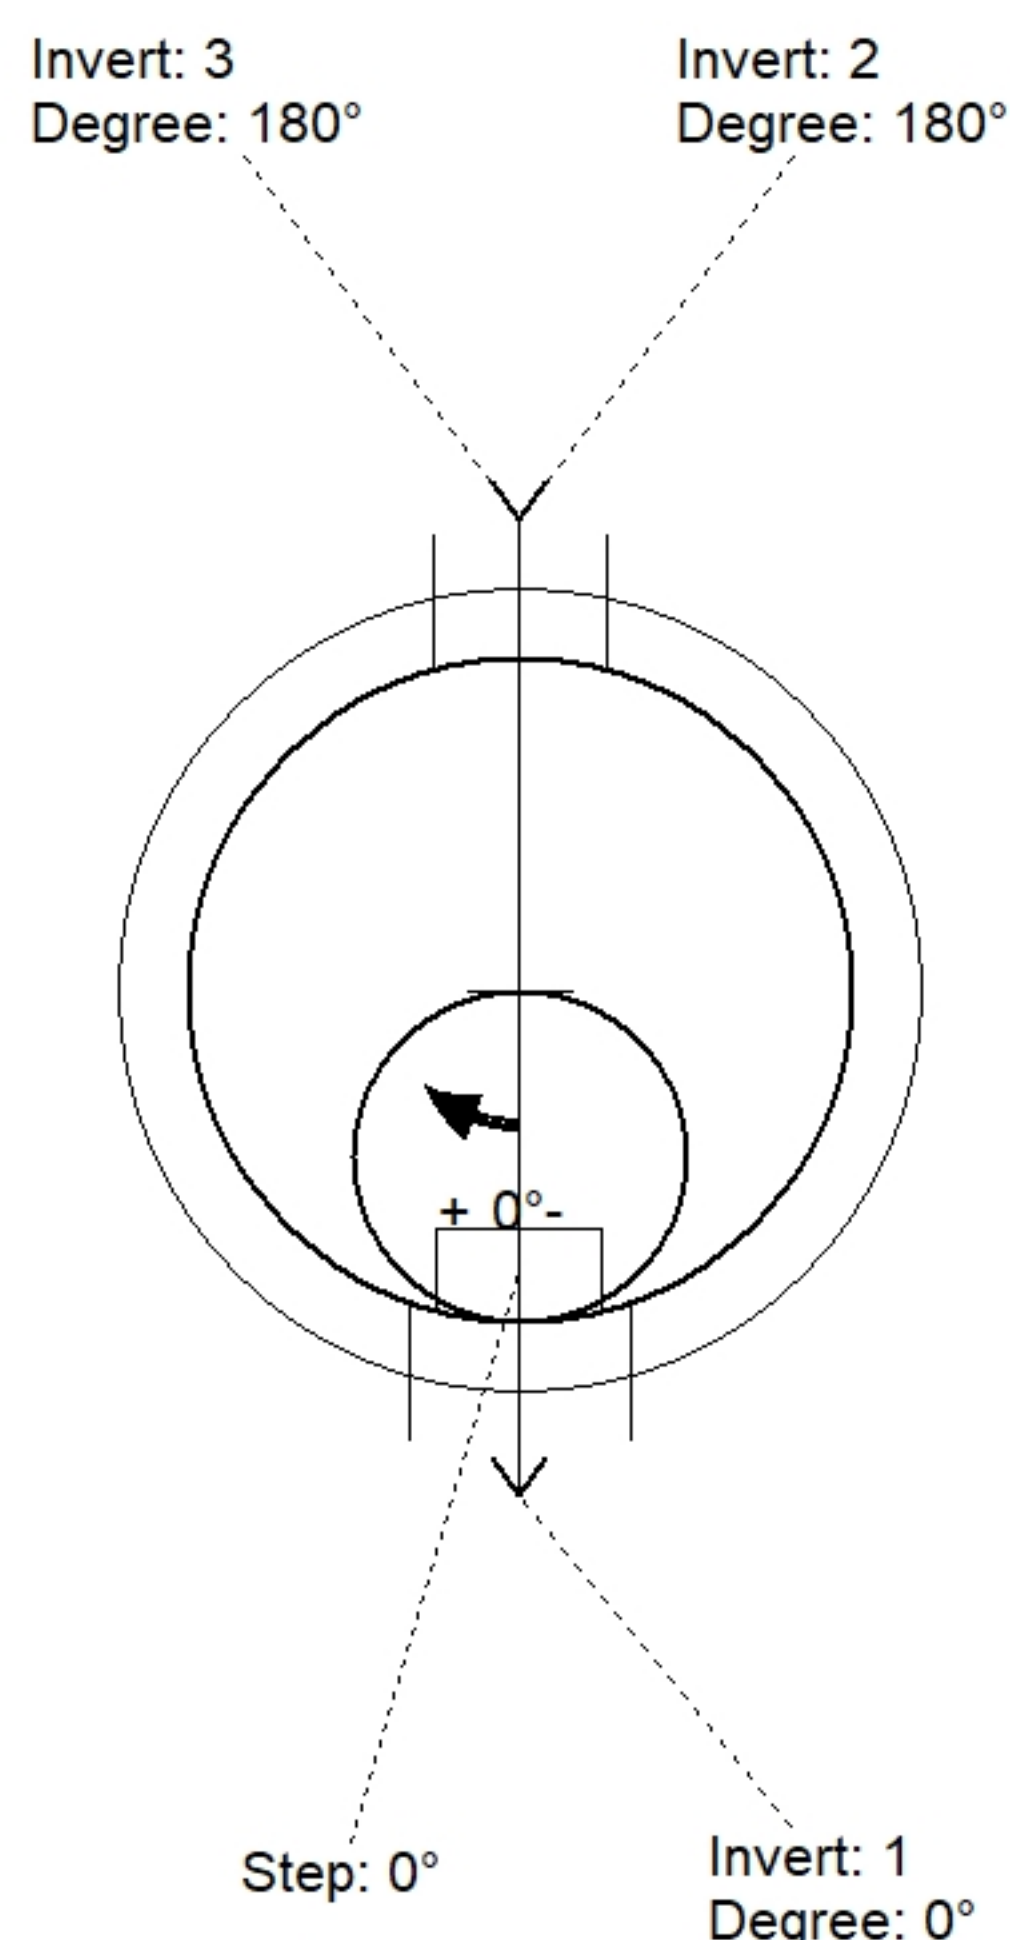

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	552.77'							
Reducer								
Invert 1	543.09'	0°	12" PVC SDR35	12.5"	16"	PSX 16M DD	0"	P1
Invert 2	545.41'	180°	12" PVC SDR35	12.5"	12.5"	Drop Tee 12" PVC	29.59"	P1
Invert 3	543.19'	180°	12" PVC SDR35	12.5"	12.5"	Drop Elbow 12" PVC	2.95"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

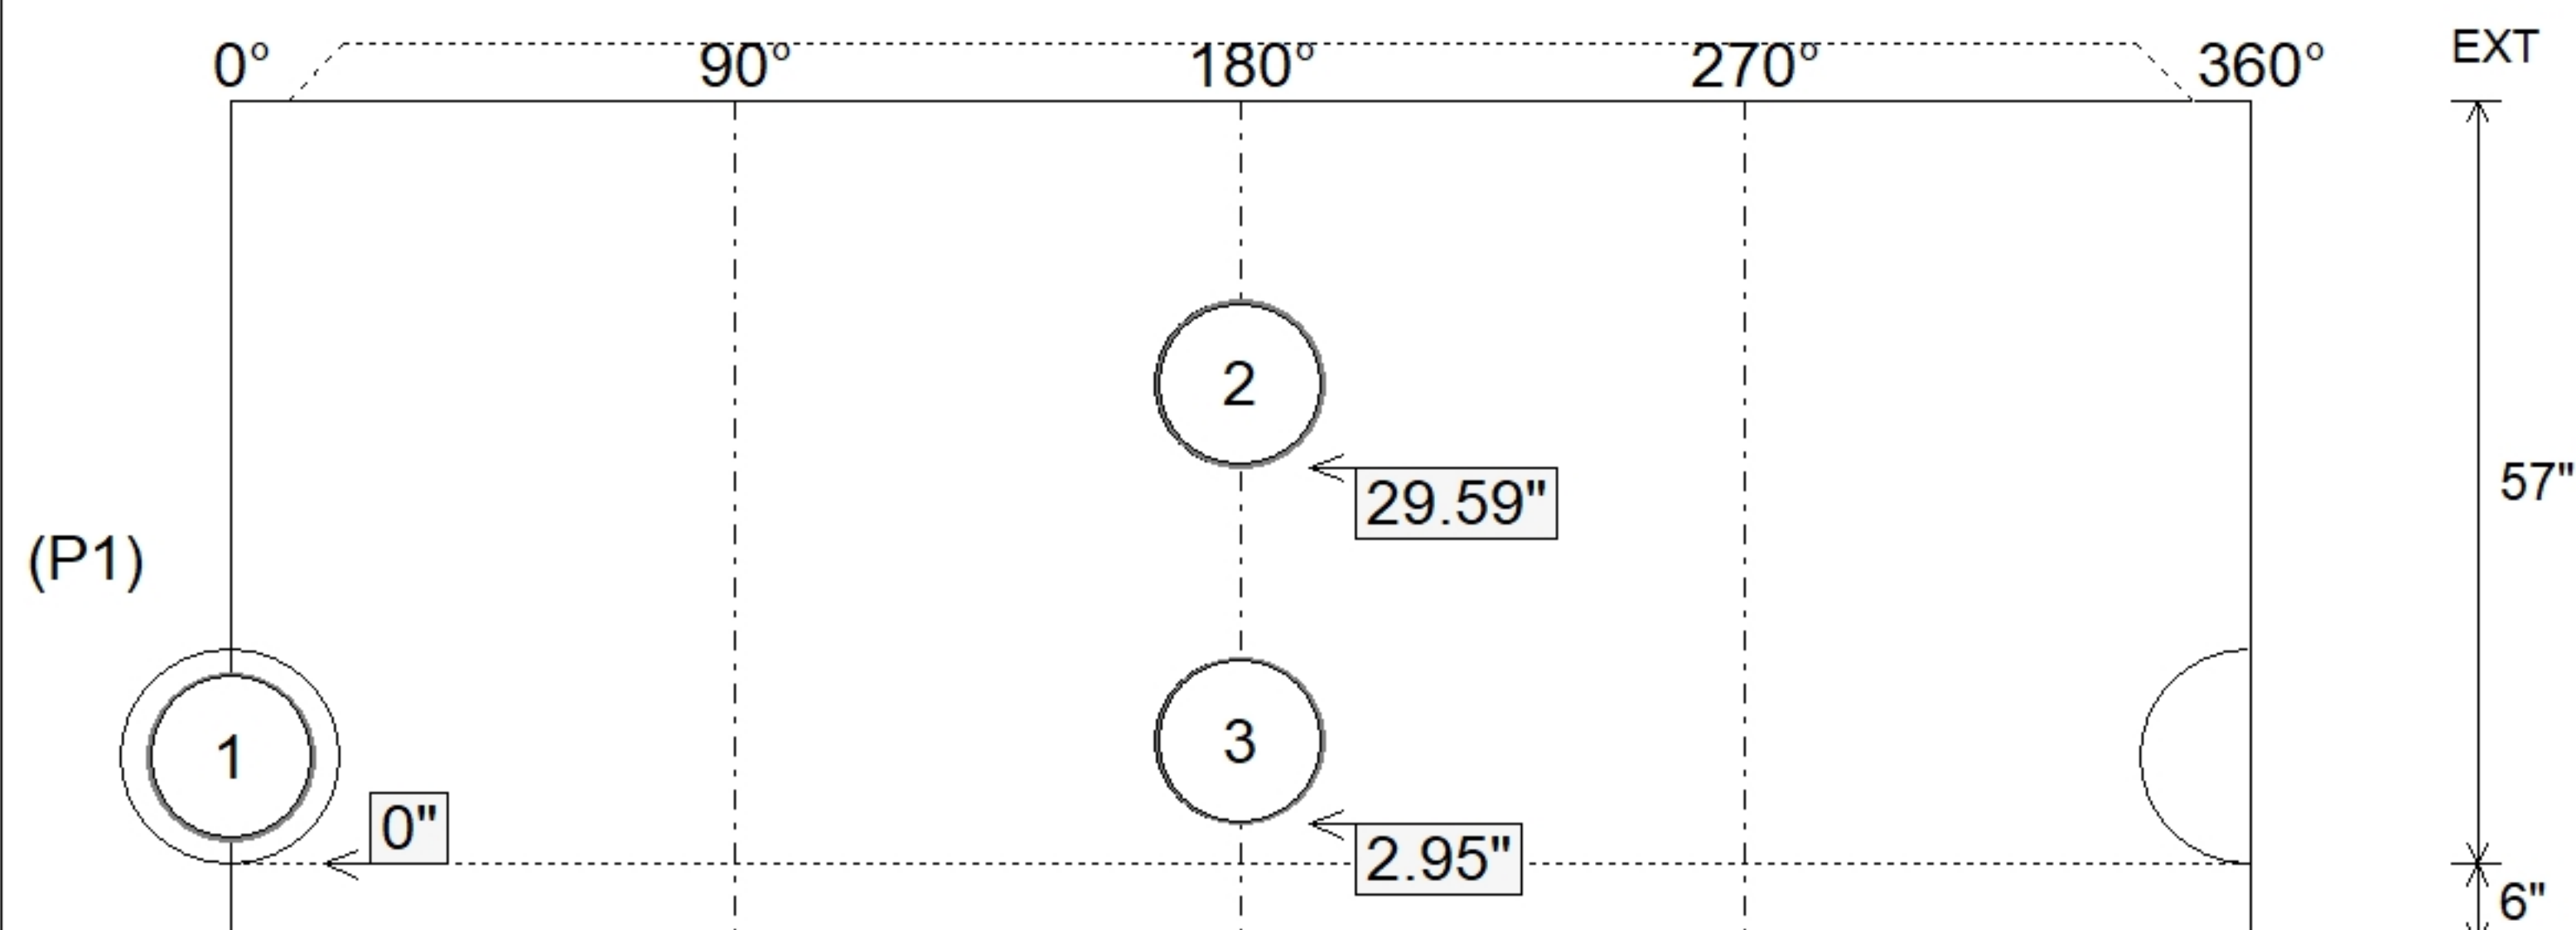

SUBMITTAL
APPROVED BY:
