



Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC					Plant: 100 6/2/2026 10:54:39 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A6 (10)											
P1 MH048BAVF			MH BASE Custom Ht T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 26" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 16M DD					0 lb 1561 lb 2975 lb 1440 lb 0 lb 0 lb 16 lb ----- Structure Total: 5992 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. ALL PIPE CONNECTORS TO INCLUDE DOUBLE PIPE BANDS. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 550.23' Rim to Invert: 3.62' Slack: 0.44" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	546.61'	0°	0"	12" PVC SDR35	12.5"	PSX 16M DD	16"	16.312"	0"	0"	
Invert 2	546.71'	165°	83.5"	12" DI	13"	PSX 16M DD	16"	16.312"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

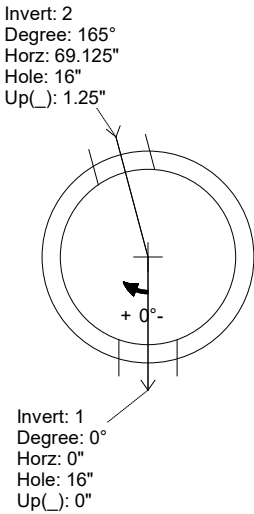

RIGHT-SIDE UP VIEW (int. dimensions)

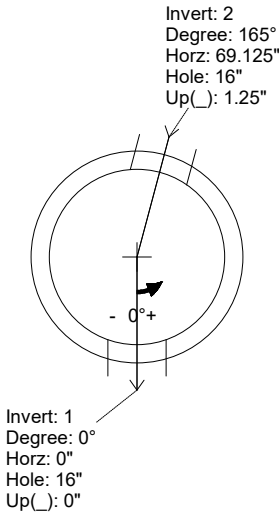

UPSIDE-DOWN VIEW (int. dimensions)




Diagram showing components P1, P2, and P3 with dimensions.

INSIDE WALL DIMENSIONS






Diagram showing inside wall dimensions with labels 1.25, 69.125, and 0.

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 26" Height (Ext): 32"	Weight (Net): 2975 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC				Plant: 100 6/2/2026 10:54:39 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: A6 (10)										
P1 MH048BAVF				MH BASE Custom Ht T/n						
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 26" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 16M DD					0 lb 1561 lb 2975 lb 1440 lb 0 lb 0 lb 16 lb ----- Structure Total: 5992 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. ALL PIPE CONNECTORS TO INCLUDE DOUBLE PIPE BANDS. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 550.23' Rim to Invert: 3.62' Slack: 0.44" Sump: 2" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	546.61'	0°	0"	12" PVC SDR35	12.5"	PSX 16M DD	16"	16.312"	0"	0"
Invert 2	546.71'	165°	83.5"	12" DI	13"	PSX 16M DD	16"	16.312"	1.25"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

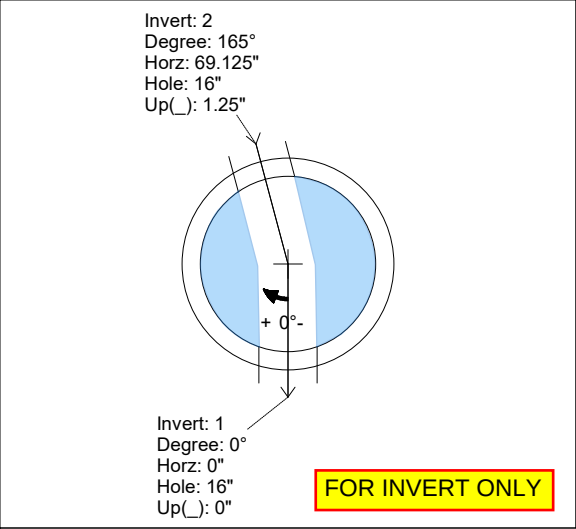

RIGHT-SIDE UP VIEW (int. dimensions)

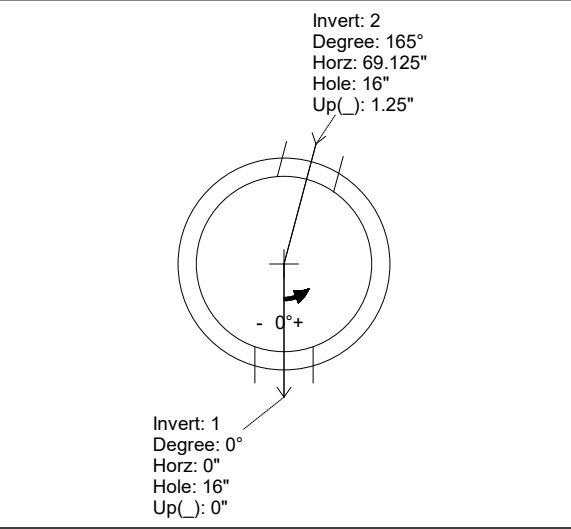

UPSIDE-DOWN VIEW (int. dimensions)





Diagram showing components P1, P2, and P3.

INSIDE WALL DIMENSIONS

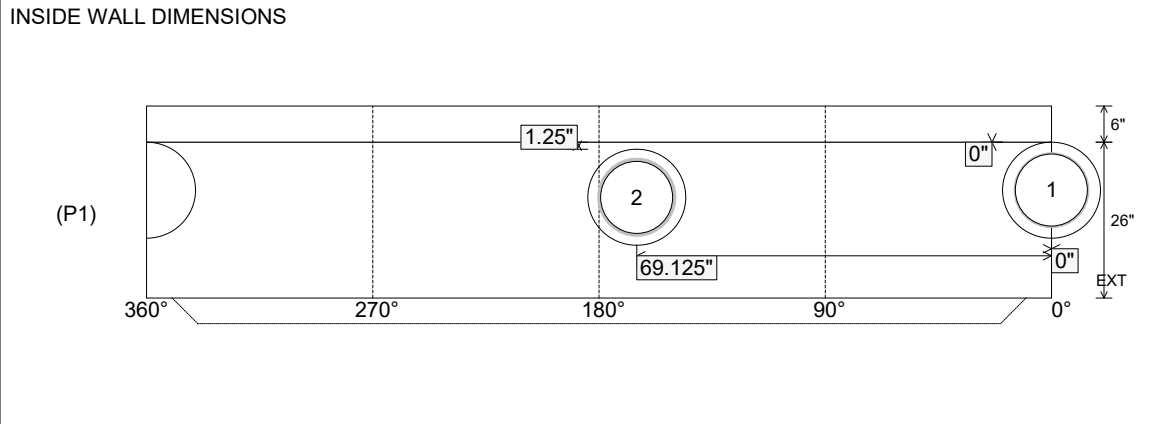

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 26" Height (Ext): 32"	Weight (Net): 2975 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--
