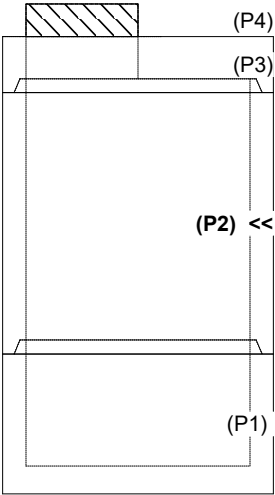

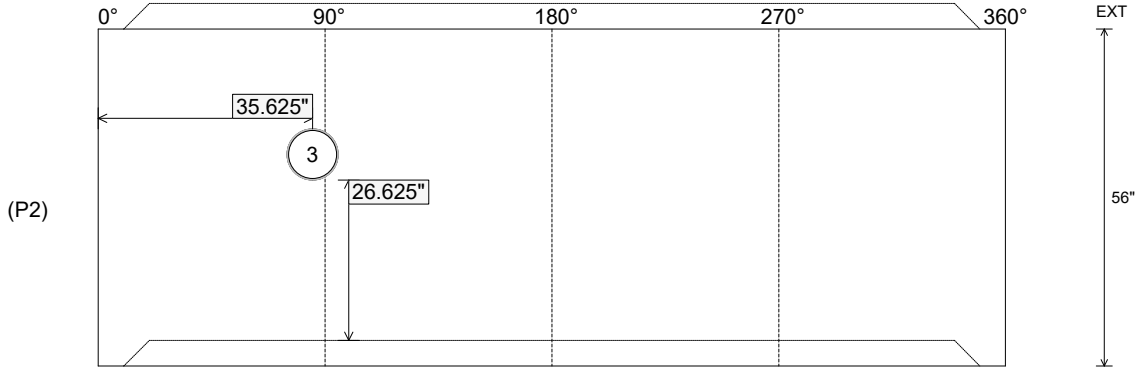


Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC					Plant: 100 6/2/2026 10:56:55 AM		Tech: Jared - F PC: E. Bradley						
Structure ID: A8 (12)													
P2 MH048RSVF-D				MH RISER Custom Ht T/G									
P4) 24" - CASTING HEIGHT - 7" P3) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P2) 48" - MH RISER Custom Ht T/G - 56" P1) 48" - MH BASE T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 16M DD 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC						0 lb 1561 lb 3888 lb 2811 lb 1440 lb 0 lb 0 lb 16 lb 0 lb 0 lb ----- Structure Total: 9717 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. EXTERIOR DROP ASSEMBLY @ 85°, PROVIDED BY ICAST. 6. ALL PIPE CONNECTORS TO INCLUDE DOUBLE PIPE BANDS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 560.41'		Rim to Invert: 8.09'		Slack: 0.08"		Sump: 2"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3	556.75'	85°	43"	8" PVC SDR35	8.5"	Drop Tee 8" PVC	8.5"	8.545"	26.625"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 56" Height (Ext): 56"		Weight (Net): 3888 lb Volume (Net): 0.99cu.yd			
