

Contractor: Connhurst, LLC

Plant: 100



Size: 48"

Rim to Invert: 8.09'

Floor Height: 6"


Slack: 0.08"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


1) Drop Elbow - 8" PVC

0 lb


Structure Total: 13417 lb

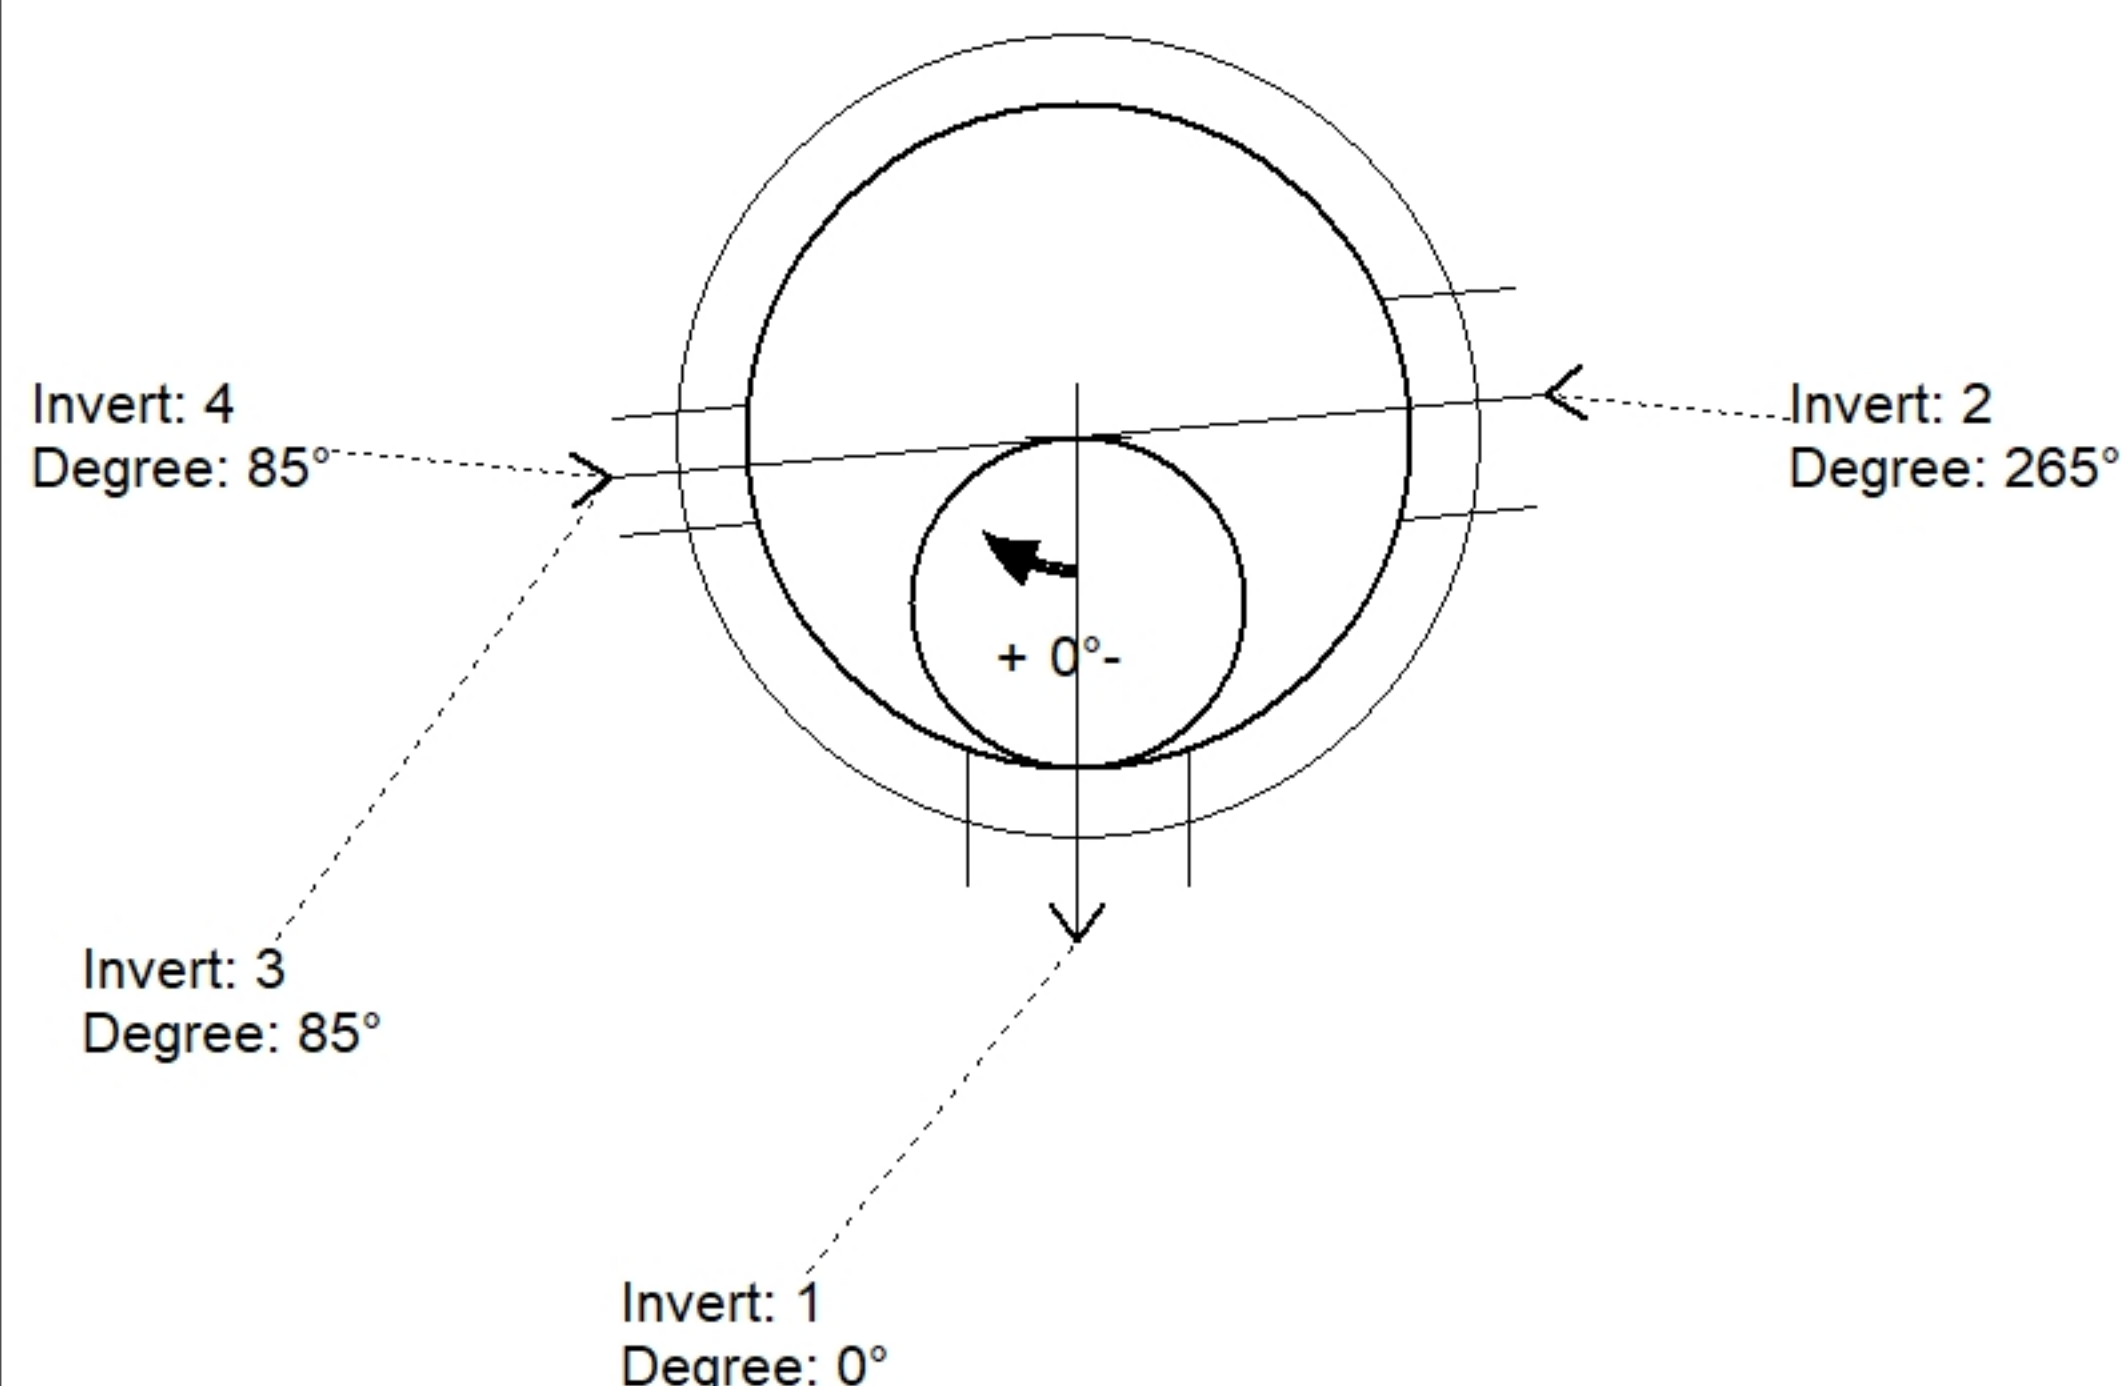

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	560.41'							
Reducer								
Invert 1	552.32'	0°	12" DI	13.2"	16"	PSX 16M DD	0.32"	P1
Invert 2	552.42'	265°	12" DI	13.2"	16"	PSX 16M DD	1.52"	P1
Invert 3	556.75'	85°	8" PVC SDR35	8.5"	8.5"	Drop Tee 8" PVC	26.66"	P2
Invert 4	552.52'	85°	8" PVC SDR35	8.5"	8.5"	Drop Elbow 8" PVC	4.15"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

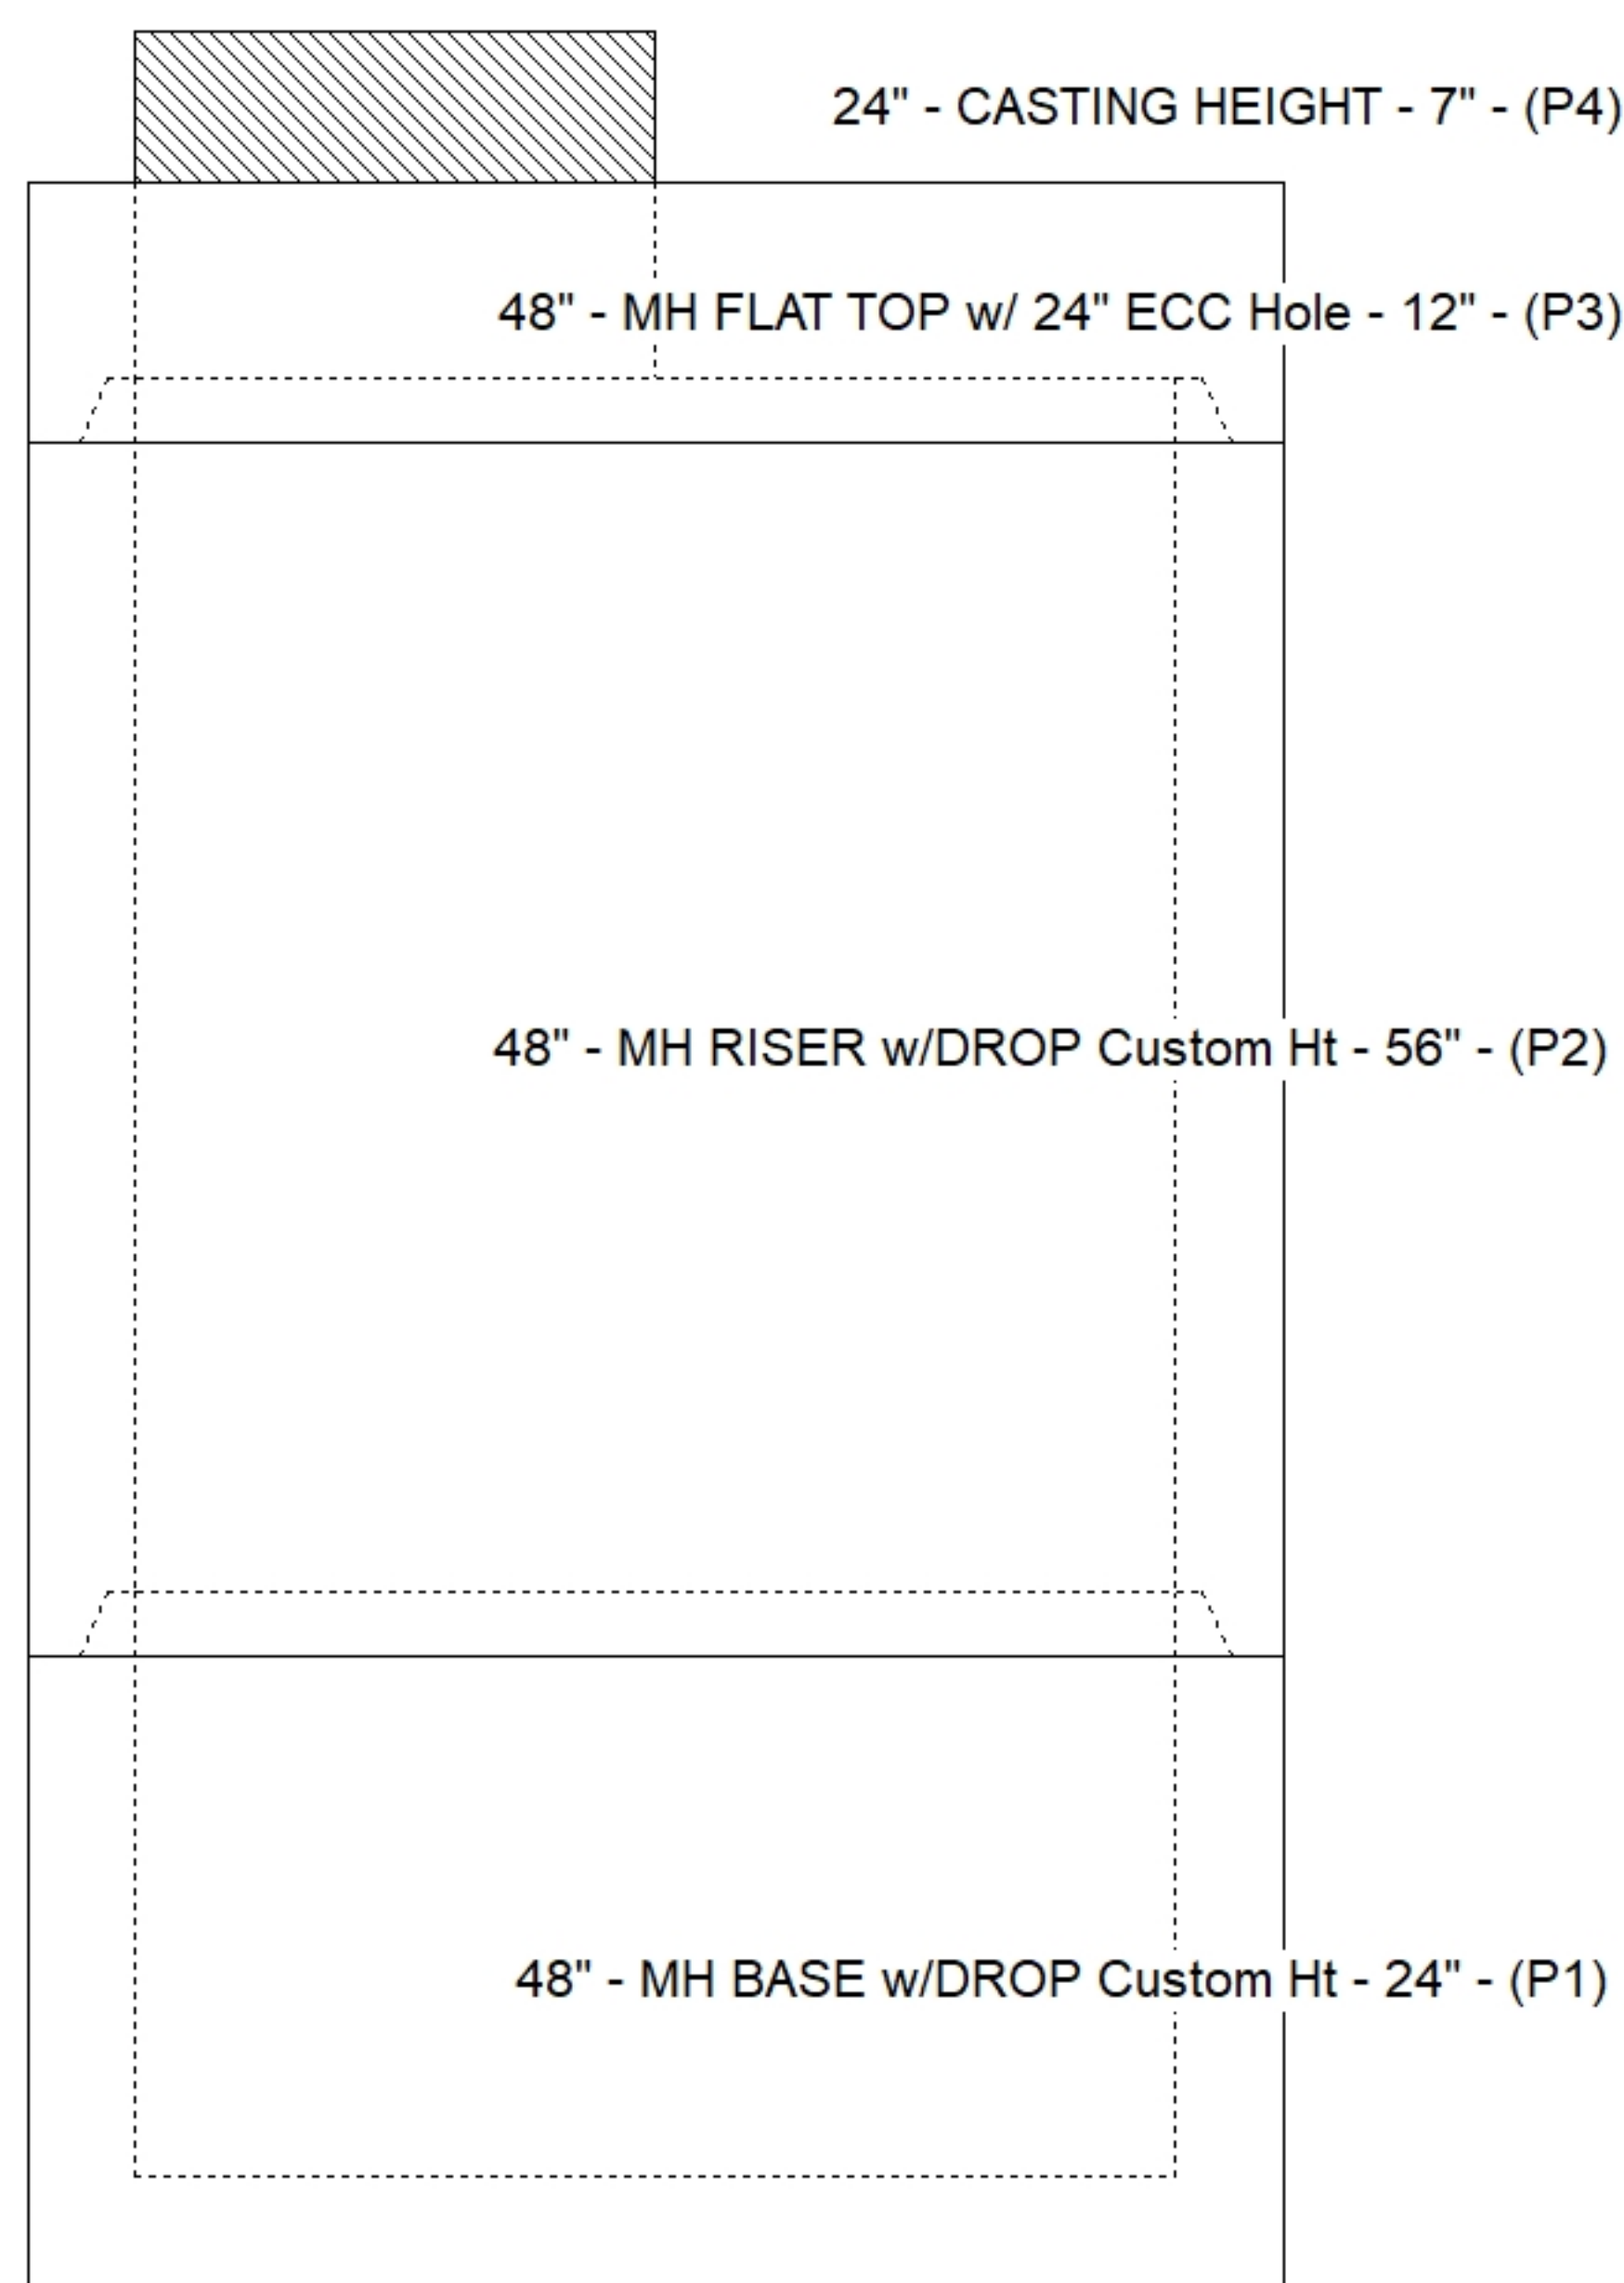

Default - Interior Dimensions

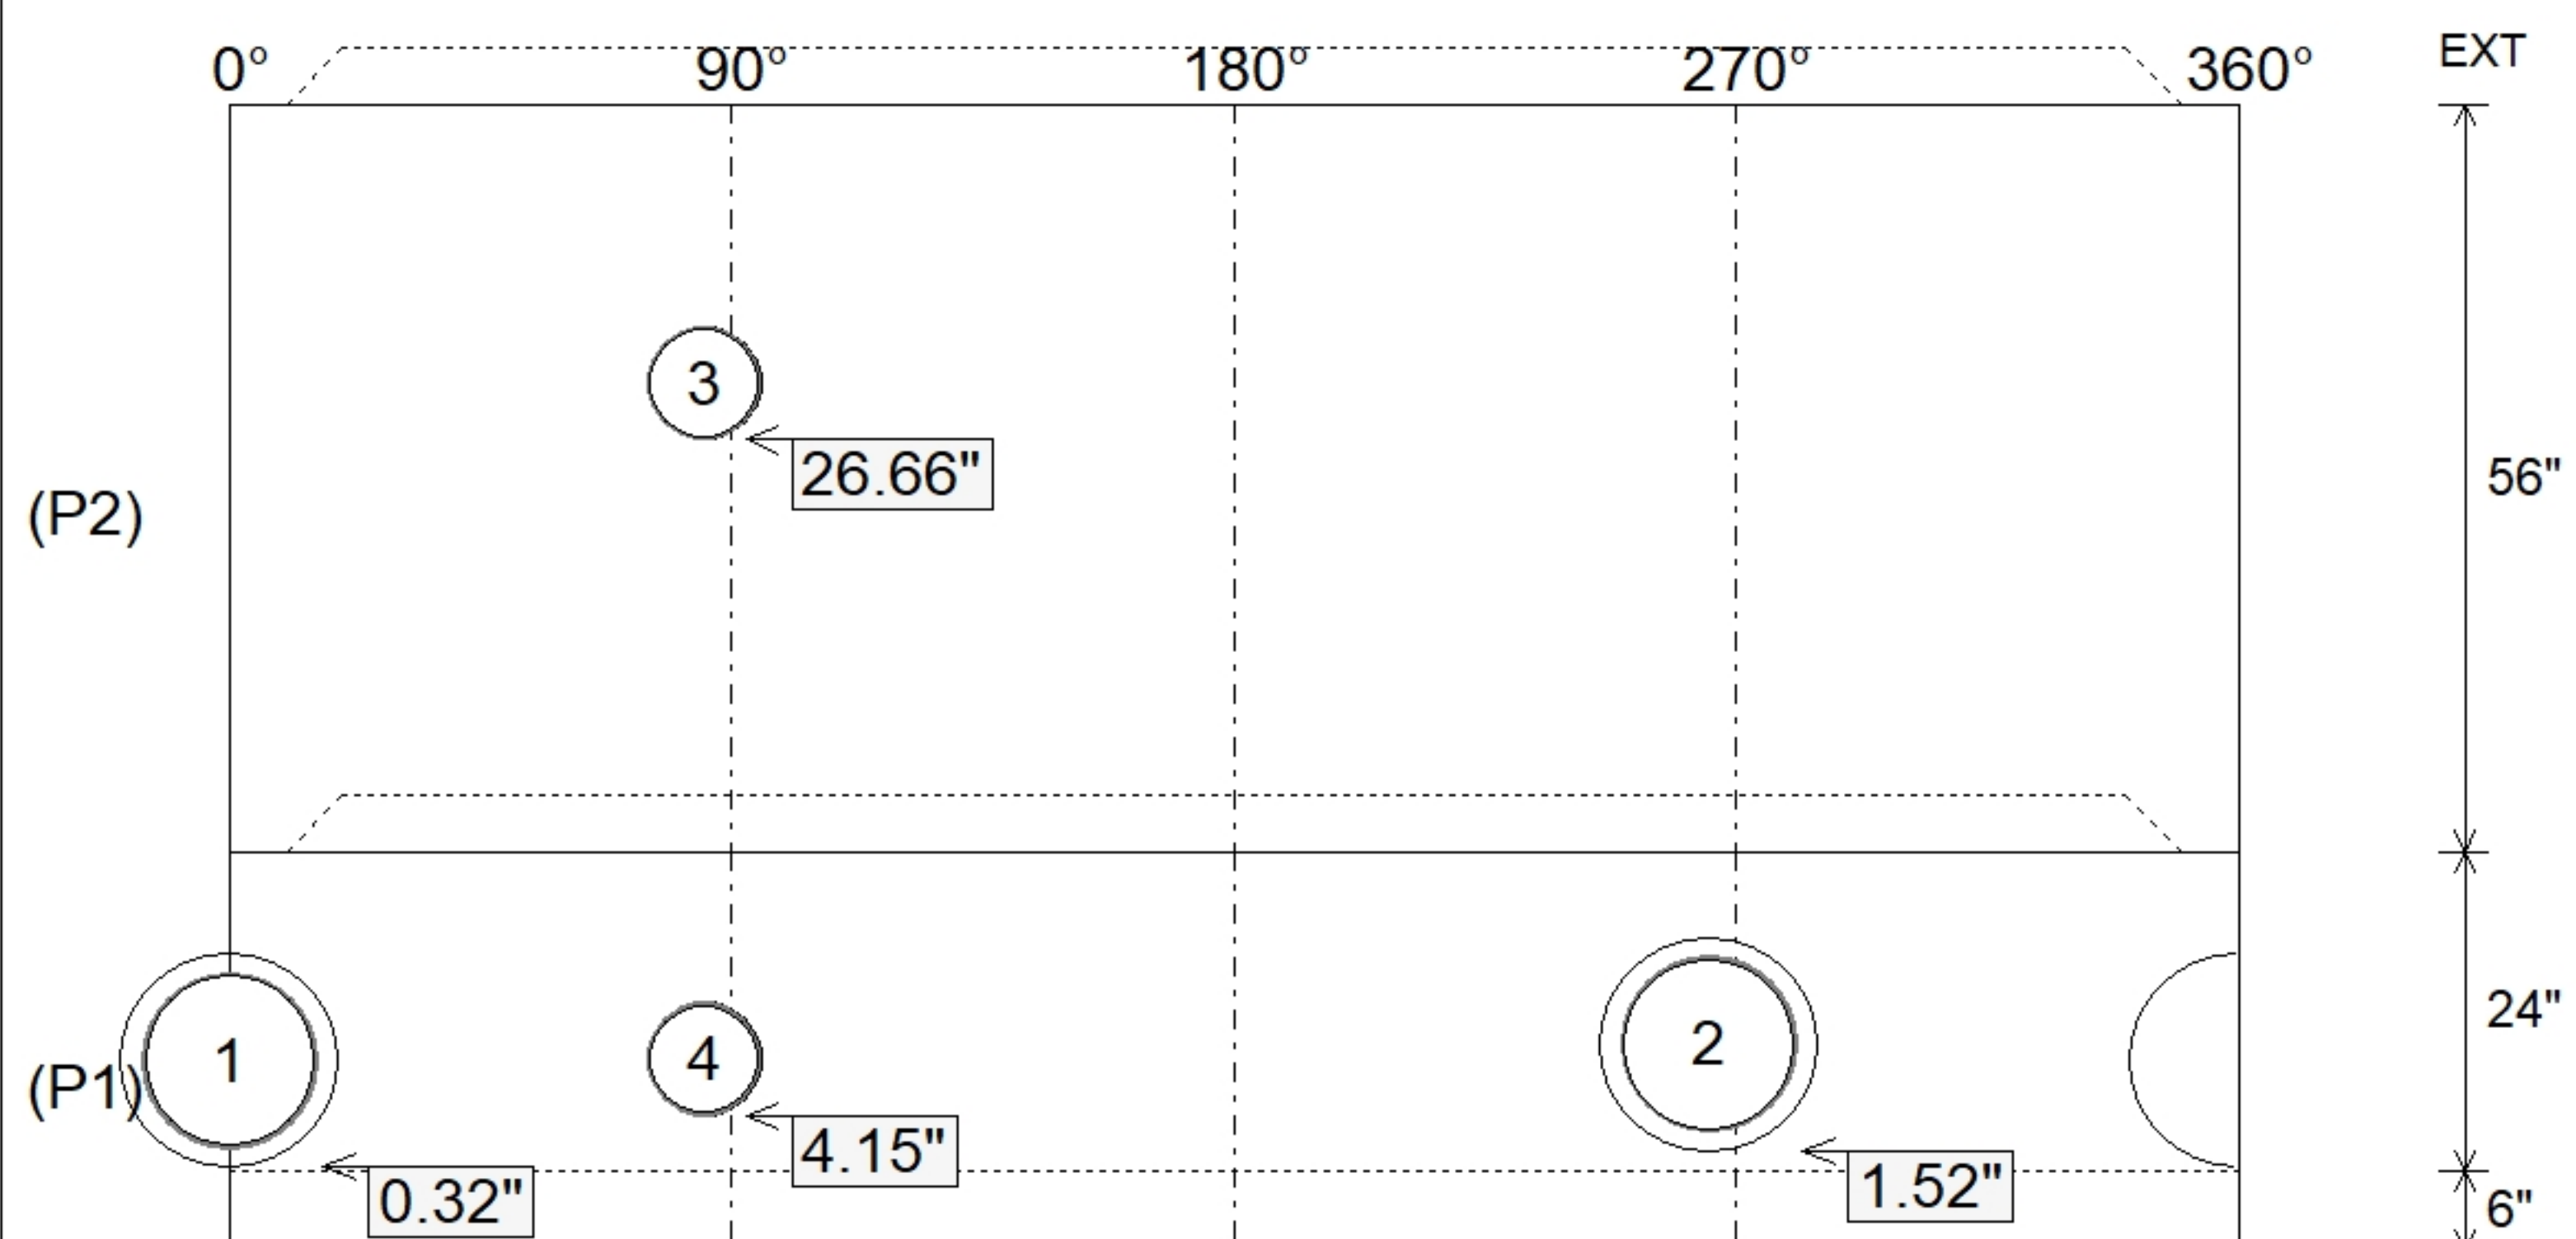

SUBMITTAL
APPROVED BY:
