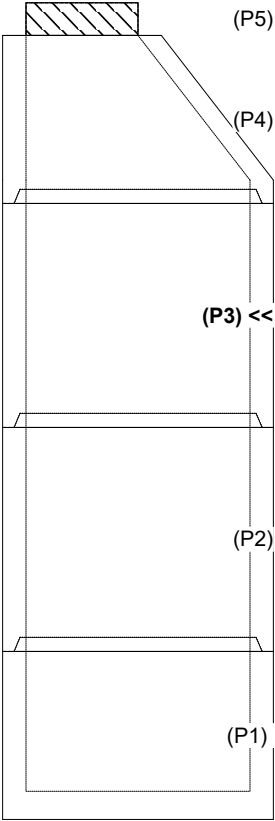

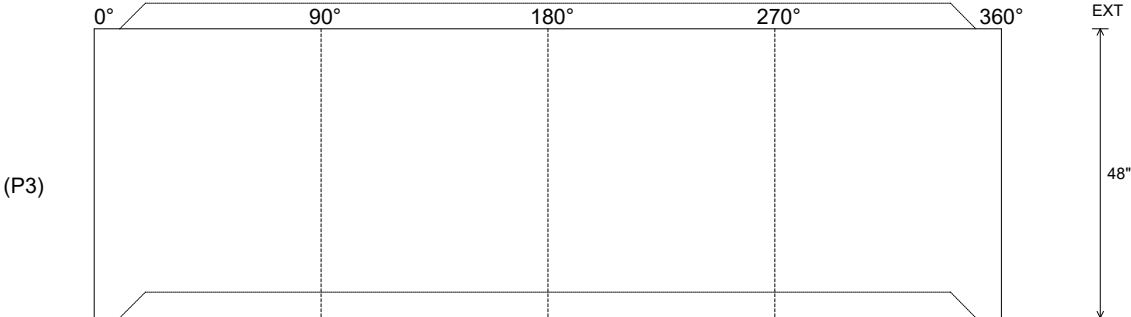


Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC					Plant: 100 6/2/2026 10:56:52 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: B1 (4)											
P3 MH048RS48S MH RISER T/G											
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE F/G - 36" P3) 48" - MH RISER T/G - 48" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE T/h - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 DD						0 lb 3000 lb 3353 lb 3353 lb 3330 lb 1440 lb 0 lb 0 lb 0 lb 16 lb ----- Structure Total: 14493 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. ALL PIPE CONNECTORS TO INCLUDE DOUBLE PIPE BANDS. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 558.5' Rim to Invert: 14.06' Slack: 1.72" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd		
