

Job Name: 26-1066 - Gunning Pump Station & Force Main
Job Location: Bardstown, KY
Contractor: Connhurst, LLC

Plant: 100

6/2/2026 10:56:16 AM

Tech: Jared - F
PC: E. Bradley



Structure ID: V V (16)

P2 MH096LD17S

MH FLAT TOP w/48"x48" Hatch F/G


P3) 48" x 48" - CASTING HEIGHT - 0"
P2) 96" - MH FLAT TOP w/48"x48" Hatch F/G - 17"
P1) 96" - MH BASE EF Cust. Ht. 08"F (14"EF = 142"OD) T/n - 73"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 96" - Conseal CS-102 1.00" (Double)
1) 48" x 48" - Conseal CS-102 1.00" (Double)
3) Hole - 12
1) PSX - 8QRS DD

0 lb
8607 lb
28510 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
6 lb
Structure Total: 37124 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS.
4. HATCH SUPPLIED BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .31) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.(DOUBLE MAT)

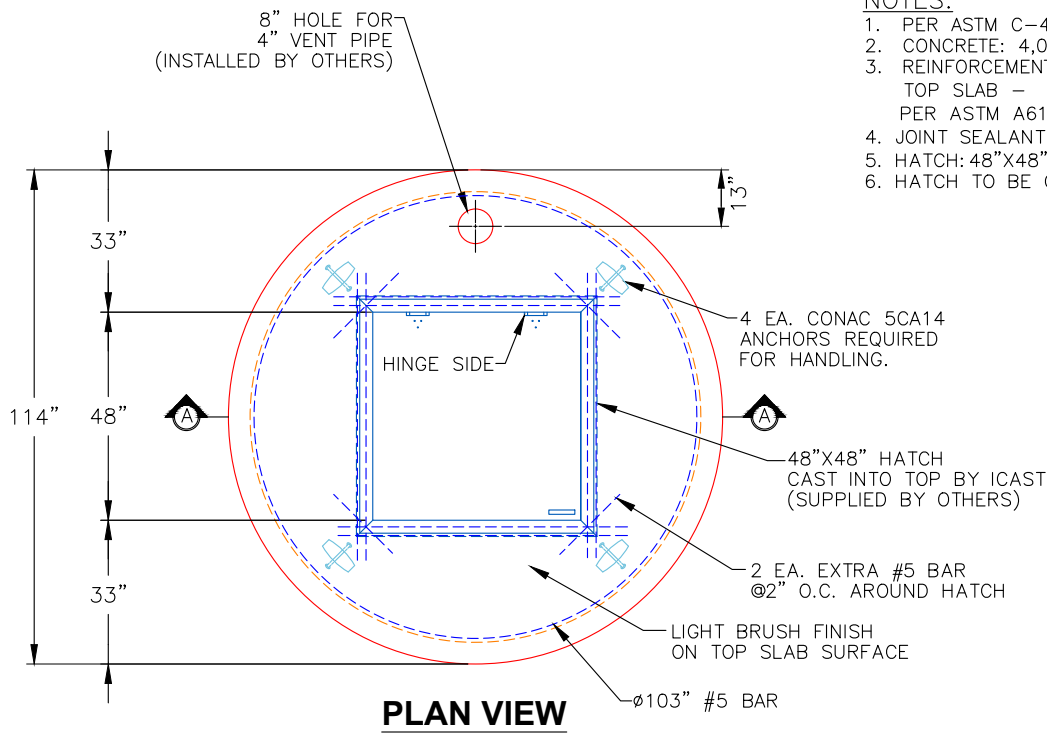

NOTES:

1. PER ASTM C-478 LATEST REVISION
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCEMENT:
TOP SLAB - #5 BAR @ 6" C.C.E.W.
PER ASTM A615 (GRADE 60)
4. JOINT SEALANT - 1" CS-102-DOUBLE
5. HATCH: 48"X48" HATCH SUPPLIED BY OTHERS.
6. HATCH TO BE CAST INTO TOP SLAB BY ICAST

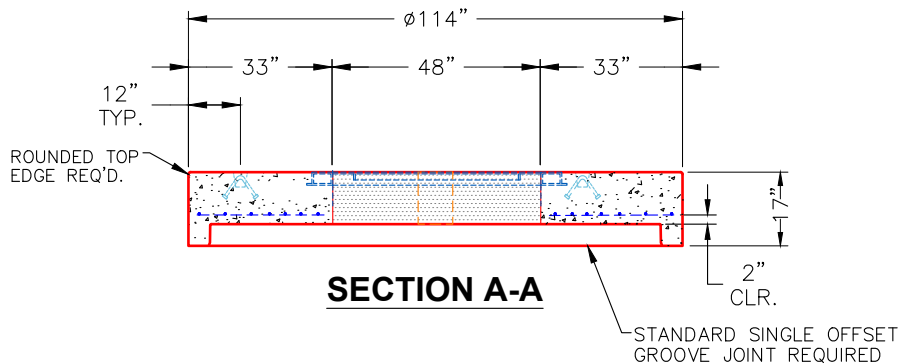

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 9"

Height (Ext): 17"

Weight (Net): 8607 lb
Volume (Net): 2.2cu.yd
