



Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC					Plant: 100 6/2/2026 10:54:42 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: W W (15)											
P1 MH096BAEVF			MH BASE EF Cust. Ht. 12"F (14"EF =142"OD) T/n								
P6) 36" x 72" - HATCH (CAST FLUSH) - 0" P5) 96" - MH FLAT TOP w/36"x72" Hatch F/G - 17" P4) 96" - MH RISER T/G - 36" P3) 96" - MH RISER T/G - 96" P2) 96" - MH RISER T/G - 84" P1) 96" - MH BASE EF Cust. Ht. 12"F (14"EF =142"OD) T/n - 79" 1) JOINT WRAP - 12" WD x 096" MAC WRAP 1) SPECIAL Internal Coating 4) 96" - Conseal CS-231 1.00" (Double) 1) 36" x 72" - Conseal CS-231 1.00" (Double) 2) Hole - 12 1) PSX - 8QRS DD 1) PSX - 16M DD 1) PSX - 12M DD					100 lb 8315 lb 8968 lb 23694 lb 20688 lb 35627 lb 0 lb 0 lb 0 lb 0 lb 0 lb 6 lb 8 lb 8 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. HATCH SUPPLIED BY OTHERS. 5. INSIDE OF STRUCTURE TO BE SANDBLASTED, THEN A COATING OF TNEMEC 218 TO BE APPLIED, FOLLOWED BY A COATING OF TNEMEC 434, FOLLOWED BY A COATING OF TNEMEC 435. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .31) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W. (DOUBLE MAT)				
Rim: 559'		Rim to Invert: 17.3'		Slack: 0"		Sump: 104.4"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

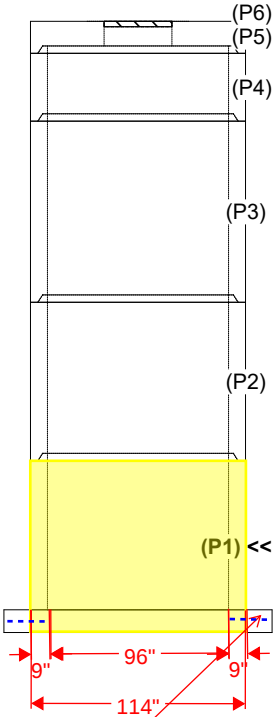


#5 BAR DOWELS @ 18" O.C TO BE DRILLED IN BASE SLAB FOR FLANGE ATTACHMENT

RIGHT-SIDE UP VIEW (int. dimensions)




1ST POUR (BASE) = 29,958 LBS
2ND POUR (EXTENDED FLANGE) = 5,669 LBS

UPSIDE-DOWN VIEW (int. dimenions)




INSIDE WALL DIMENSIONS

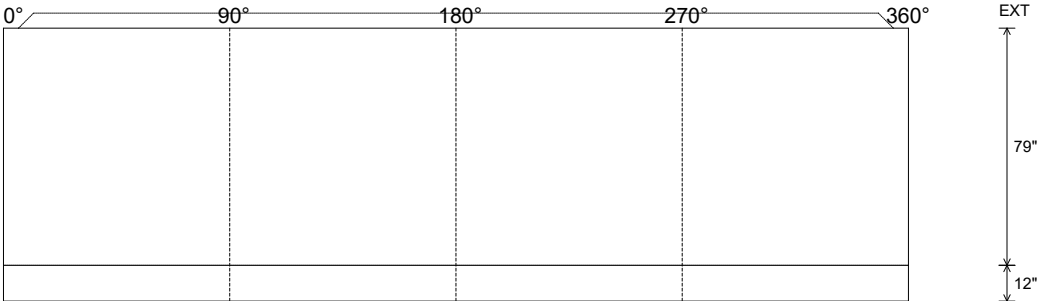

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 9" Floor Height: 12"	Height (Int): 79" Height (Ext): 91"	Weight (Net): 35627 lb Volume (Net): 9.1cu.yd
----------------------------------	---------------------------------	---	--	--


Job Name: 26-1066 - Gunning Pump Station & Force Main Job Location: Bardstown, KY Contractor: Connhurst, LLC					Plant: 100 6/2/2026 10:54:42 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: W W (15)											
P1 MH096BAEVF			MH BASE EF Cust. Ht. 12"F (14"EF =142"OD) T/n								
P6) 36" x 72" - HATCH (CAST FLUSH) - 0" P5) 96" - MH FLAT TOP w/36"x72" Hatch F/G - 17" P4) 96" - MH RISER T/G - 36" P3) 96" - MH RISER T/G - 96" P2) 96" - MH RISER T/G - 84" P1) 96" - MH BASE EF Cust. Ht. 12"F (14"EF =142"OD) T/n - 79" 1) JOINT WRAP - 12" WD x 096" MAC WRAP 1) SPECIAL Internal Coating 4) 96" - Conseal CS-231 1.00" (Double) 1) 36" x 72" - Conseal CS-231 1.00" (Double) 2) Hole - 12 1) PSX - 8QRS DD 1) PSX - 16M DD 1) PSX - 12M DD					100 lb 8315 lb 8968 lb 23694 lb 20688 lb 35627 lb 0 lb 0 lb 0 lb 0 lb 0 lb 6 lb 8 lb 8 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. HATCH SUPPLIED BY OTHERS. 5. INSIDE OF STRUCTURE TO BE SANDBLASTED, THEN A COATING OF TNEMEC 218 TO BE APPLIED, FOLLOWED BY A COATING OF TNEMEC 434, FOLLOWED BY A COATING OF TNEMEC 435. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .31) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W. (DOUBLE MAT)				
Rim: 559'		Rim to Invert: 17.3'		Slack: 0"		Sump: 104.4"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)




1ST POUR (BASE) = 29,958 LBS
2ND POUR (EXTENDED FLANGE) = 5,669 LBS

UPSIDE-DOWN VIEW (int. dimensions)

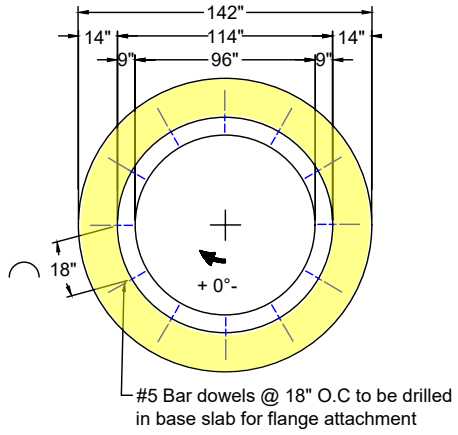


#5 Bar dowels @ 18" O.C to be drilled in base slab for flange attachment

INSIDE WALL DIMENSIONS

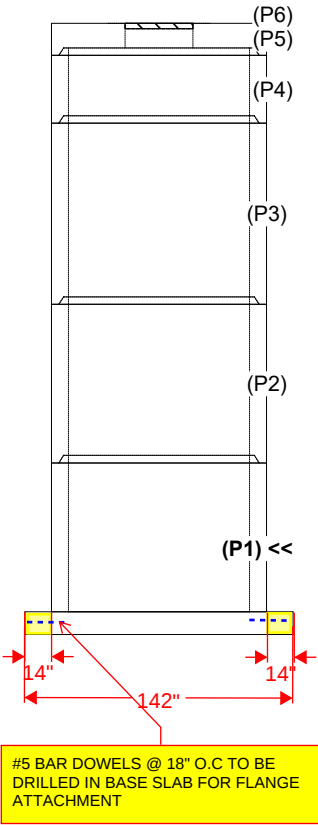

#5 BAR DOWELS @ 18" O.C TO BE DRILLED IN BASE SLAB FOR FLANGE ATTACHMENT

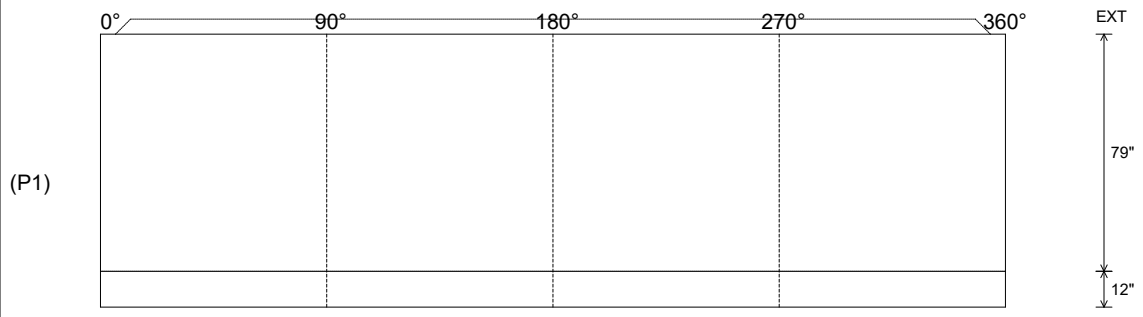

EXT 79"
12"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 9" Floor Height: 12"	Height (Int): 79" Height (Ext): 91"	Weight (Net): 35627 lb Volume (Net): 9.1cu.yd
----------------------------------	---------------------------------	---	--	--
