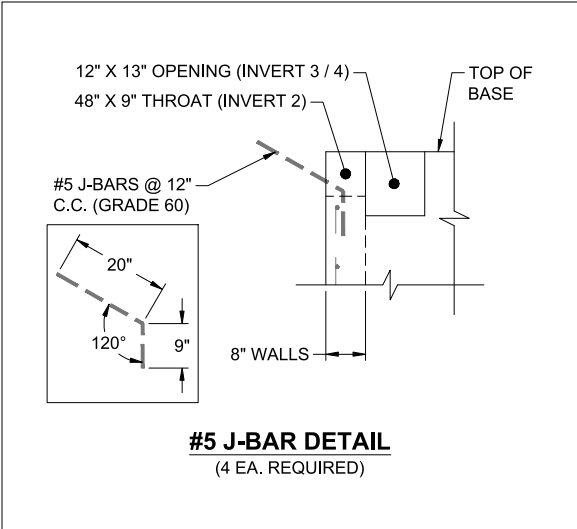
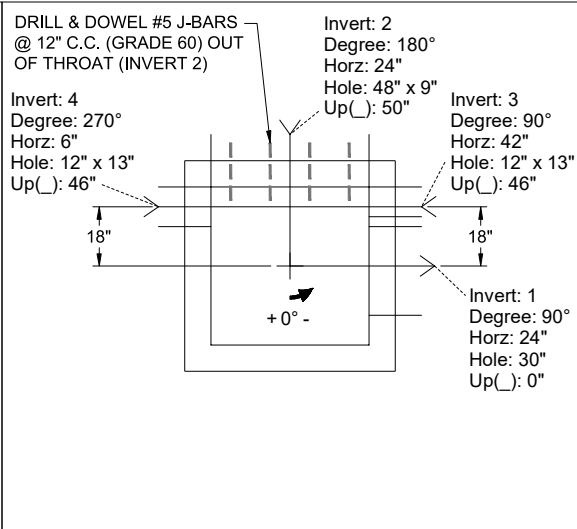
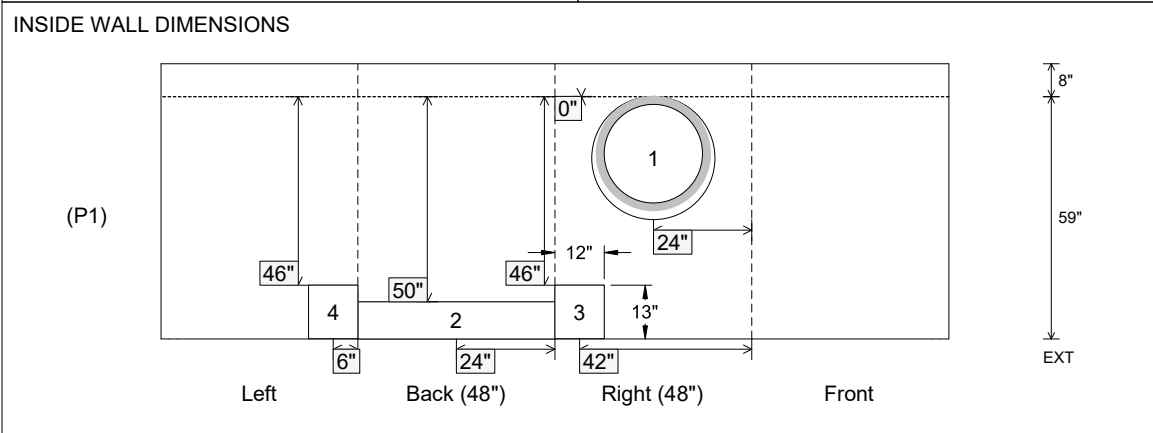
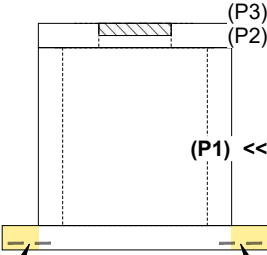
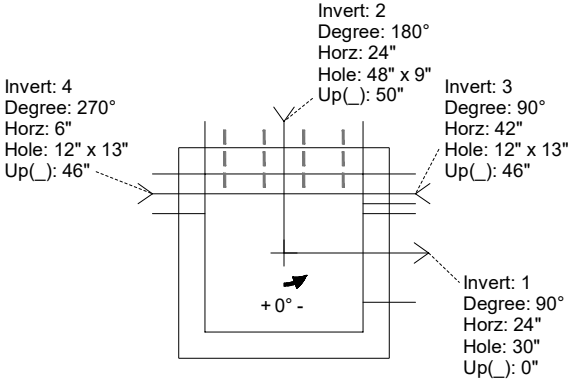
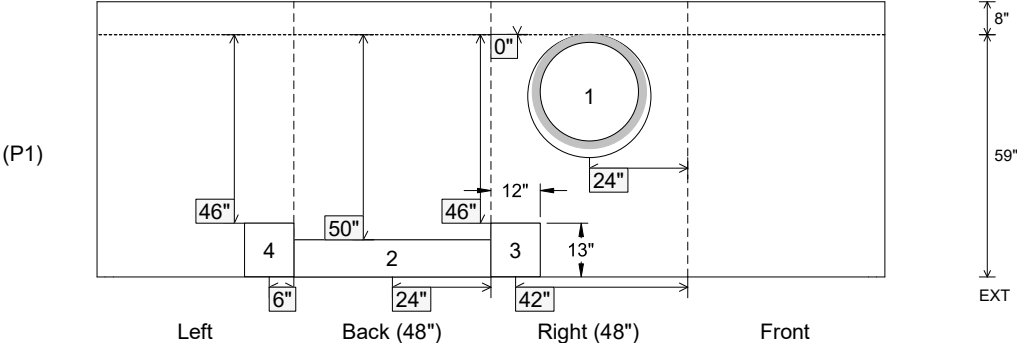


Job Name: 26-1075 - Walmart Fuel Station 00674-1008 Job Location: Gallatin, TN Contractor: Stewart Richey				Plant: 100 6/11/2026 2:22:05 PM		Tech: PC: T. Lewis					
Structure ID: CI 1 (3)											
P1 BX4848-08BAVF-EB				BX BASE w/FLANGE 08W/08F/12EF F/n							
P3) 24" - CASTING (cast in) - 4" P2) 48" x 48" - CB FLAT TOP 8"W SPEC. (JBS 1072) F/F - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/08F/12EF F/n - 59" 1) SECONDARY POUR - Extended Flange 1) This Structure Includes a Cast-in Item - MCS-288 Frame (Supplied by iCast) 1) CASTING - MCS-288 F/C STORM 1) 48" x 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 30 1) Horiz Slot n/n - 48"x9" 2) Vert. Slot n/n - 12"x13"				0 lb 2507 lb 13378 lb 0 lb 0 lb 250 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 16135 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. MCS-288 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO FLAT LID FLANGE SIDE UP 7. INVERTS 3 & 4 OFFSET 18" FROM CENTER OF WALL 8. DRILL & DOWEL #5 J-BARS @ 12" C.C. (GRADE 60) OUT OF 48" X 9" THROAT (INVERT 2) FOR CURB POUR TIE-IN (SEE J-BAR DETAIL) 9. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED IN 0° & 180° WALLS, 18" FROM TOP OF WALLS					
FIRST POUR (BASE): 10,929 LBS											
SECOND POUR (12" EXT. FLANGE): 2,449 LBS											
Rim: 519.52' Rim to Invert: 5.43' Slack: 0.05" Sump: 1.9" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	514.09'	90°	32"	24" HDPE	27.8"	Hole 30	30"	30"	0"	0"	
Invert 2	518.1'	180°	32"	48" x 9" Horiz Slot	48" x 9"	Horiz Slot 48"x9"	48" x 9"	48"	50"	0"	
Invert 3	517.765'	90°	50"	12" x 13" Vert. Slot	12" x 13"	Vert. Slot 12"x13"	12" x 13"	12"	46"	18"	
Invert 4	517.765'	270°	14"	12" x 13" Vert. Slot	12" x 13"	Vert. Slot 12"x13"	12" x 13"	12"	46"	-18"	
Invert 5											
UPSIDE-DOWN VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 59" Height (Ext): 67"		Weight (Net): 13378 lb Volume (Net): 3.42cu.yd	

Job Name: 26-1075 - Walmart Fuel Station 00674-1008 Job Location: Gallatin, TN Contractor: Stewart Richey				Plant: 100 6/11/2026 2:22:05 PM		Tech: PC: T. Lewis					
Structure ID: CI 1 (3)											
P1 BX4848-08BAVF-EB				BX BASE w/FLANGE 08W/08F/12EF F/n							
P3) 24" - CASTING (cast in) - 4" P2) 48" x 48" - CB FLAT TOP 8"W SPEC. (JBS 1072) F/F - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/08F/12EF F/n - 59" 1) SECONDARY POUR - Extended Flange 1) This Structure Includes a Cast-in Item - MCS-288 Frame (Supplied by iCast) 1) CASTING - MCS-288 F/C STORM 1) 48" x 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 30 1) Horiz Slot n/n - 48"x9" 2) Vert. Slot n/n - 12"x13"				0 lb 2507 lb 13378 lb 0 lb 0 lb 250 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 16135 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: DRILL & DOWEL #5 BAR @ 12" C.C. E.W. (GRADE 60) OUT OF BASE FLOOR FOR EXT. FLANGE POUR TIE-IN - 4" MIN. PENETRATION INTO BASE FLOOR & 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. MCS-288 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO FLAT LID FLANGE SIDE UP					
FIRST POUR (BASE): 10,929 LBS				SECOND POUR (12" EXT. FLANGE): 2,449 LBS							
Rim: 519.52'				Rim to Invert: 5.43'		Slack: 0.05"		Sump: 1.9"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	514.09'	90°	32"	24" HDPE	27.8"	Hole 30	30"	30"	0"	0"	
Invert 2	518.1'	180°	32"	48" x 9" Horiz Slot	48" x 9"	Horiz Slot 48"x9"	48" x 9"	48"	50"	0"	
Invert 3	517.765'	90°	50"	12" x 13" Vert. Slot	12" x 13"	Vert. Slot 12"x13"	12" x 13"	12"	46"	18"	
Invert 4	517.765'	270°	14"	12" x 13" Vert. Slot	12" x 13"	Vert. Slot 12"x13"	12" x 13"	12"	46"	-18"	
Invert 5											
UPSIDE-DOWN VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 59" Height (Ext): 67"		Weight (Net): 13378 lb Volume (Net): 3.42cu.yd	
