



Job Name: 26-1162 - Youngstown Sewer Replacement Job Location: Jeffersonville, IN 47130 Contractor: SLB Pipe Solutions	Plant: 100	Tech: J. Horsley - F
	3/12/2026 4:21:09 PM	PC: T. Lewis

Structure ID: S2 (3)

P3 MH048CN36-S

ECC CONE w/ 24" HOLE F/G

P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 21" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO	0 lb 3000 lb 2515 lb 2701 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 16 lb ----- Structure Total: 9943 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C SANITARY) 4. NO STEPS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
---	--	---

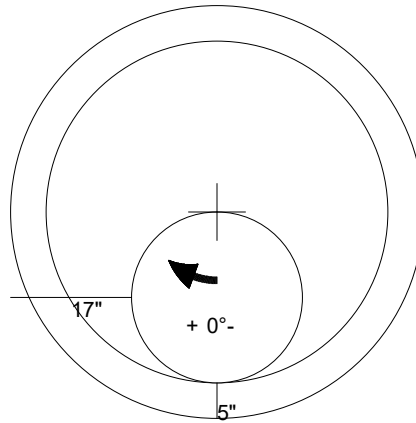

48" - ECC CONE w/ 24" HOLE F/G - 36" - (P3)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	---
