

Structure ID: 25-CS-12

P2 MH144RS60

MH RISER T/G

| | |
|---|---|
| P5) 24" - CASTING HEIGHT - 4" P4) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18" P3) 144" - MH RISER T/G - 96" P2) 144" - MH RISER T/G - 60" P1) 144" - MH MONOBASE 14F, Custom Ht T/n - 24" 1) CVSTENCILING 1) ASSEMBLY REQUIRED - INSTALL BRACKETS 3) 144" - Conseal CS-102 1.00" 2) Hole - 44 1) Hole - 16 | 0 lb 23623 lb 48069 lb 32283 lb 39578 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 143553 lb |
|---|---|

Structure Notes:
 4" CASTING BY OTHERS



ICAST TO INSTALL THE INTERNAL BRACKETS, INTERNAL COMPONENTS TO BE INSTALLED ON SITE BY CONTECH FIELD CONSULTANT

CONTECH'S LOGO AS WELL AS THE INLETS AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE


Rim: 482.63' Rim to Invert: 8.01' Slack: 2.12" Sump: 108" Step Position:

| Position | Elev | Angle | Ext. (cw) | Pipe | Pipe OD | Connector | Hole | Horz Size | Up (L) | Offset |
|----------|------|-------|-----------|------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | | | | | | | | | | |
| Invert 2 | | | | | | | | | | |
| Invert 3 | | | | | | | | | | |
| Invert 4 | | | | | | | | | | |
| Invert 5 | | | | | | | | | | |
| Invert 6 | | | | | | | | | | |
| Invert 7 | | | | | | | | | | |
| Invert 8 | | | | | | | | | | |

RIGHT-SIDE UP VIEW (int. dimensions)

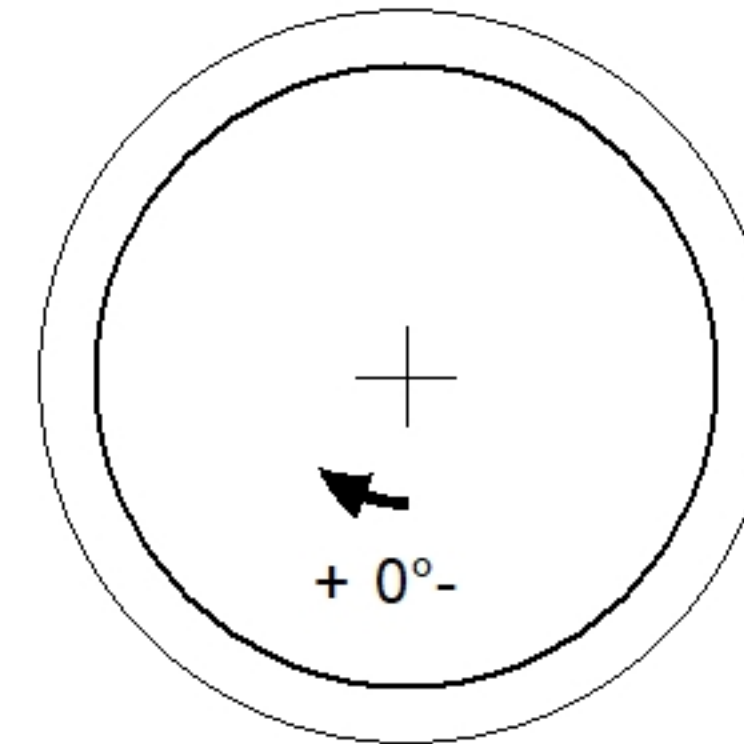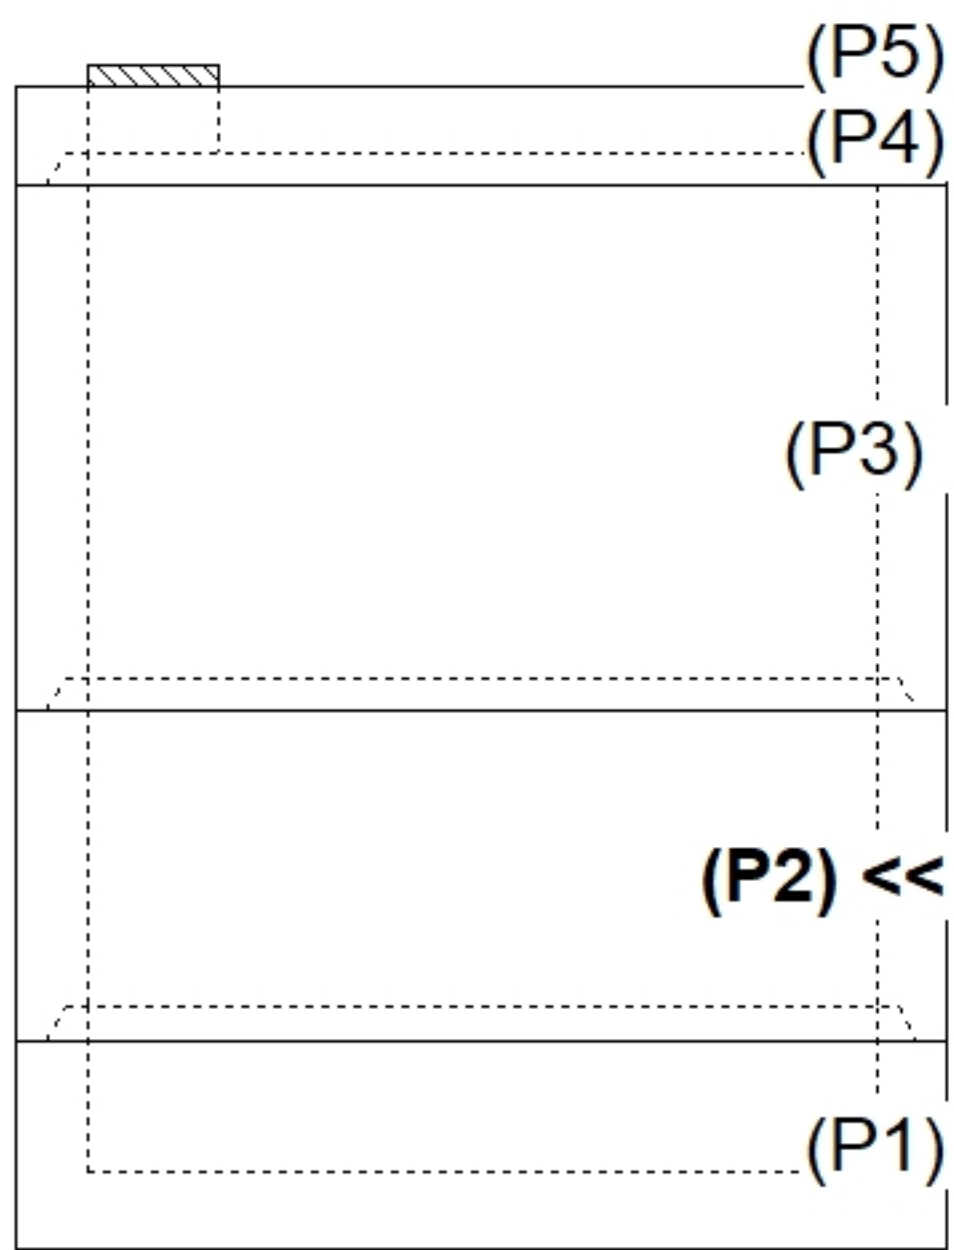

INSIDE WALL DIMENSIONS

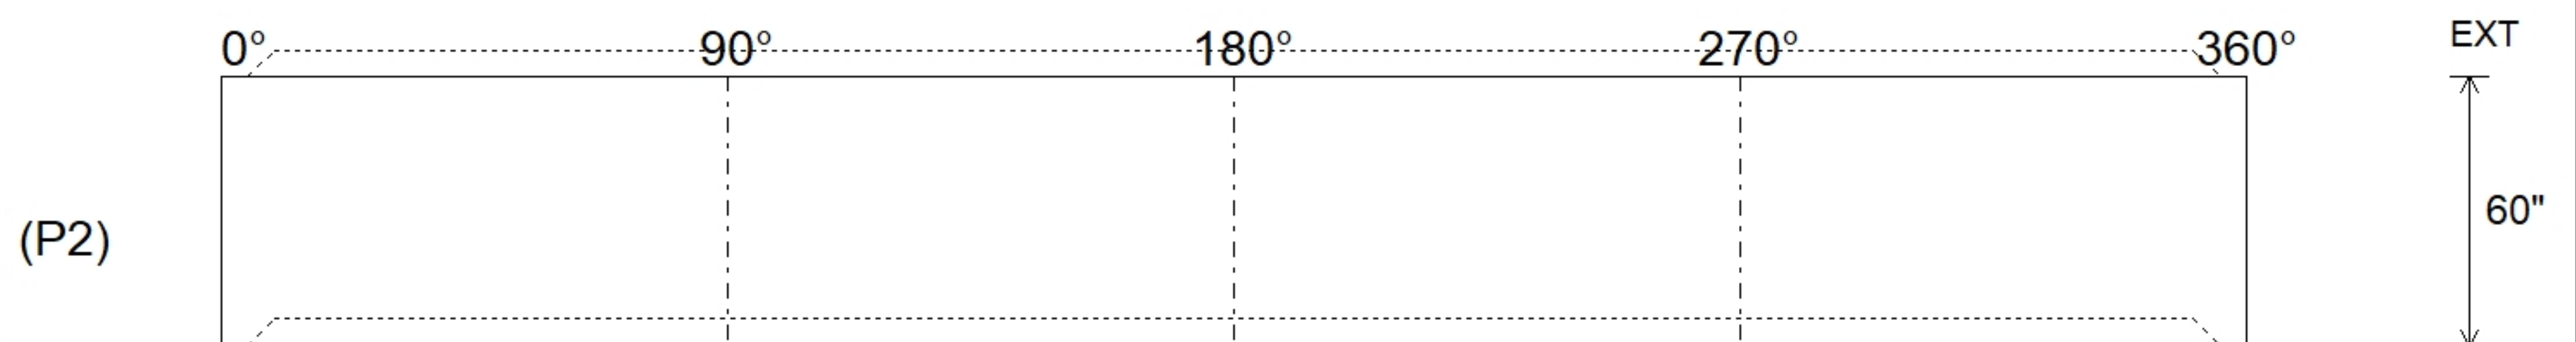

| | | | | |
|----------------------------------|------------------------------------|---|--|---|
| Coating (Int): Coating (Ext): | Seam Up: Tongue Seam Dn: Groove | Wall Thickness: 13" Floor Height: 0" | Height (Int): 60" Height (Ext): 60" | Weight (Net): 32283 lb Volume (Net): 8.25cu.yd |
|----------------------------------|------------------------------------|---|--|---|
