

Job Name: 26-1216 Hayden Rd. Sanitary
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam

Tech: S. Felletter

7/7/2026 2:10:26 PM

PC: A. Chambers



Structure ID: B2 SS-MH

P1 MH048BA18CDARED

MH BASE w/ConBlock-CDA Red T/n

P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 24"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 48"

P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 18"

- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
- 1) CASTING - HOE MC-315 F/C Sanitary
- 2) 48" - Con Seal CS-102 1.00" (Double)
- 1) 24" - Con Seal CS-102 1.00" (Double)
- 1) PSX - 12-08 NYLO
- 7) MH Step ML-10-TDS-NCR - 10"

0 lb
1738 lb
3353 lb
2540 lb
0 lb
0 lb
1440 lb
258 lb
0 lb
0 lb
8 lb
0 lb

Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY").
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.




Structure Total: 9337 lb

Rim: 439.58' Rim to Invert: 8.08' Slack: 1.96" Sump: 2" Step Position: 180°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	431.5'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

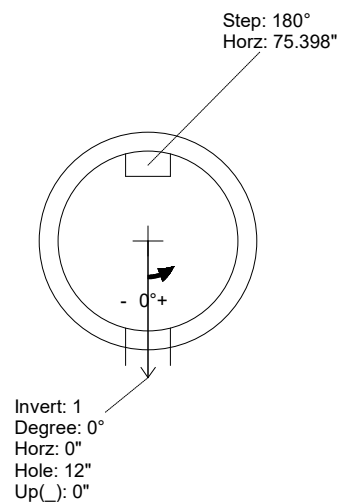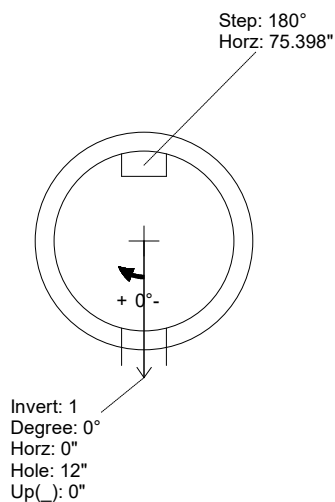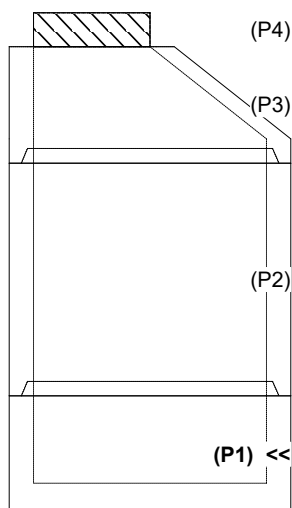

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 18"
Height (Ext): 24"

Weight (Net): 2540 lb
Volume (Net): 0.65cu.yd

Job Name: 26-1216 Hayden Rd. Sanitary
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam

7/7/2026 2:10:26 PM

Tech: S. Felletter

PC: A. Chambers



Structure ID: B2 SS-MH

P1 MH048BA18CDARED

MH BASE w/ConBlock-CDA Red T/n

- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 24"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 48"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 18"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) CASTING - HOE MC-315 F/C Sanitary
2) 48" - Con Seal CS-102 1.00" (Double)
1) 24" - Con Seal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
7) MH Step ML-10-TDS-NCR - 10"

- 0 lb
1738 lb
3353 lb
2540 lb
0 lb
0 lb
1440 lb
258 lb
0 lb
0 lb
8 lb
0 lb
- Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY").
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 9337 lb



**Invert channel drawing
Full height invert**

Rim: 439.58' Rim to Invert: 8.08' Slack: 1.96" Sump: 2" Step Position: 180°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	431.5'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

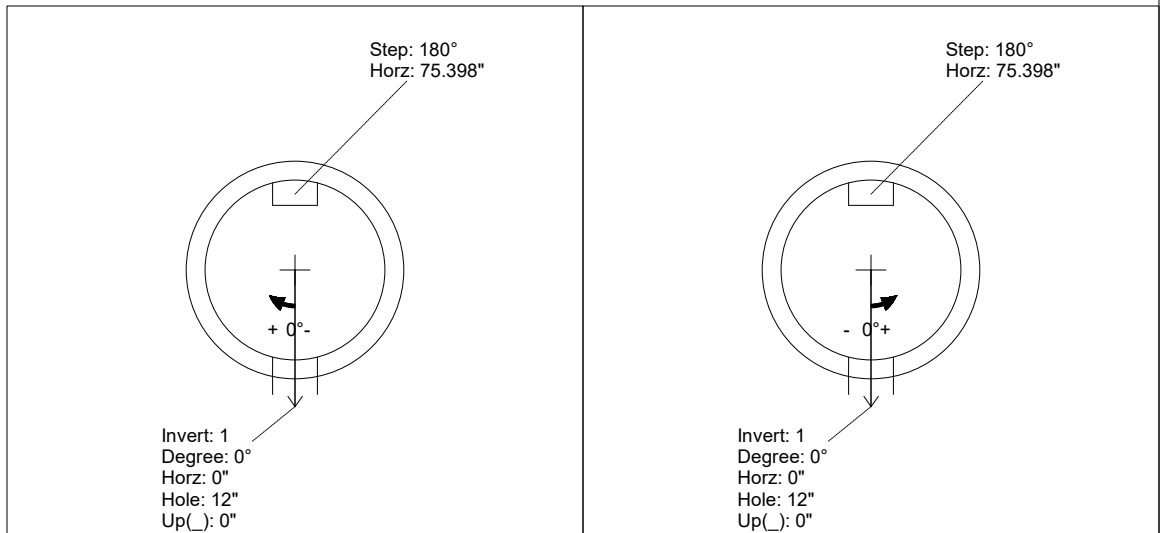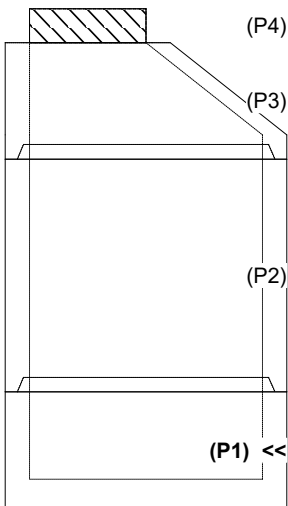

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 18"
Height (Ext): 24"

Weight (Net): 2540 lb
Volume (Net): 0.65cu.yd
