

Contractor: Hayes Pipe Supply

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 6.91'

Floor Height: 6"

Slack: 1.92"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING SUPPLIED BY OTHERS.

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P4) 24" - CASTING HEIGHT - 7"

P3) 24" - GRADE RING w/ConBlock-CDA Red - 4"

P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36"

P1) 48" - MH BASE w/ConBlock-CDA Red - 36"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1) 48" - Conseal CS-102 1.00" (Double)

2) PSX - 12-08 NYLO

6) MH Step ML-10-TDS-NCR - 10"

0 lb

270 lb

2251 lb

3749 lb

0 lb

0 lb


1440 lb

0 lb

16 lb


0 lb

Structure Total: 7726 lb

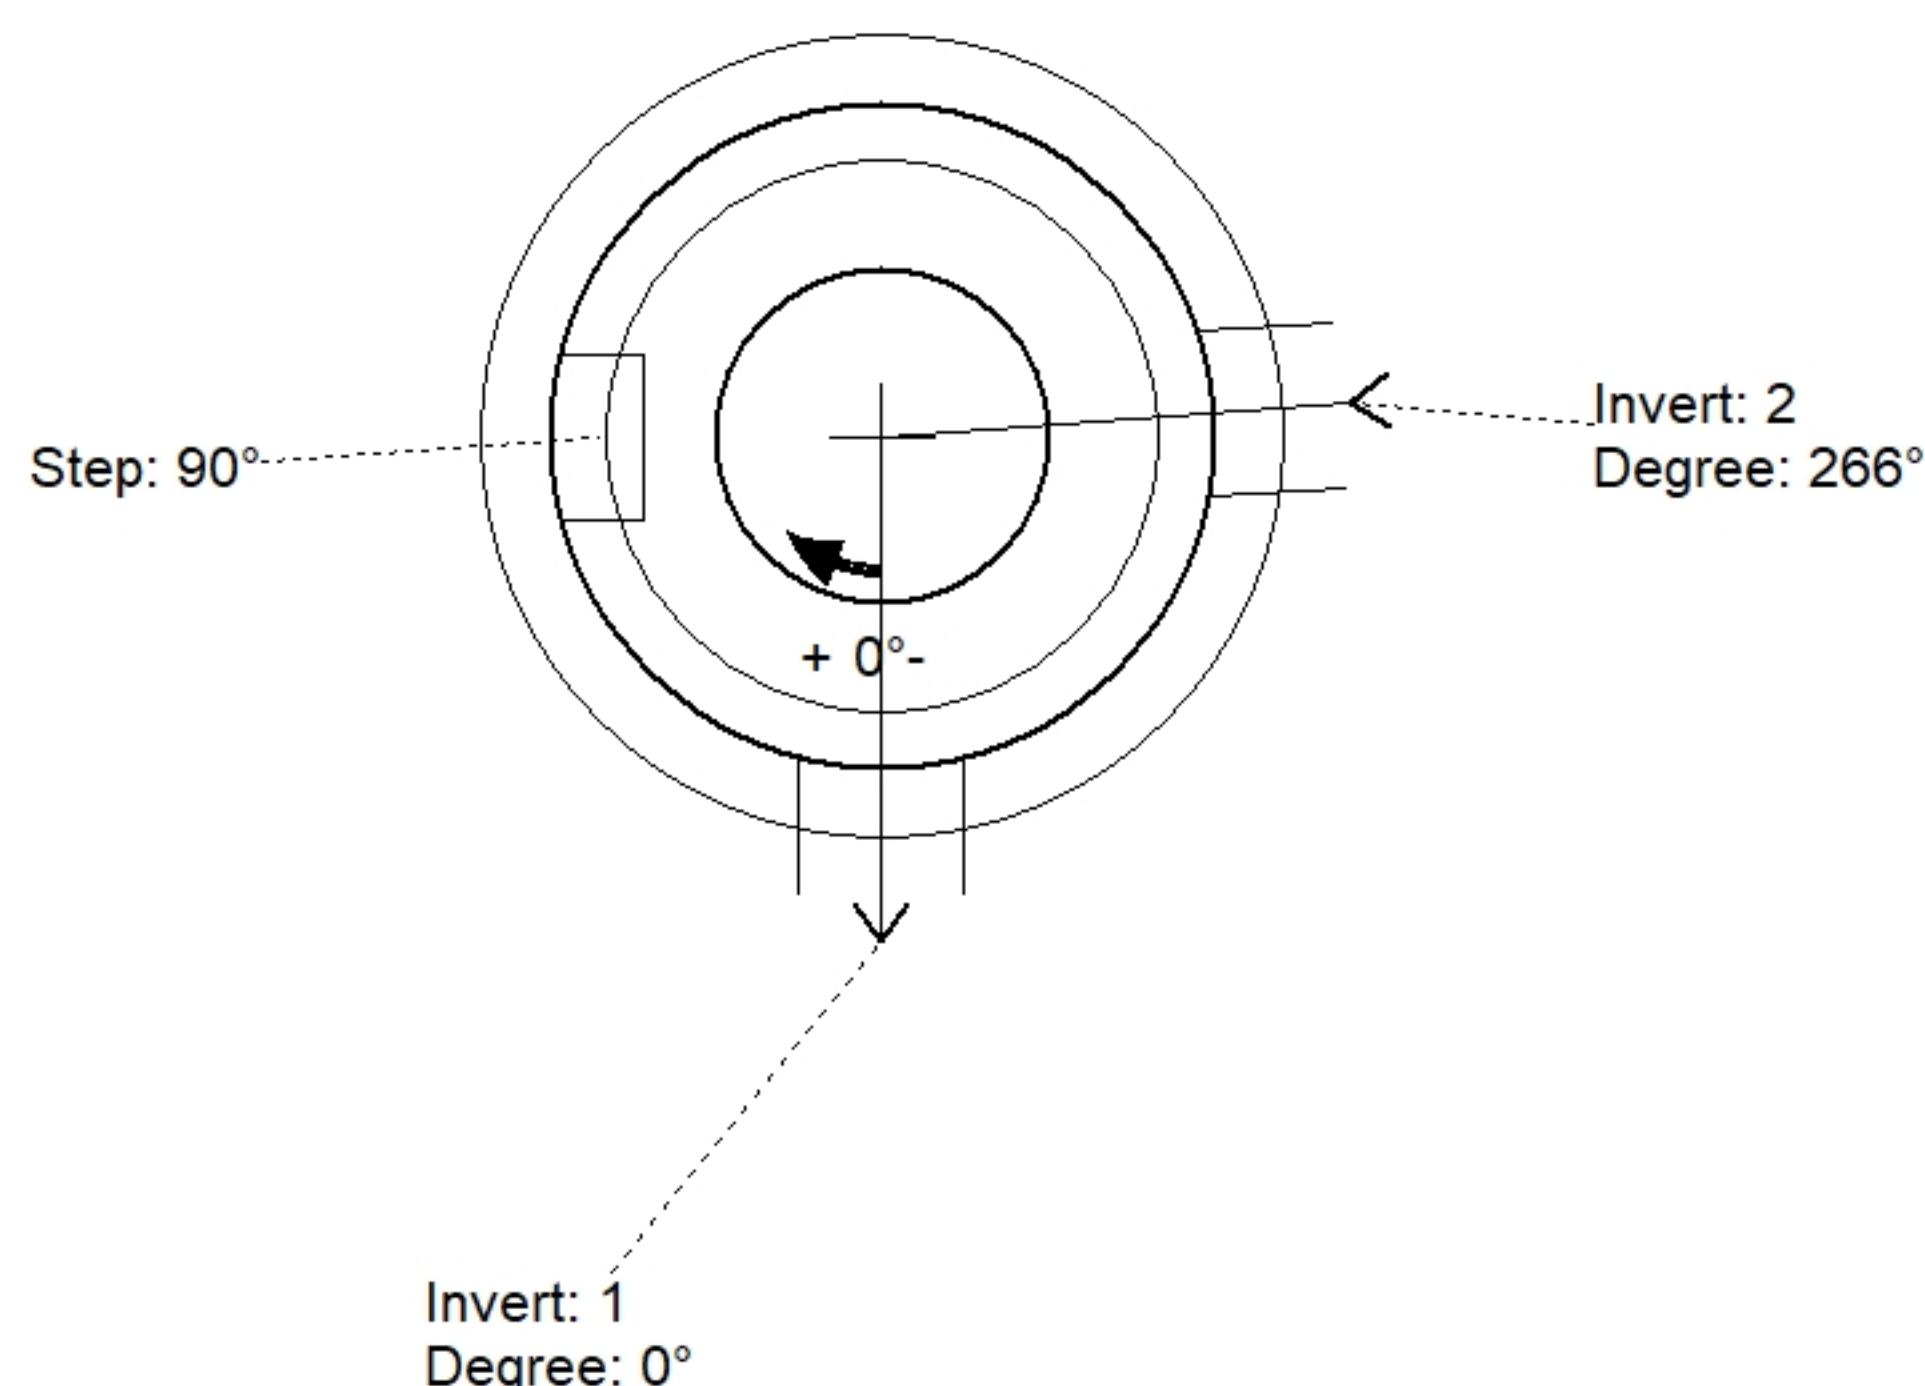

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	575.49'							
Reducer								
Invert 1	568.58'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	568.78'	266°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	2.4"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

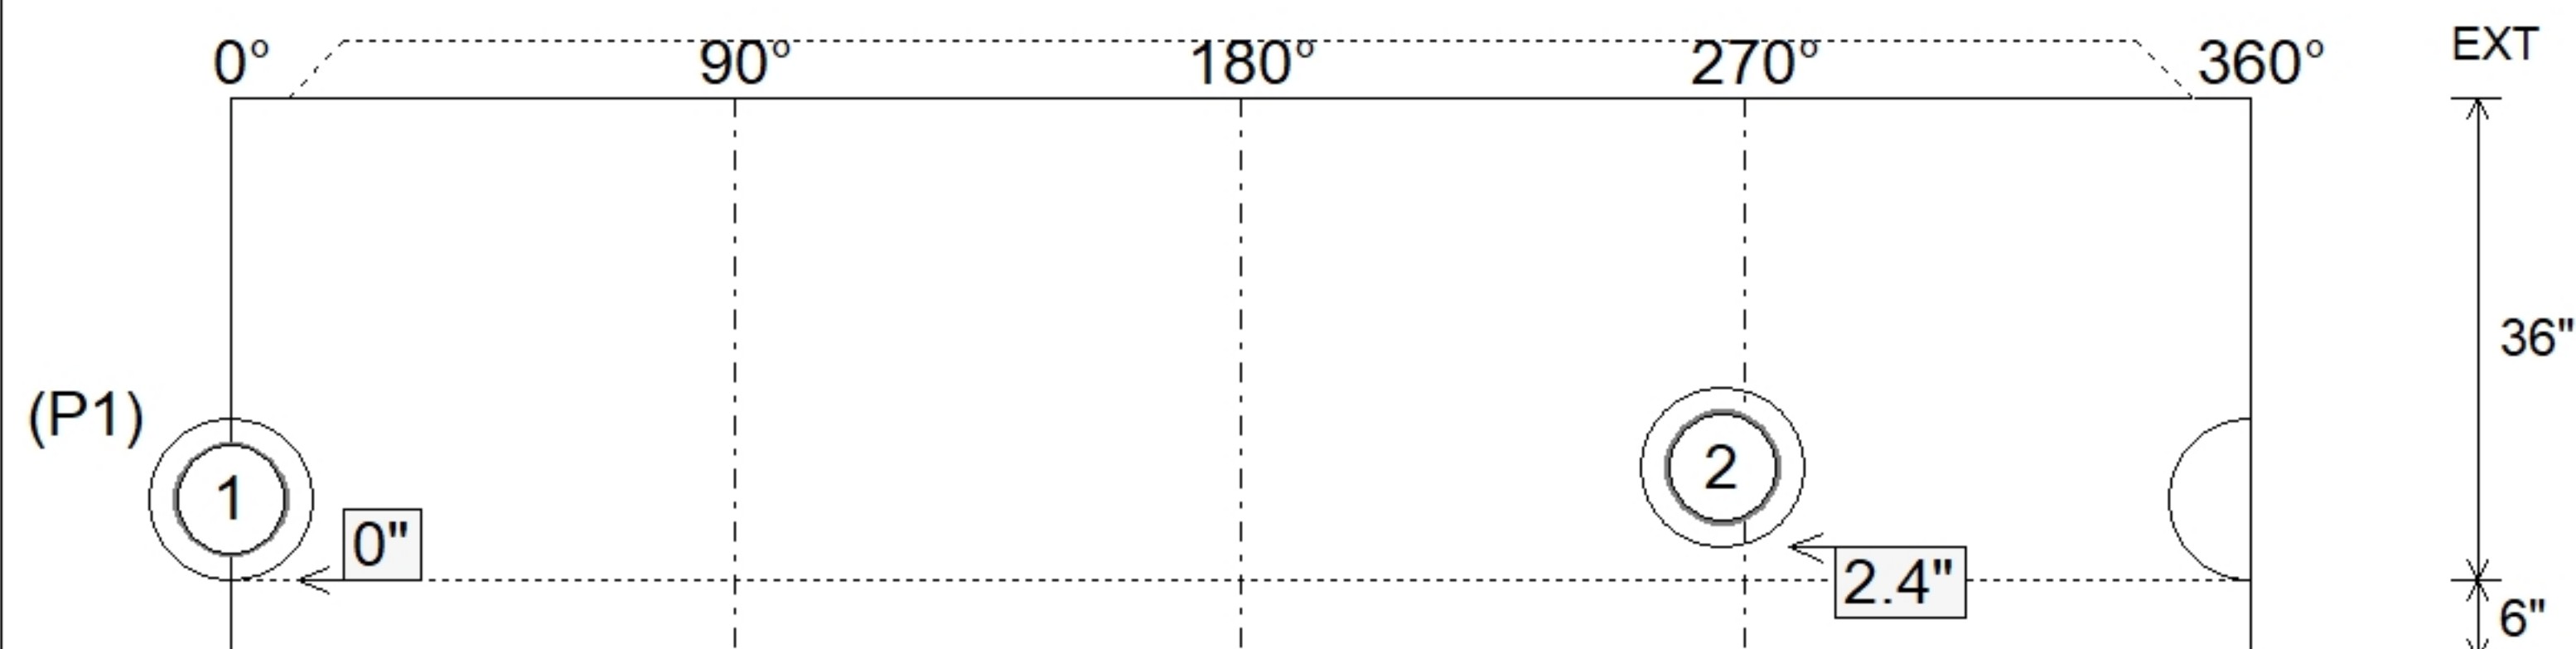

Submittal Drawing
5/11/2026 3:28:16 PM

SUBMITTAL
APPROVED BY:
