

Job Name: 26-1233 - StorPlace Tulip Mini Storage
Job Location: Gallatin, TN 37066
Contractor: Hayes Pipe Supply

Plant: Beaver Dam
9/17/2026 2:08:19 PM

Tech: J. Coppage
PC: E. Bradley



Structure ID: MH A1-12 SS-MH

P1 MH048BA24CDARED

MH BASE w/ConBlock-CDA Red

- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36"
P2) 48" - MH RISER w/ConBlock-CDA Red - 36"
P1) 48" - MH BASE w/ConBlock-CDA Red - 24"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
2) 48" - Con seal CS-102 1.00" (Double)
1) 24" - Con seal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
8) MH Step ML-10-TDS-NCR - 10"

- Structure Notes:
1. (7" TALL CASTING PROVIDED BY OTHERS)
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Structure Total: 8843 lb

Rim: 504.01' Rim to Invert: 8' Slack: 1" Sump: 2" Step Position: 135°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	496.01'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	496.21'	270°	136.659"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.4"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

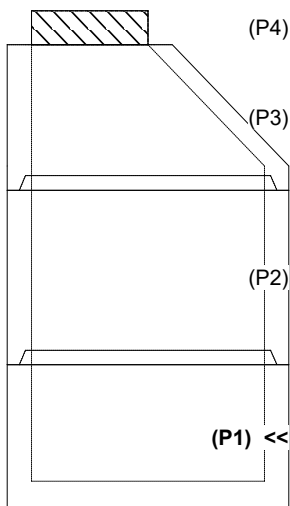


Step: 135°
Horz: 56.549"



Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"


Invert: 2
Degree: 270°
Horz: 113.097"
Hole: 12"
Up(): 2.4"

Step: 135°
Horz: 56.549"



Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 24"
Height (Ext): 30"

Weight (Net): 2911 lb
Volume (Net): 0.74cu.yd

Job Name: 26-1233 - StorPlace Tulip Mini Storage
Job Location: Gallatin, TN 37066
Contractor: Hayes Pipe Supply

Plant: Beaver Dam

9/17/2026 2:08:19 PM

Tech: J. Coppage

PC: E. Bradley



Structure ID: MH A1-12 SS-MH

P1 MH048BA24CDARED

MH BASE w/ConBlock-CDA Red

- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36"
P2) 48" - MH RISER w/ConBlock-CDA Red - 36"
P1) 48" - MH BASE w/ConBlock-CDA Red - 24"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
2) 48" - Con seal CS-102 1.00" (Double)
1) 24" - Con seal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
8) MH Step ML-10-TDS-NCR - 10"

Structure Total: 8843 lb

Structure Notes:

1. (7" TALL CASTING PROVIDED BY OTHERS)
 2. PER ASTM C478 SPECIFICATIONS.
 3. CONCRETE = 4,000 PSI AT 28 DAYS.
 4. ADMIXTURE = CONBLOCK CDA RED.
 5. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


**INVERT CHANNEL DRAWING
FULL HEIGHT INVERT**

Rim: 504.01' Rim to Invert: 8' Slack: 1" Sump: 2" Step Position: 135°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	496.01'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	496.21'	270°	136.659"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.4"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

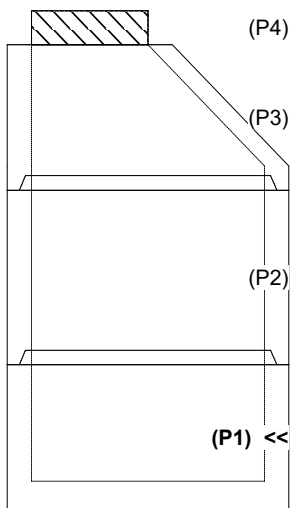


Step: 135°
Horz: 56.549"



Invert: 2
Degree: 270°
Horz: 113.097"
Hole: 12"
Up(): 2.4"


Invert: 2
Degree: 270°
Horz: 113.097"
Hole: 12"
Up(): 2.4"

Step: 135°
Horz: 56.549"



Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 24"
Height (Ext): 30"

Weight (Net): 2911 lb
Volume (Net): 0.74cu.yd
