

Contractor: Hayes Pipe Supply

TECH: J. Coppage

Plant: Beaver Dam



Size: 48"

Rim to Invert: 8'

Floor Height: 6"


Slack: 1"

1. (7" TALL CASTING PROVIDED BY OTHERS)
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


8) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 8843 lb

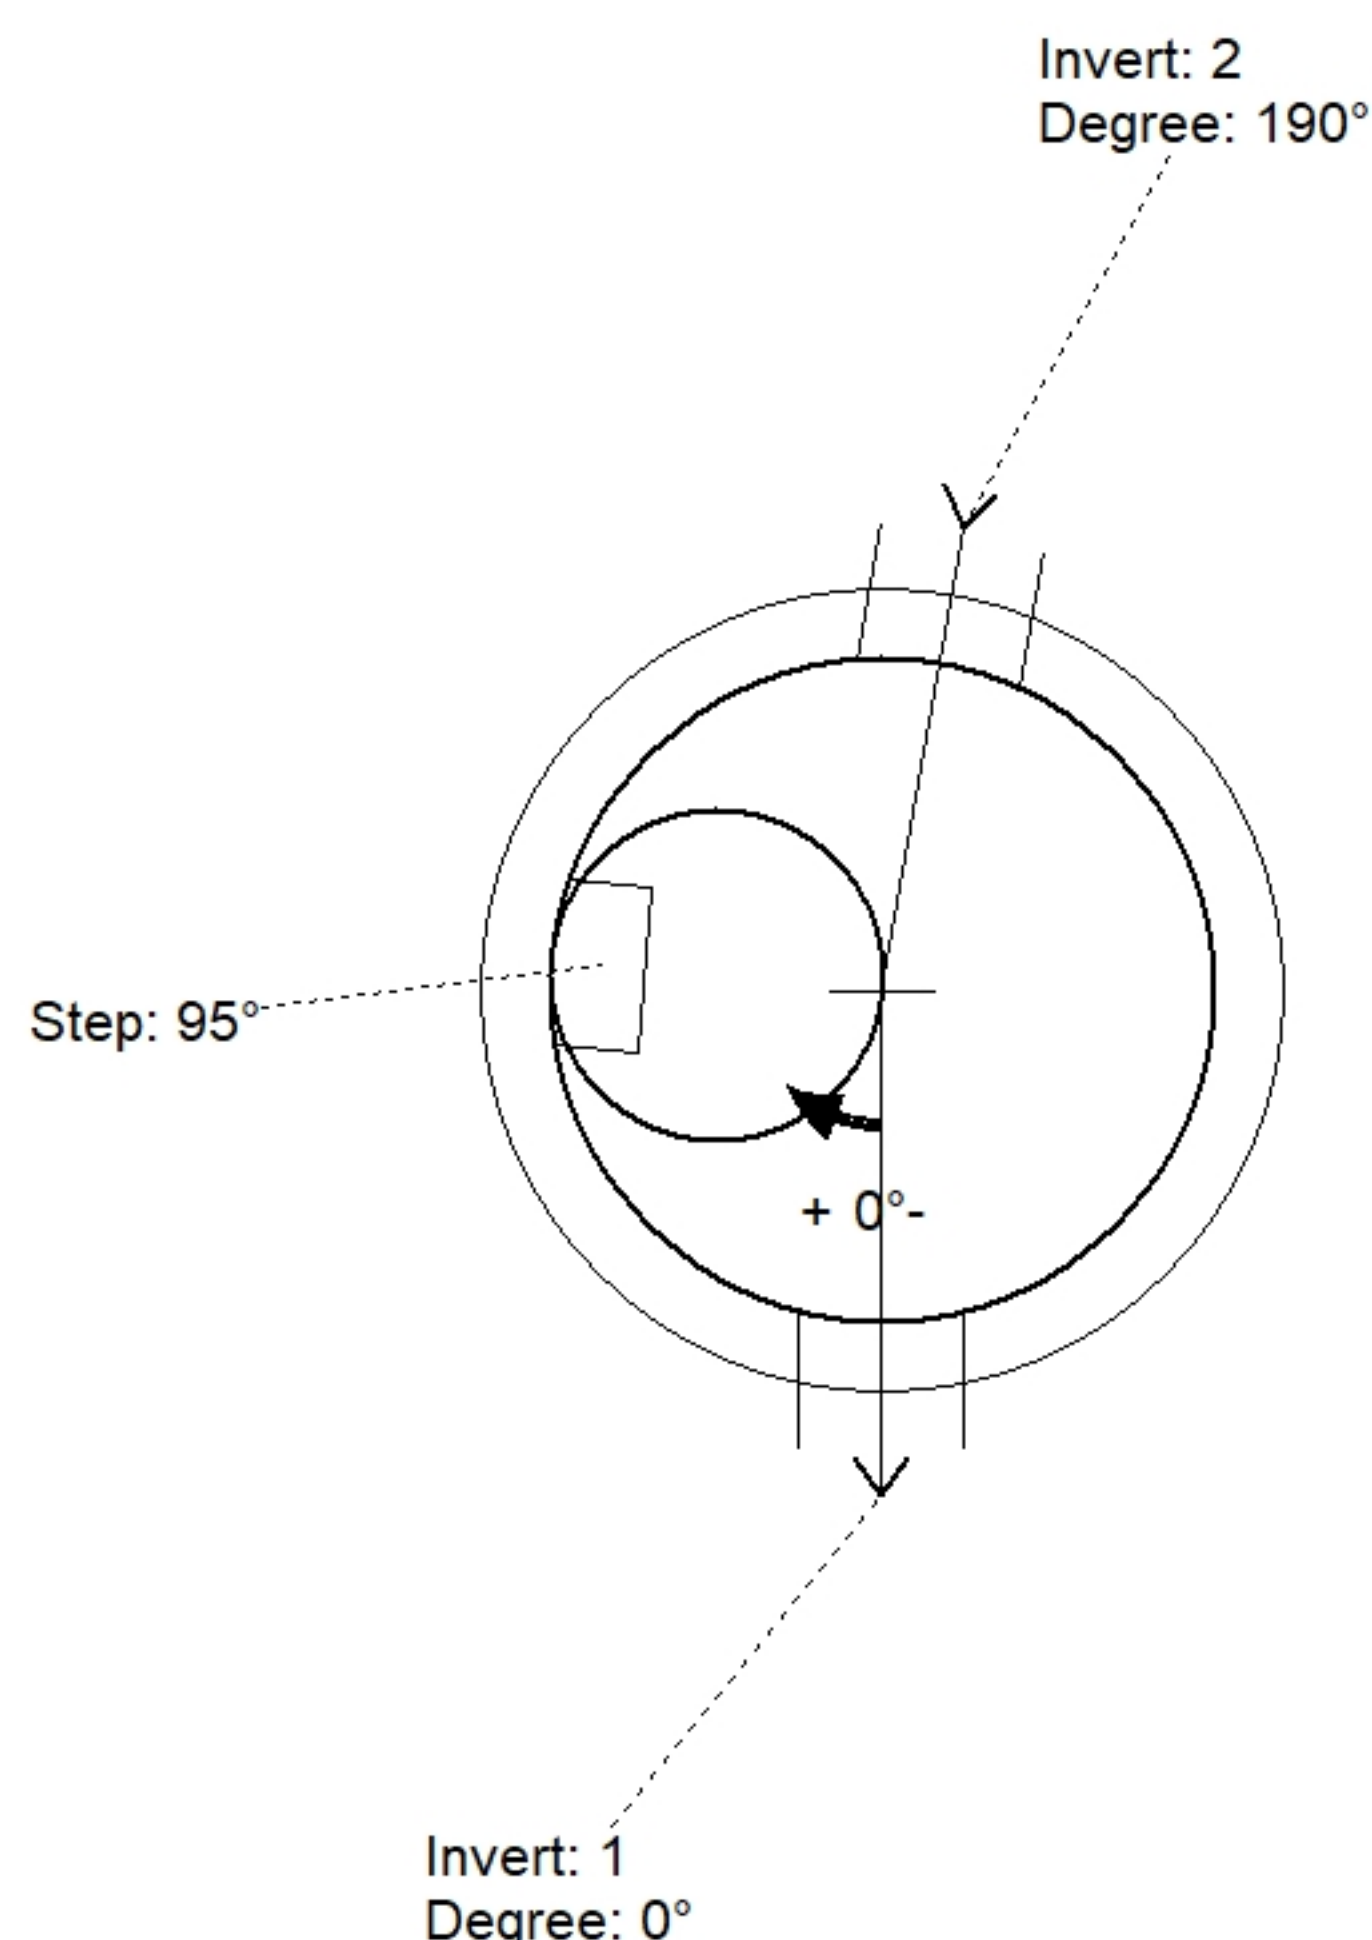

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	507.01'							
Reducer								
Invert 1	499.01'	0°	8" PVC SDR26	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	499.21'	190°	8" PVC SDR26	8.5"	12"	PSX 12-08 NYLO	2.4"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

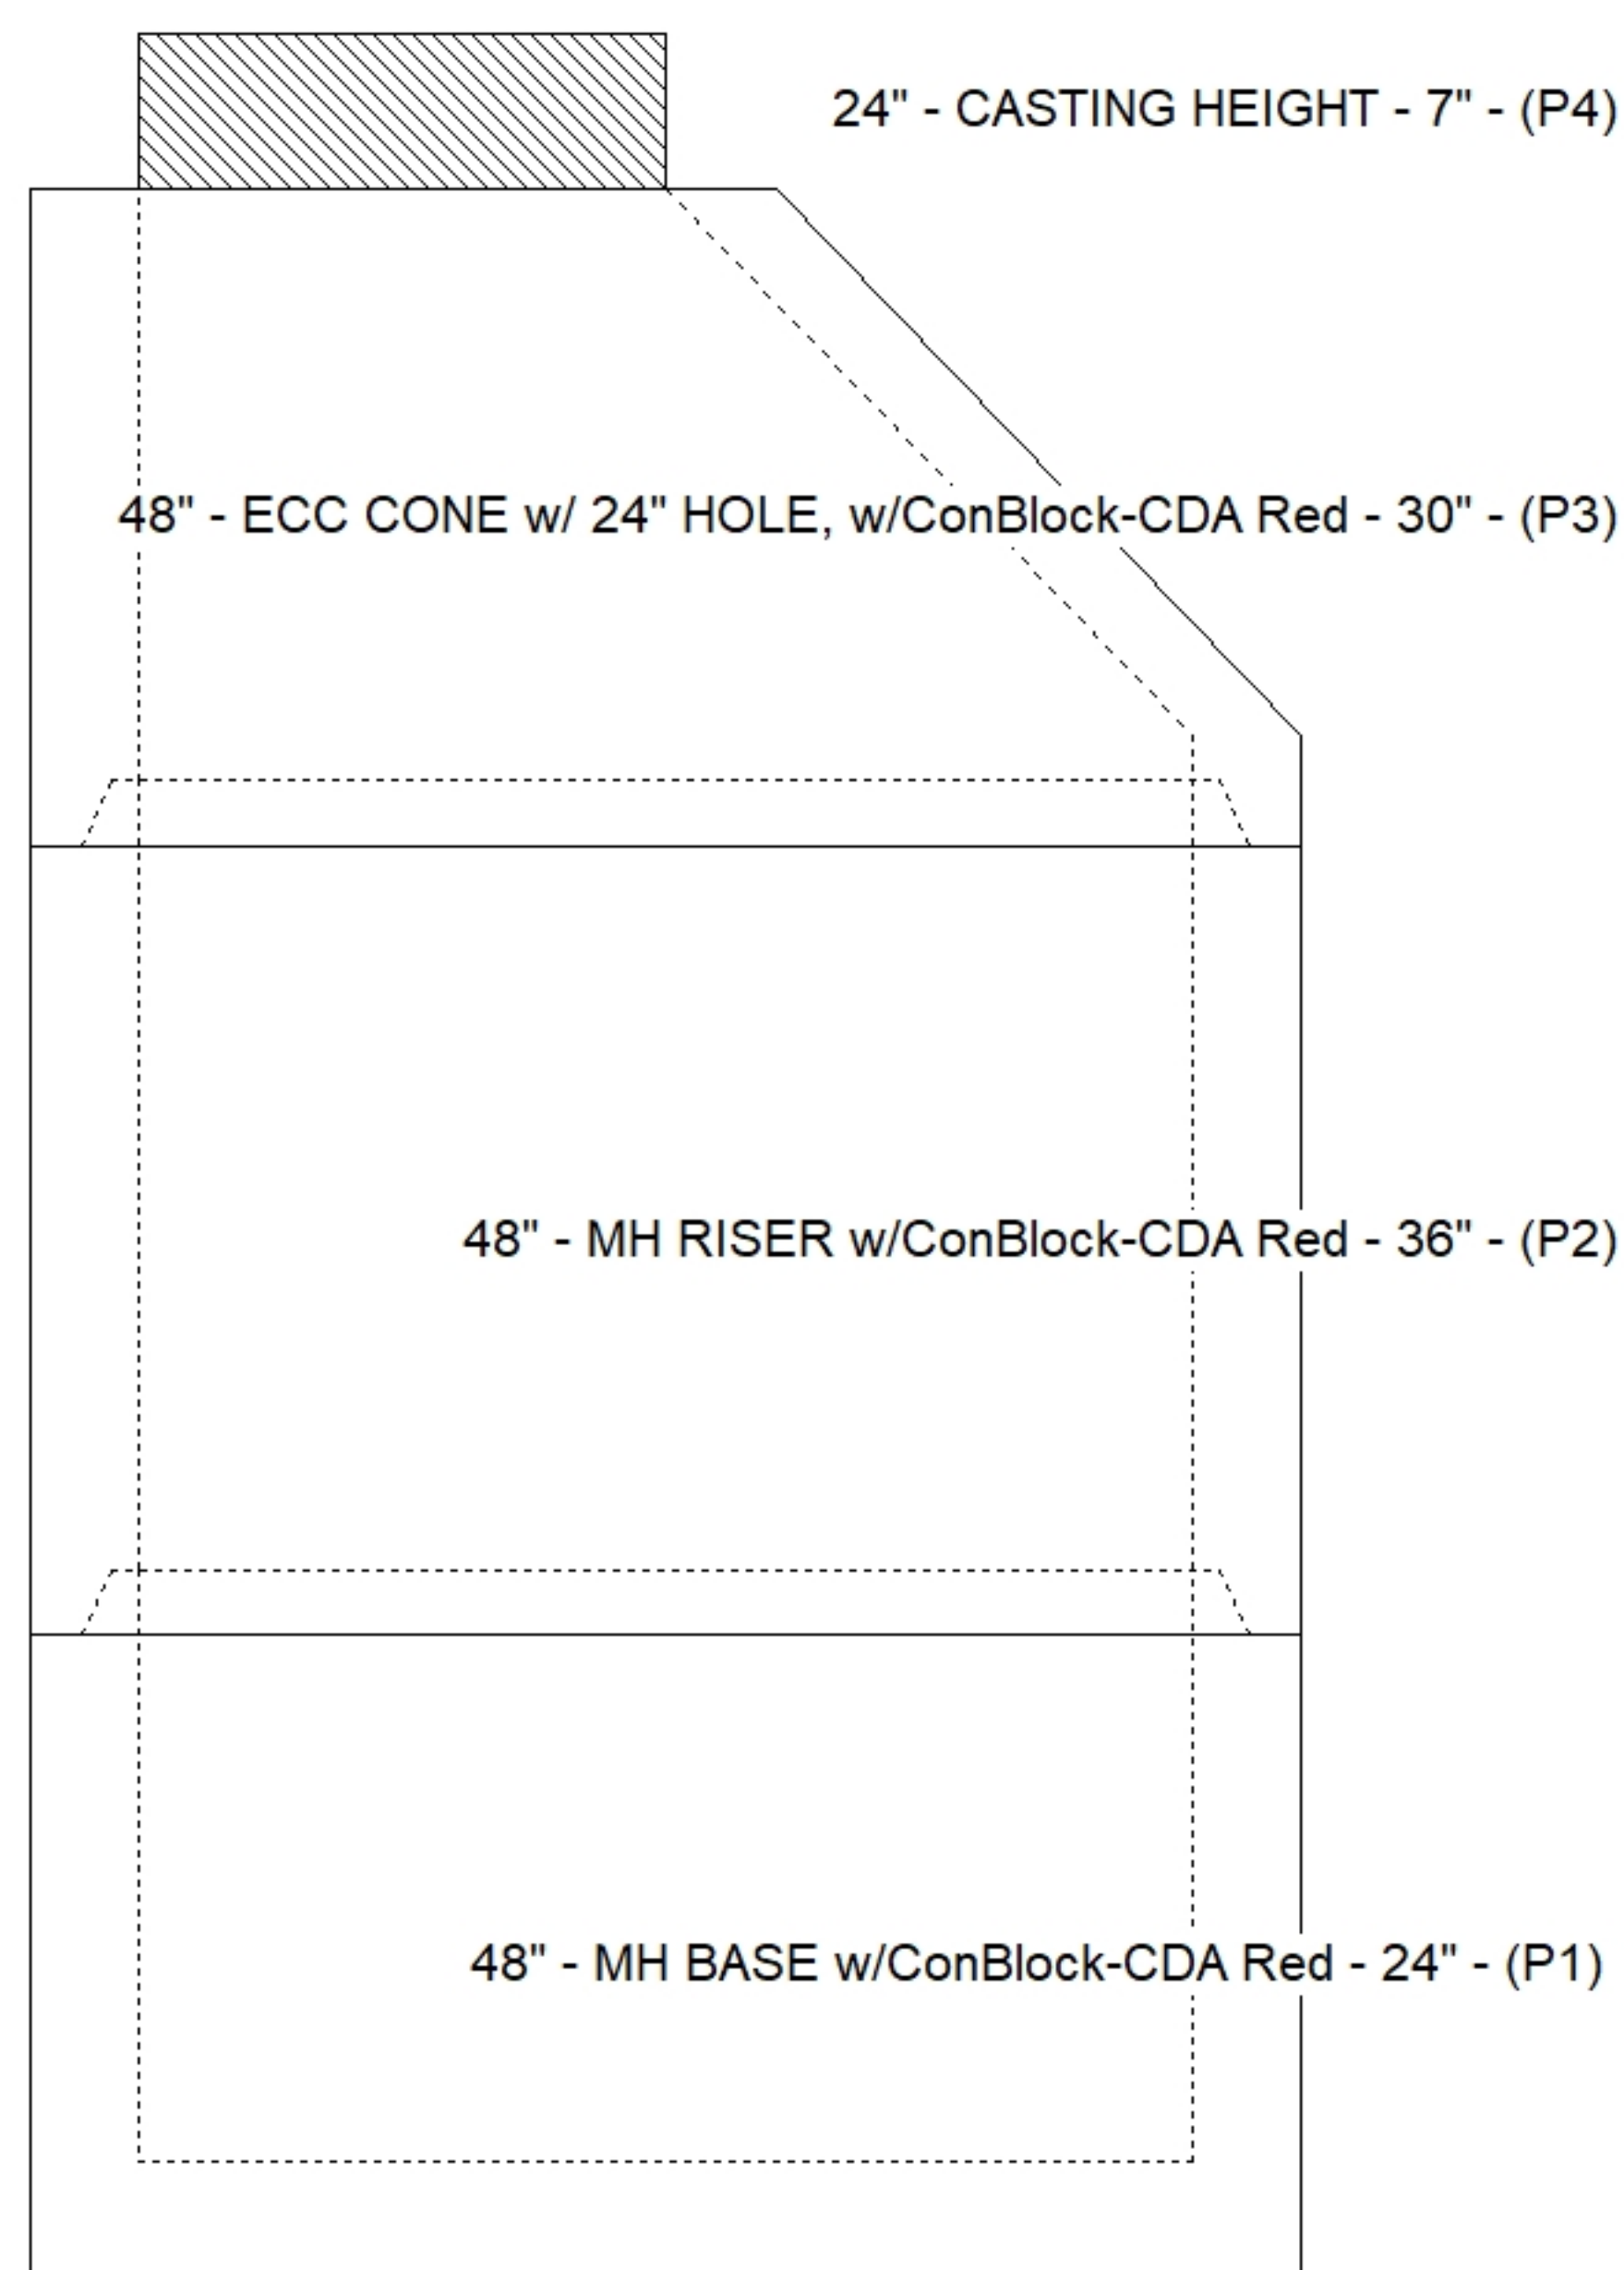

Default - Interior Dimensions

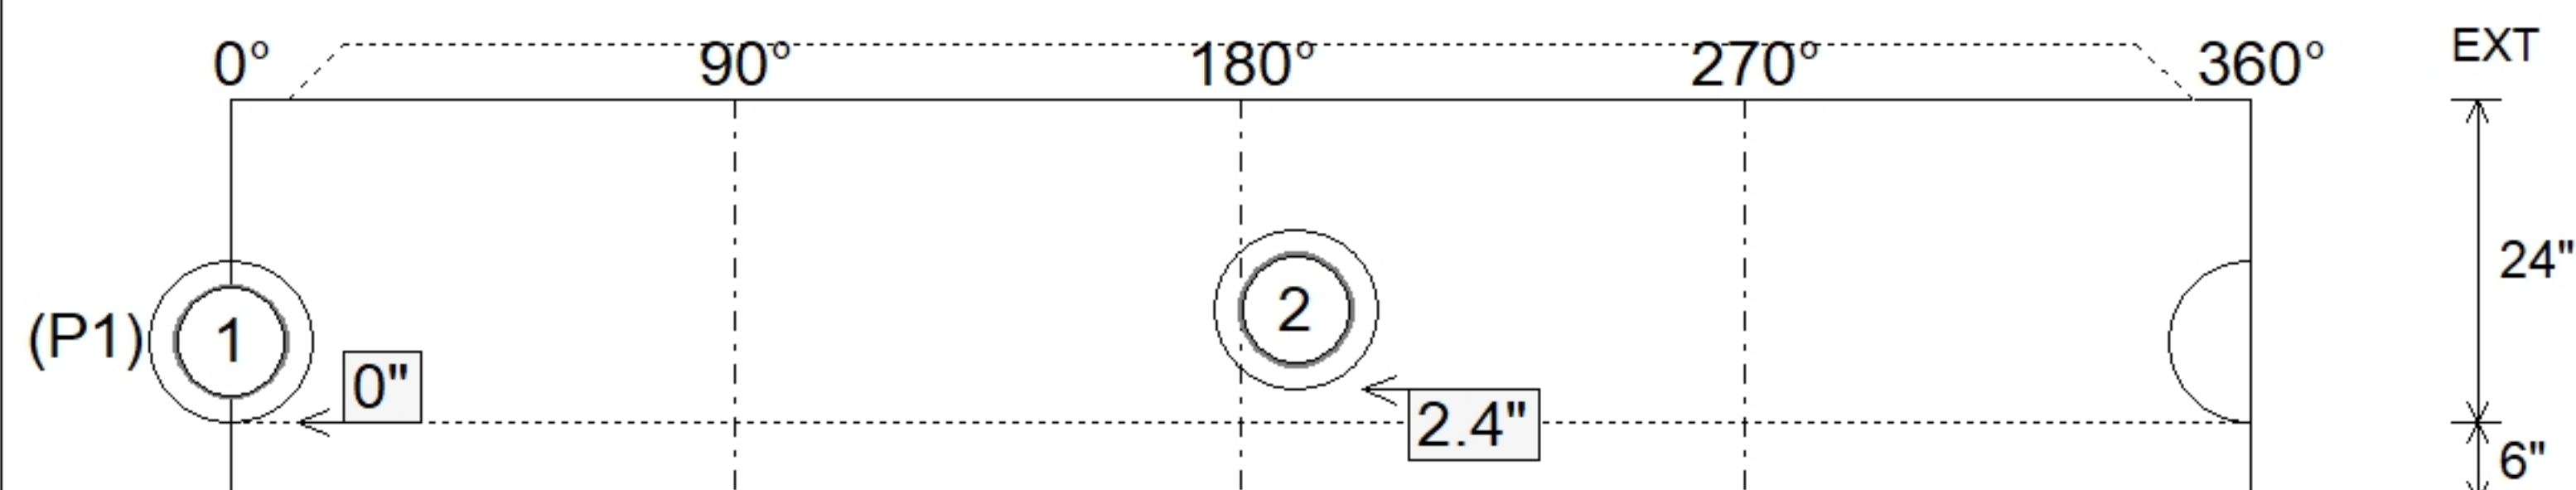

Submittal Drawing
9/24/2026 11:19:43 AM

SUBMITTAL
APPROVED BY:
