

Job Name: 26-1237 860558 Beulah Crossing Townhomes  
 Job Location: Lexington, KY  
 Contractor: Contech Engineering Solutions

Plant: Beaver Dam  
 2/6/2026 12:09:03 PM

Tech: S. Felletter  
 PC: T. Sekula



**Structure ID: 10-CS-5**

**P1 MH060BA18**

**MH BASE T/n**

P5) 30" - CASTING HEIGHT - 0"	0 lb
P4) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13"	2589 lb
P3) 60" - MH RISER T/G - 24"	2505 lb
P2) 60" - MH RISER T/G - 60"	5916 lb
P1) 60" - MH BASE T/n - 18"	4612 lb
1) CVSTENCILING	0 lb
1) ASSEMBLY REQUIRED	0 lb
3) 60" - Conseal CS-102 1.00"	0 lb
2) Hole - 20	0 lb
Structure Total:	15623 lb




Structure Notes:  
 4" CASTING BY OTHERS  
  
 LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE  
  
 ICAST TO INSTALL THE INTERNALS  
  
 CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE

Rim: 689' Rim to Invert: 5.65' Slack: 10.88" Sump: 58.08" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

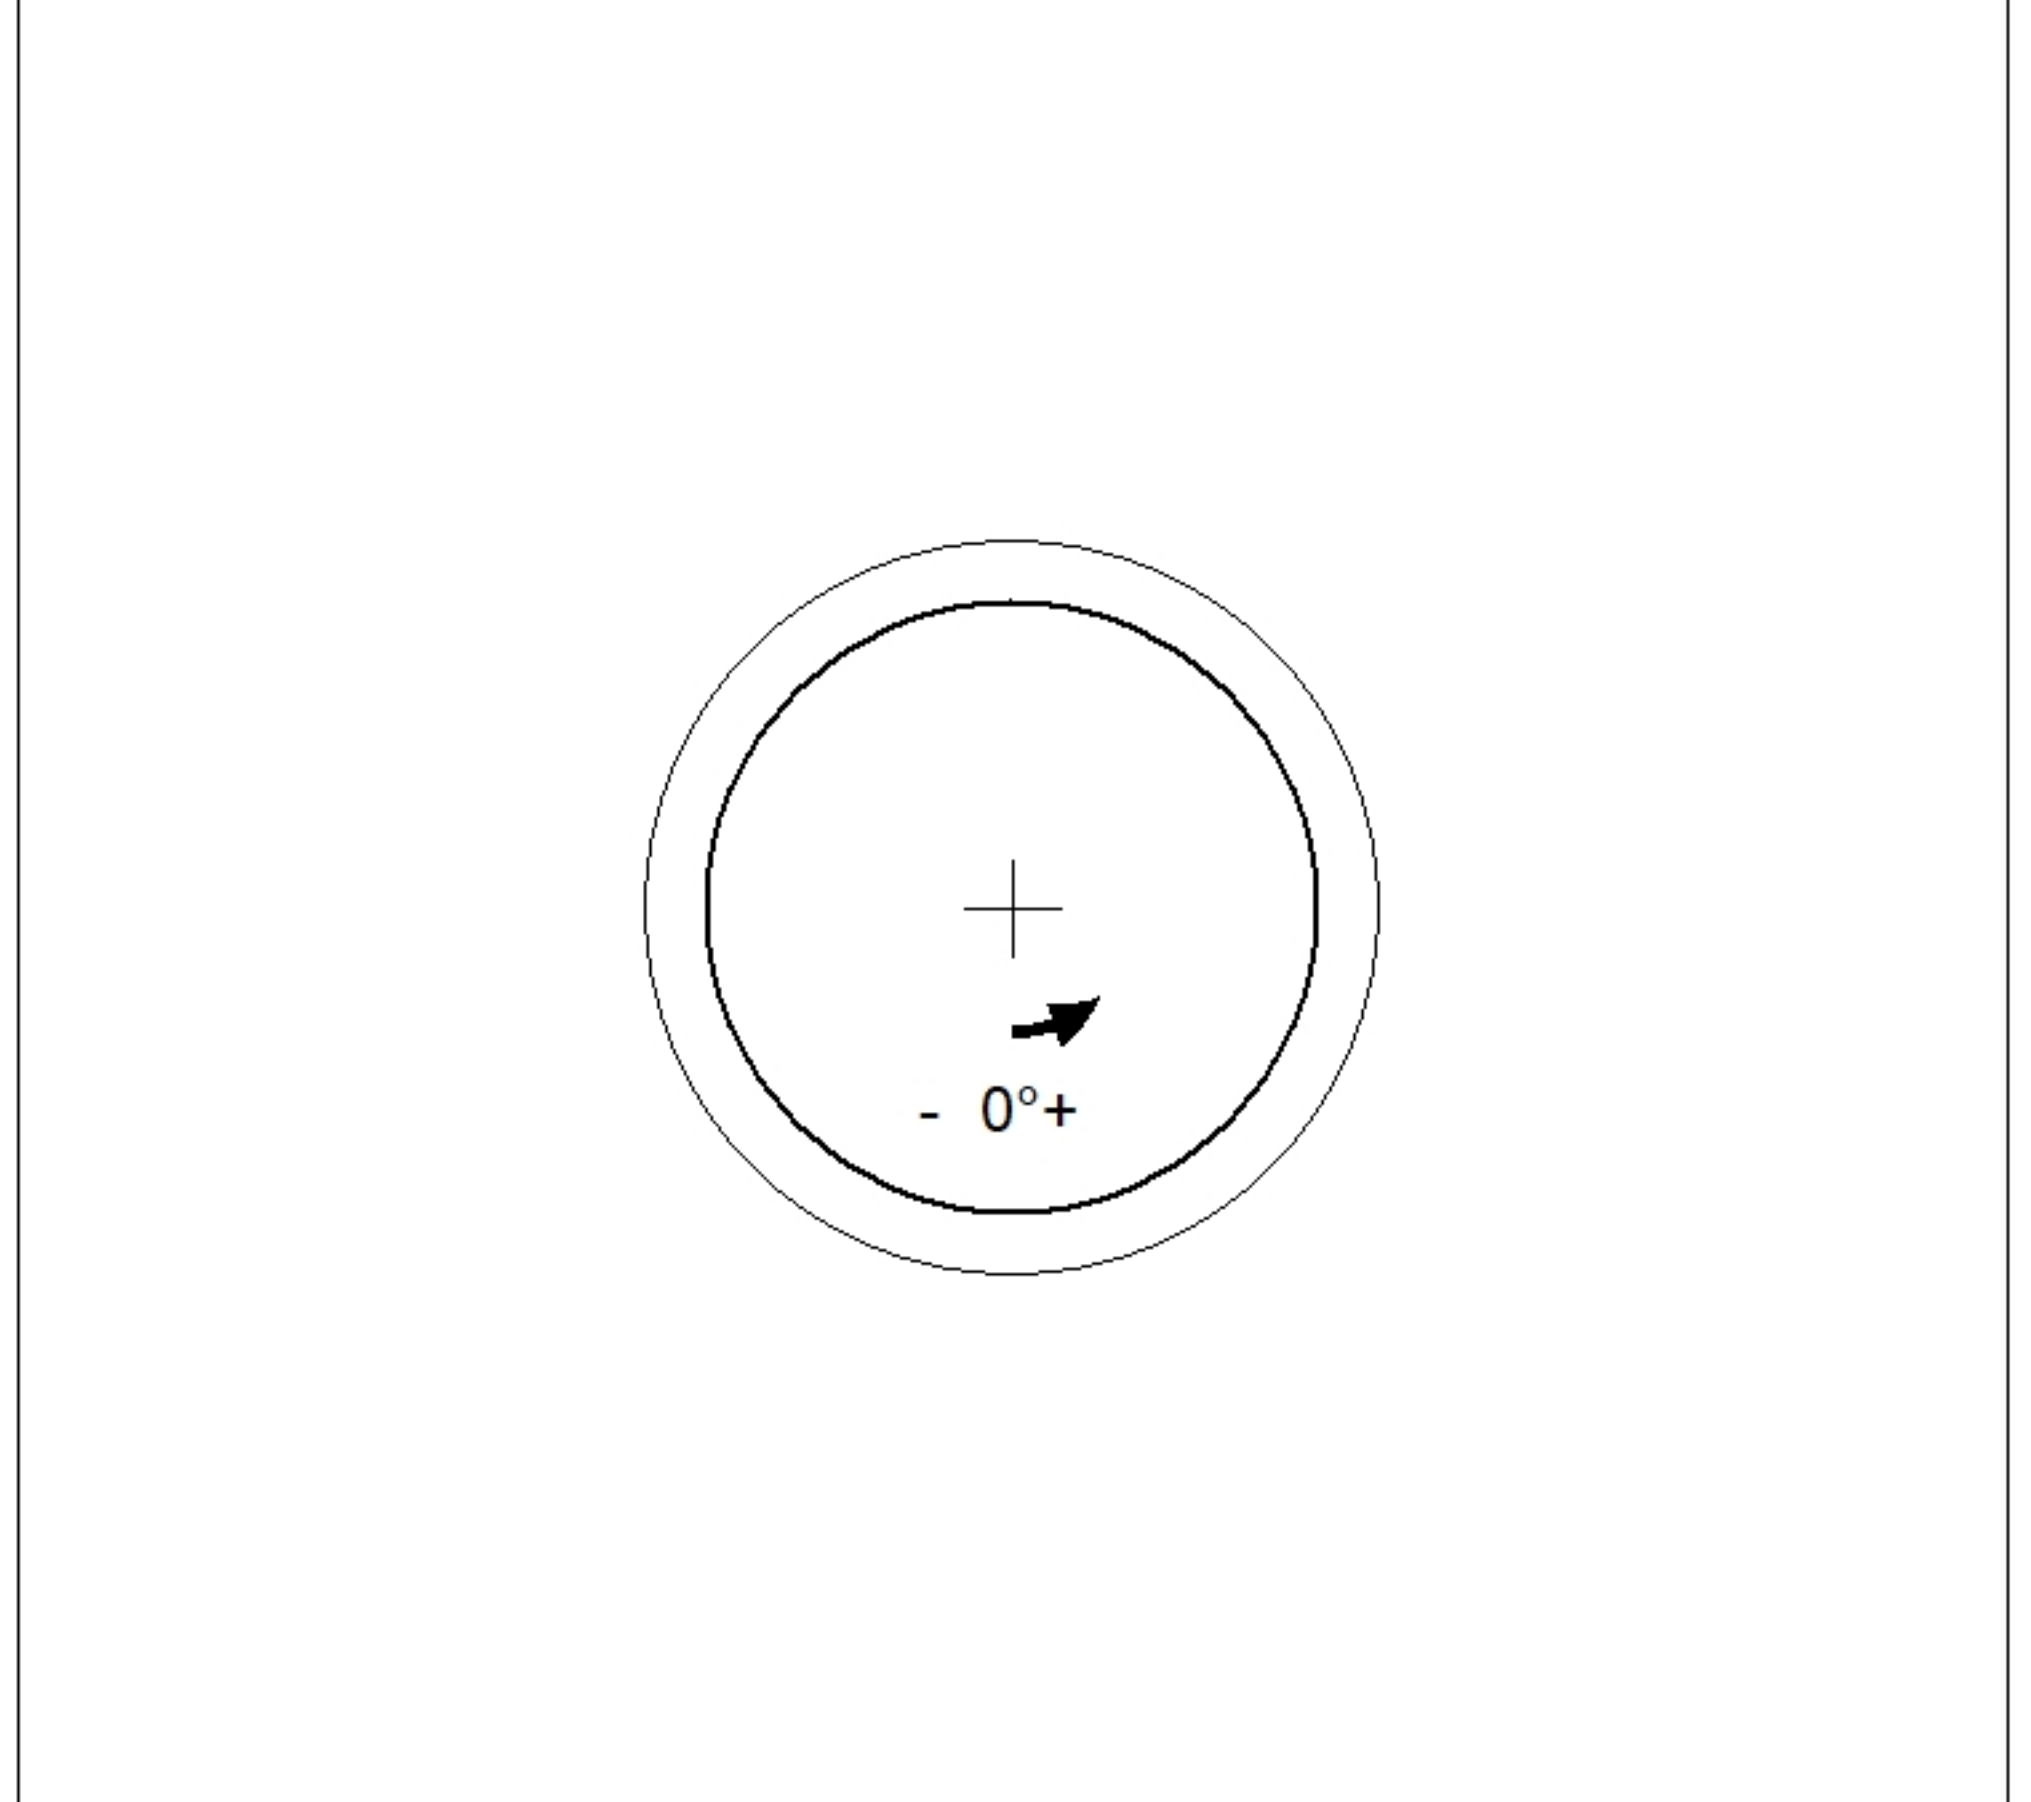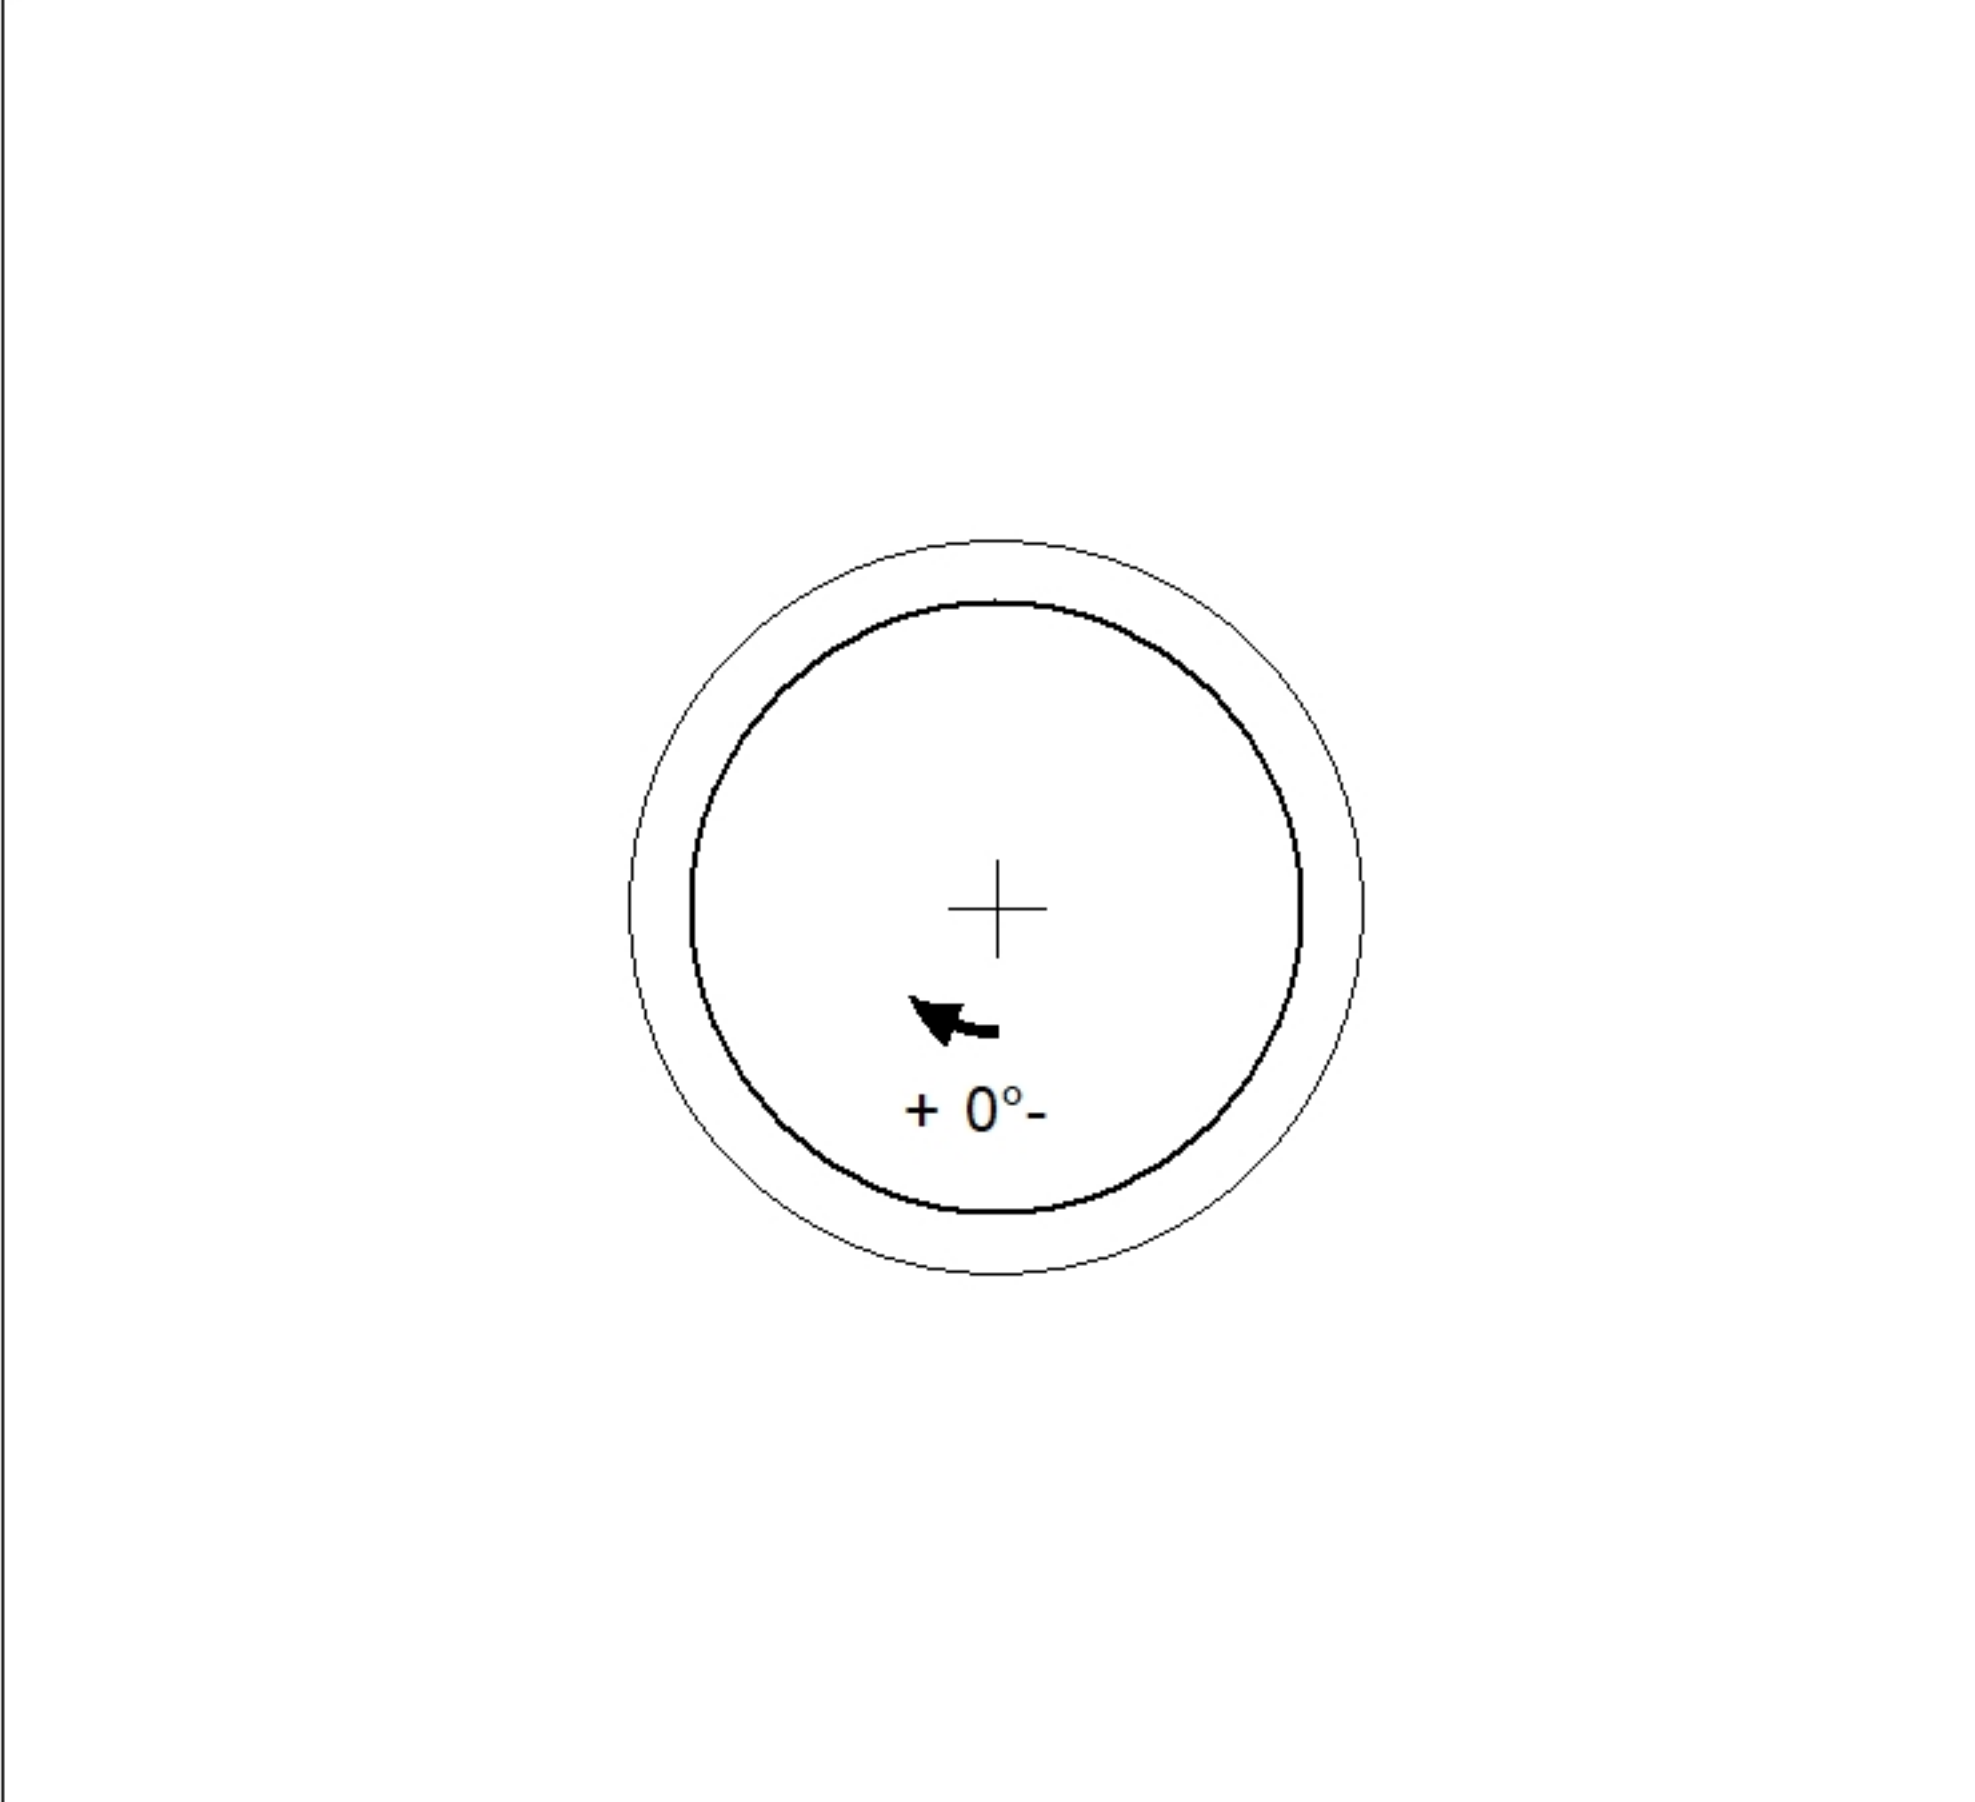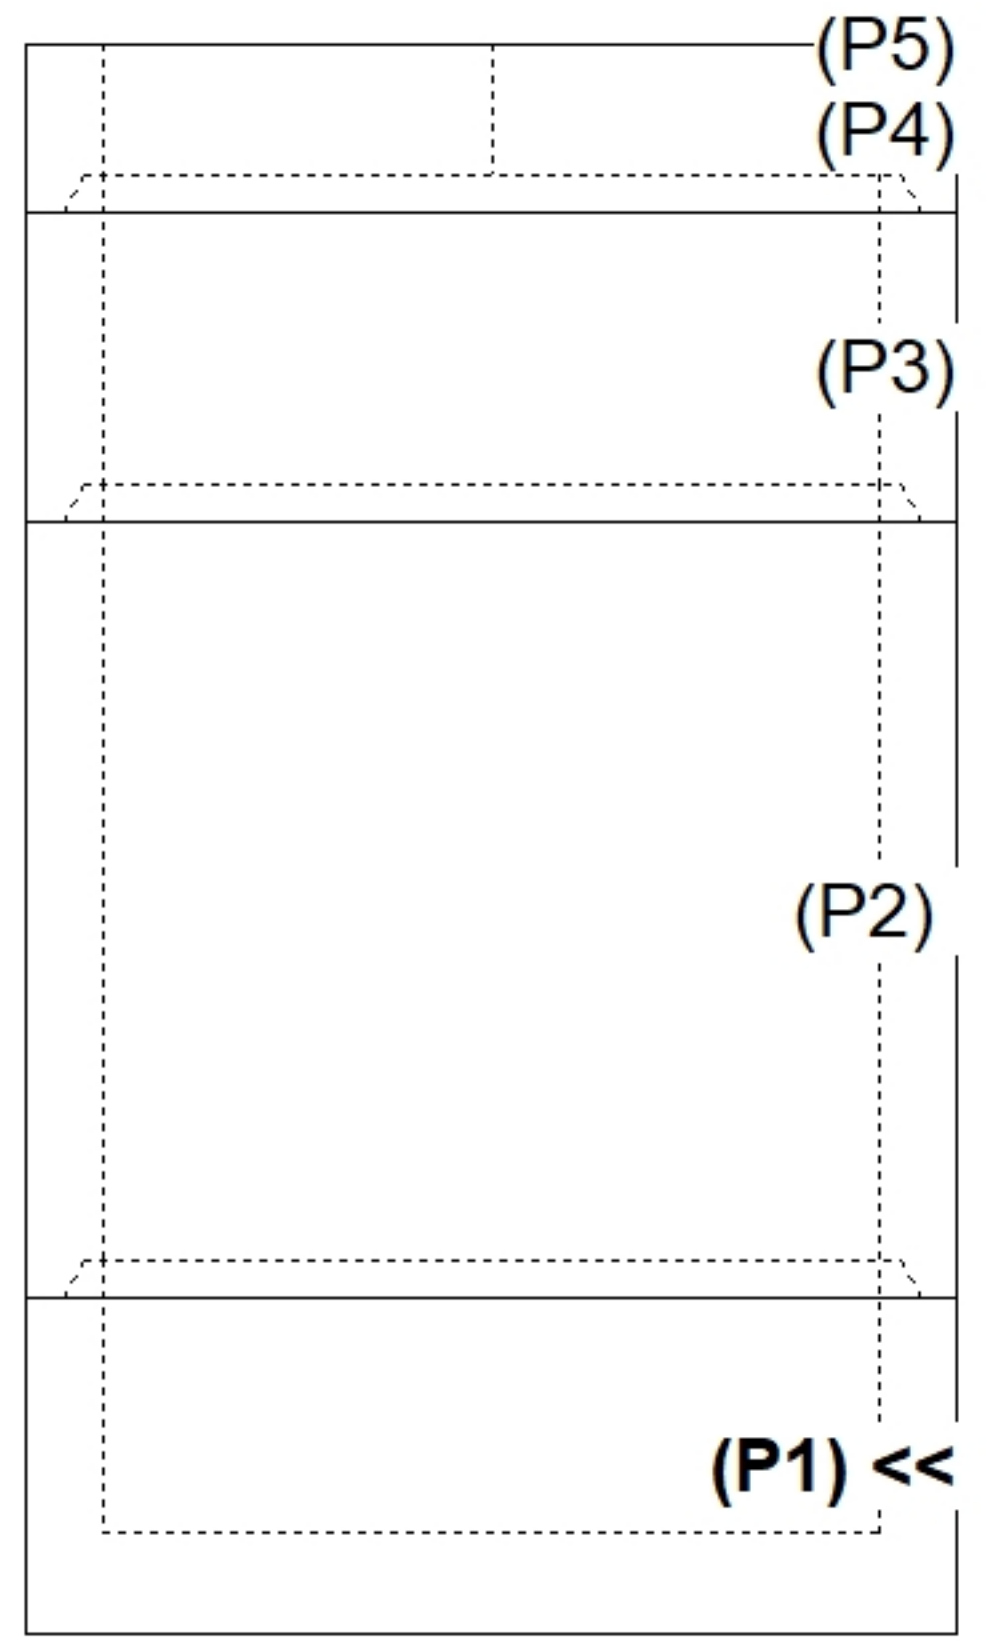

INSIDE WALL DIMENSIONS

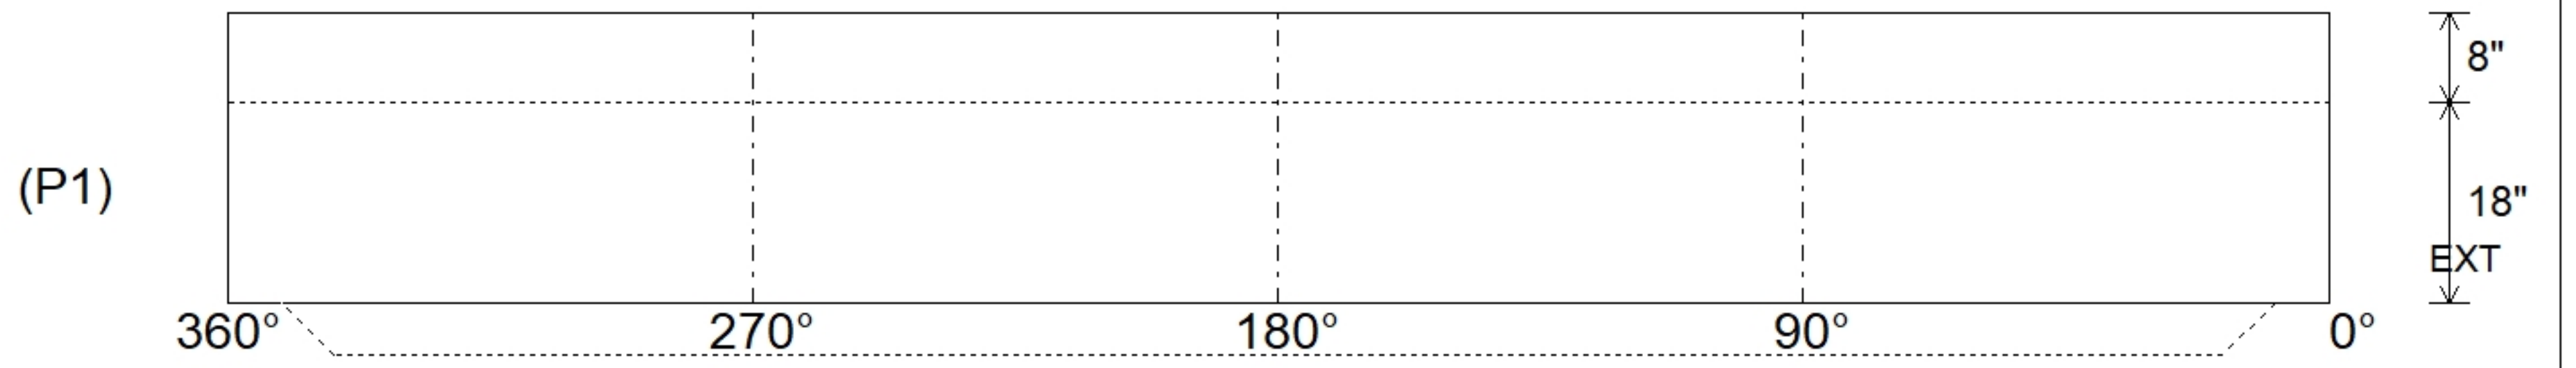

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 18" Height (Ext): 26"	Weight (Net): 4612 lb Volume (Net): 1.18cu.yd
----------------------------------	---------------------------------	--	--	--
