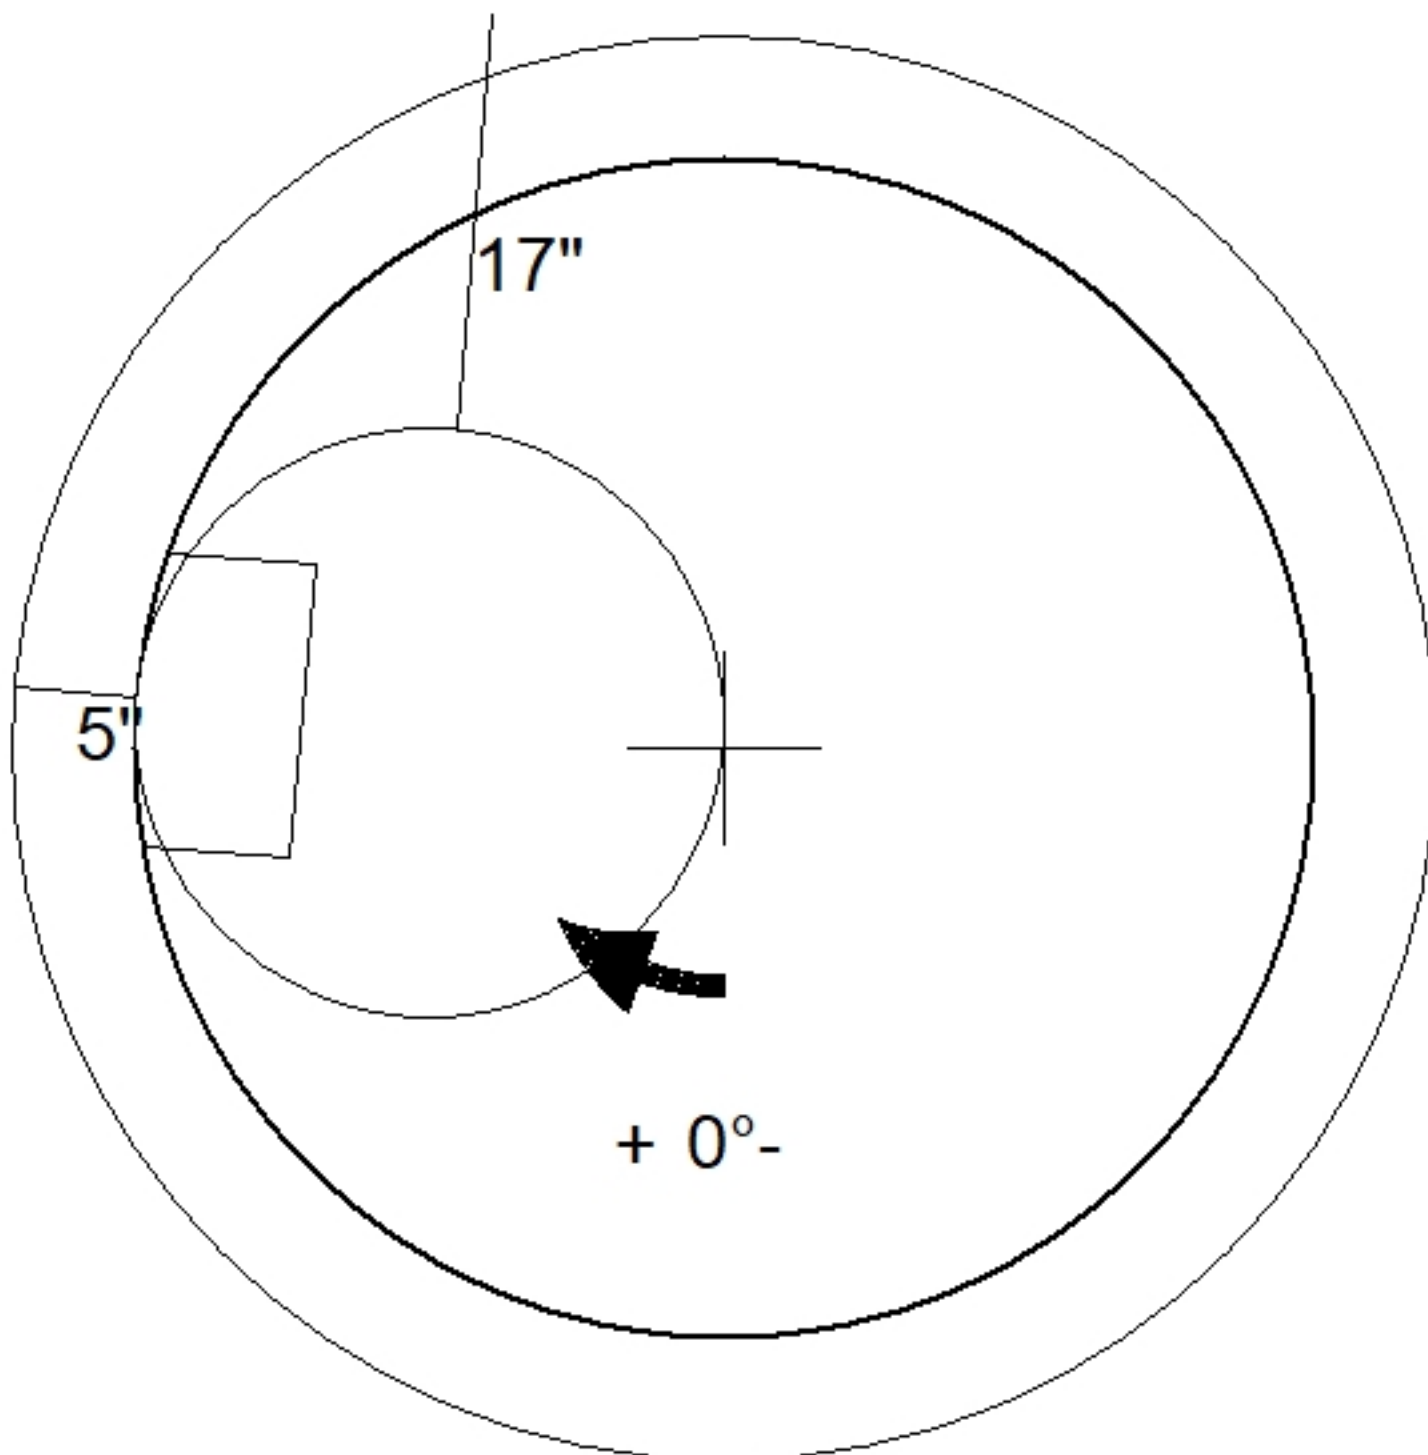
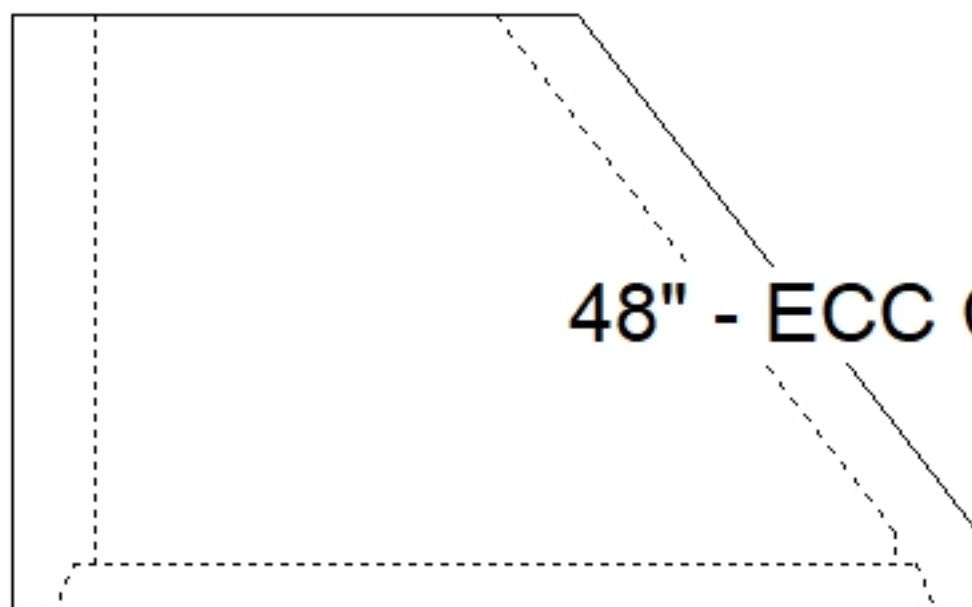


Job Name: 26-1279 Hilltopper Hall Ph. 2		Plant: Beaver Dam	Tech: S. Felletter	
Job Location: Bowling Green, KY		6/24/2026 8:45:41 AM	PC: M. Sullivan	
Contractor: Stewart Richey				
Structure ID: 6-3 ST-MH				
P2 MH048CN36		ECC CONE w/ 24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 3" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 48" 1) CASTING - HOE MCB-315-B Fr./Bar Grate 1) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 16 7) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 3000 lb 4512 lb 255 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7969 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MCB-315-B). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12). - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 36" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
