

Job Name: 26-1301 WCSC New Pre-K Classroom Addition
Job Location: Newburgh, IN
Contractor: Hahn Excavating, Inc.

PC: E. Bradley
 TECH: S. Felletter
 Plant: Beaver Dam



Structure ID: **Str. 8-9 ST-CI**
 Spec: Storm
 Type: BX 8inW, 8inF
 Size: 24" x 36"

Rim: 444.88'
 Invert: 441.7'
 Rim to Invert: 3.18'

Sump: 6"
 Floor (Top): 441.2'
 Floor Height: 8"


Floor (Bot): 440.533'
 Overall Height: 4.333'
 Slack: 0.16"

Structure Notes:


- PER ASTM C913 SPECIFICATIONS.
 - CONCRETE = 4,000 PSI AT 28 DAYS.
 - NO INVERT CHANNEL.
 - CASTING BY ICAST (HOE 525 FLAT SET)
- REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:


P2) 24" x 36" - CASTING HEIGHT - 6"	0 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 38"	4948 lb
1) CASTING - HOE 525 SET FLAT GRATE (F/G/H)	442 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
2) Hole - 16	0 lb
Structure Total:	5390 lb

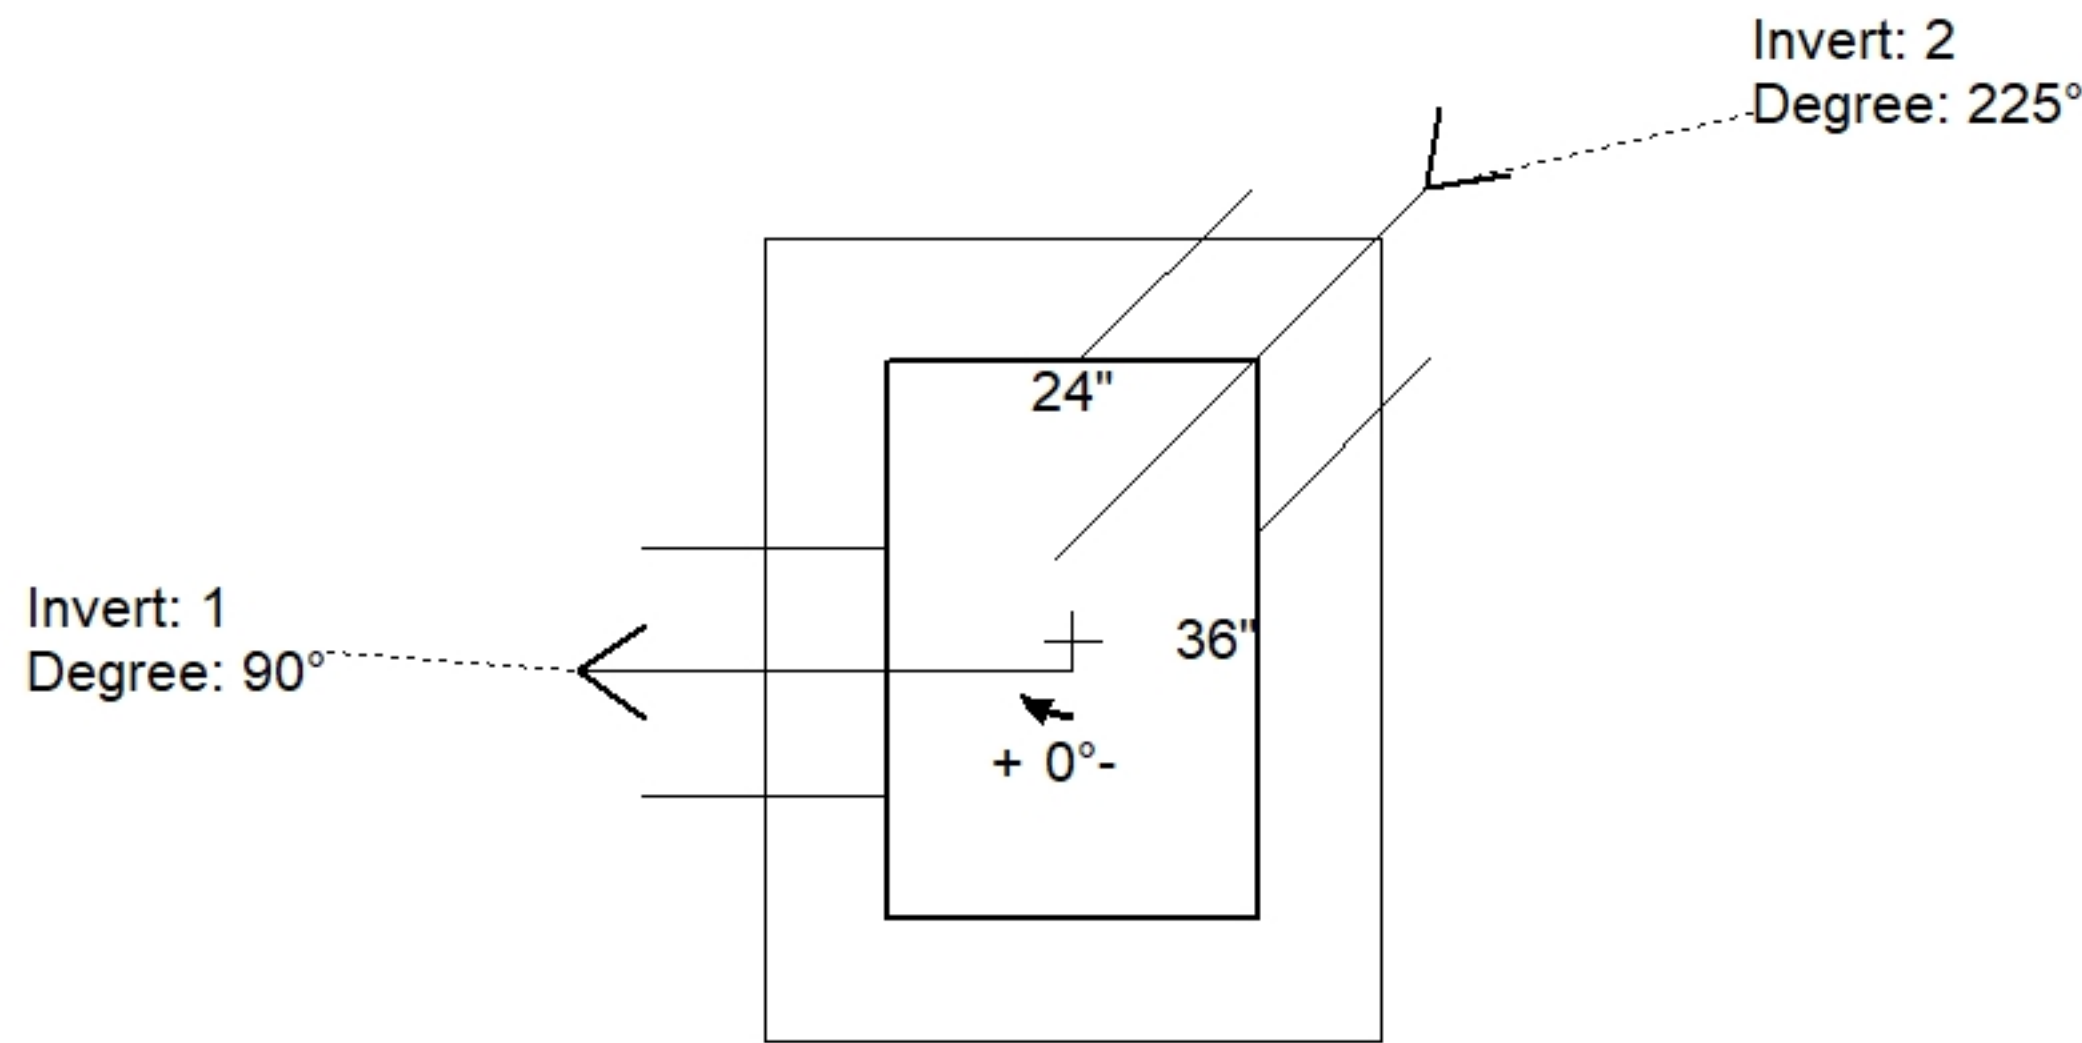

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	444.88'							
Reducer								
Invert 1	441.7'	90°	12" HDPE	14.5"	16"	Hole 16	4.75"	P1
Invert 2	441.7'	225°	12" HDPE	14.5"	16"	Hole 16	4.75"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

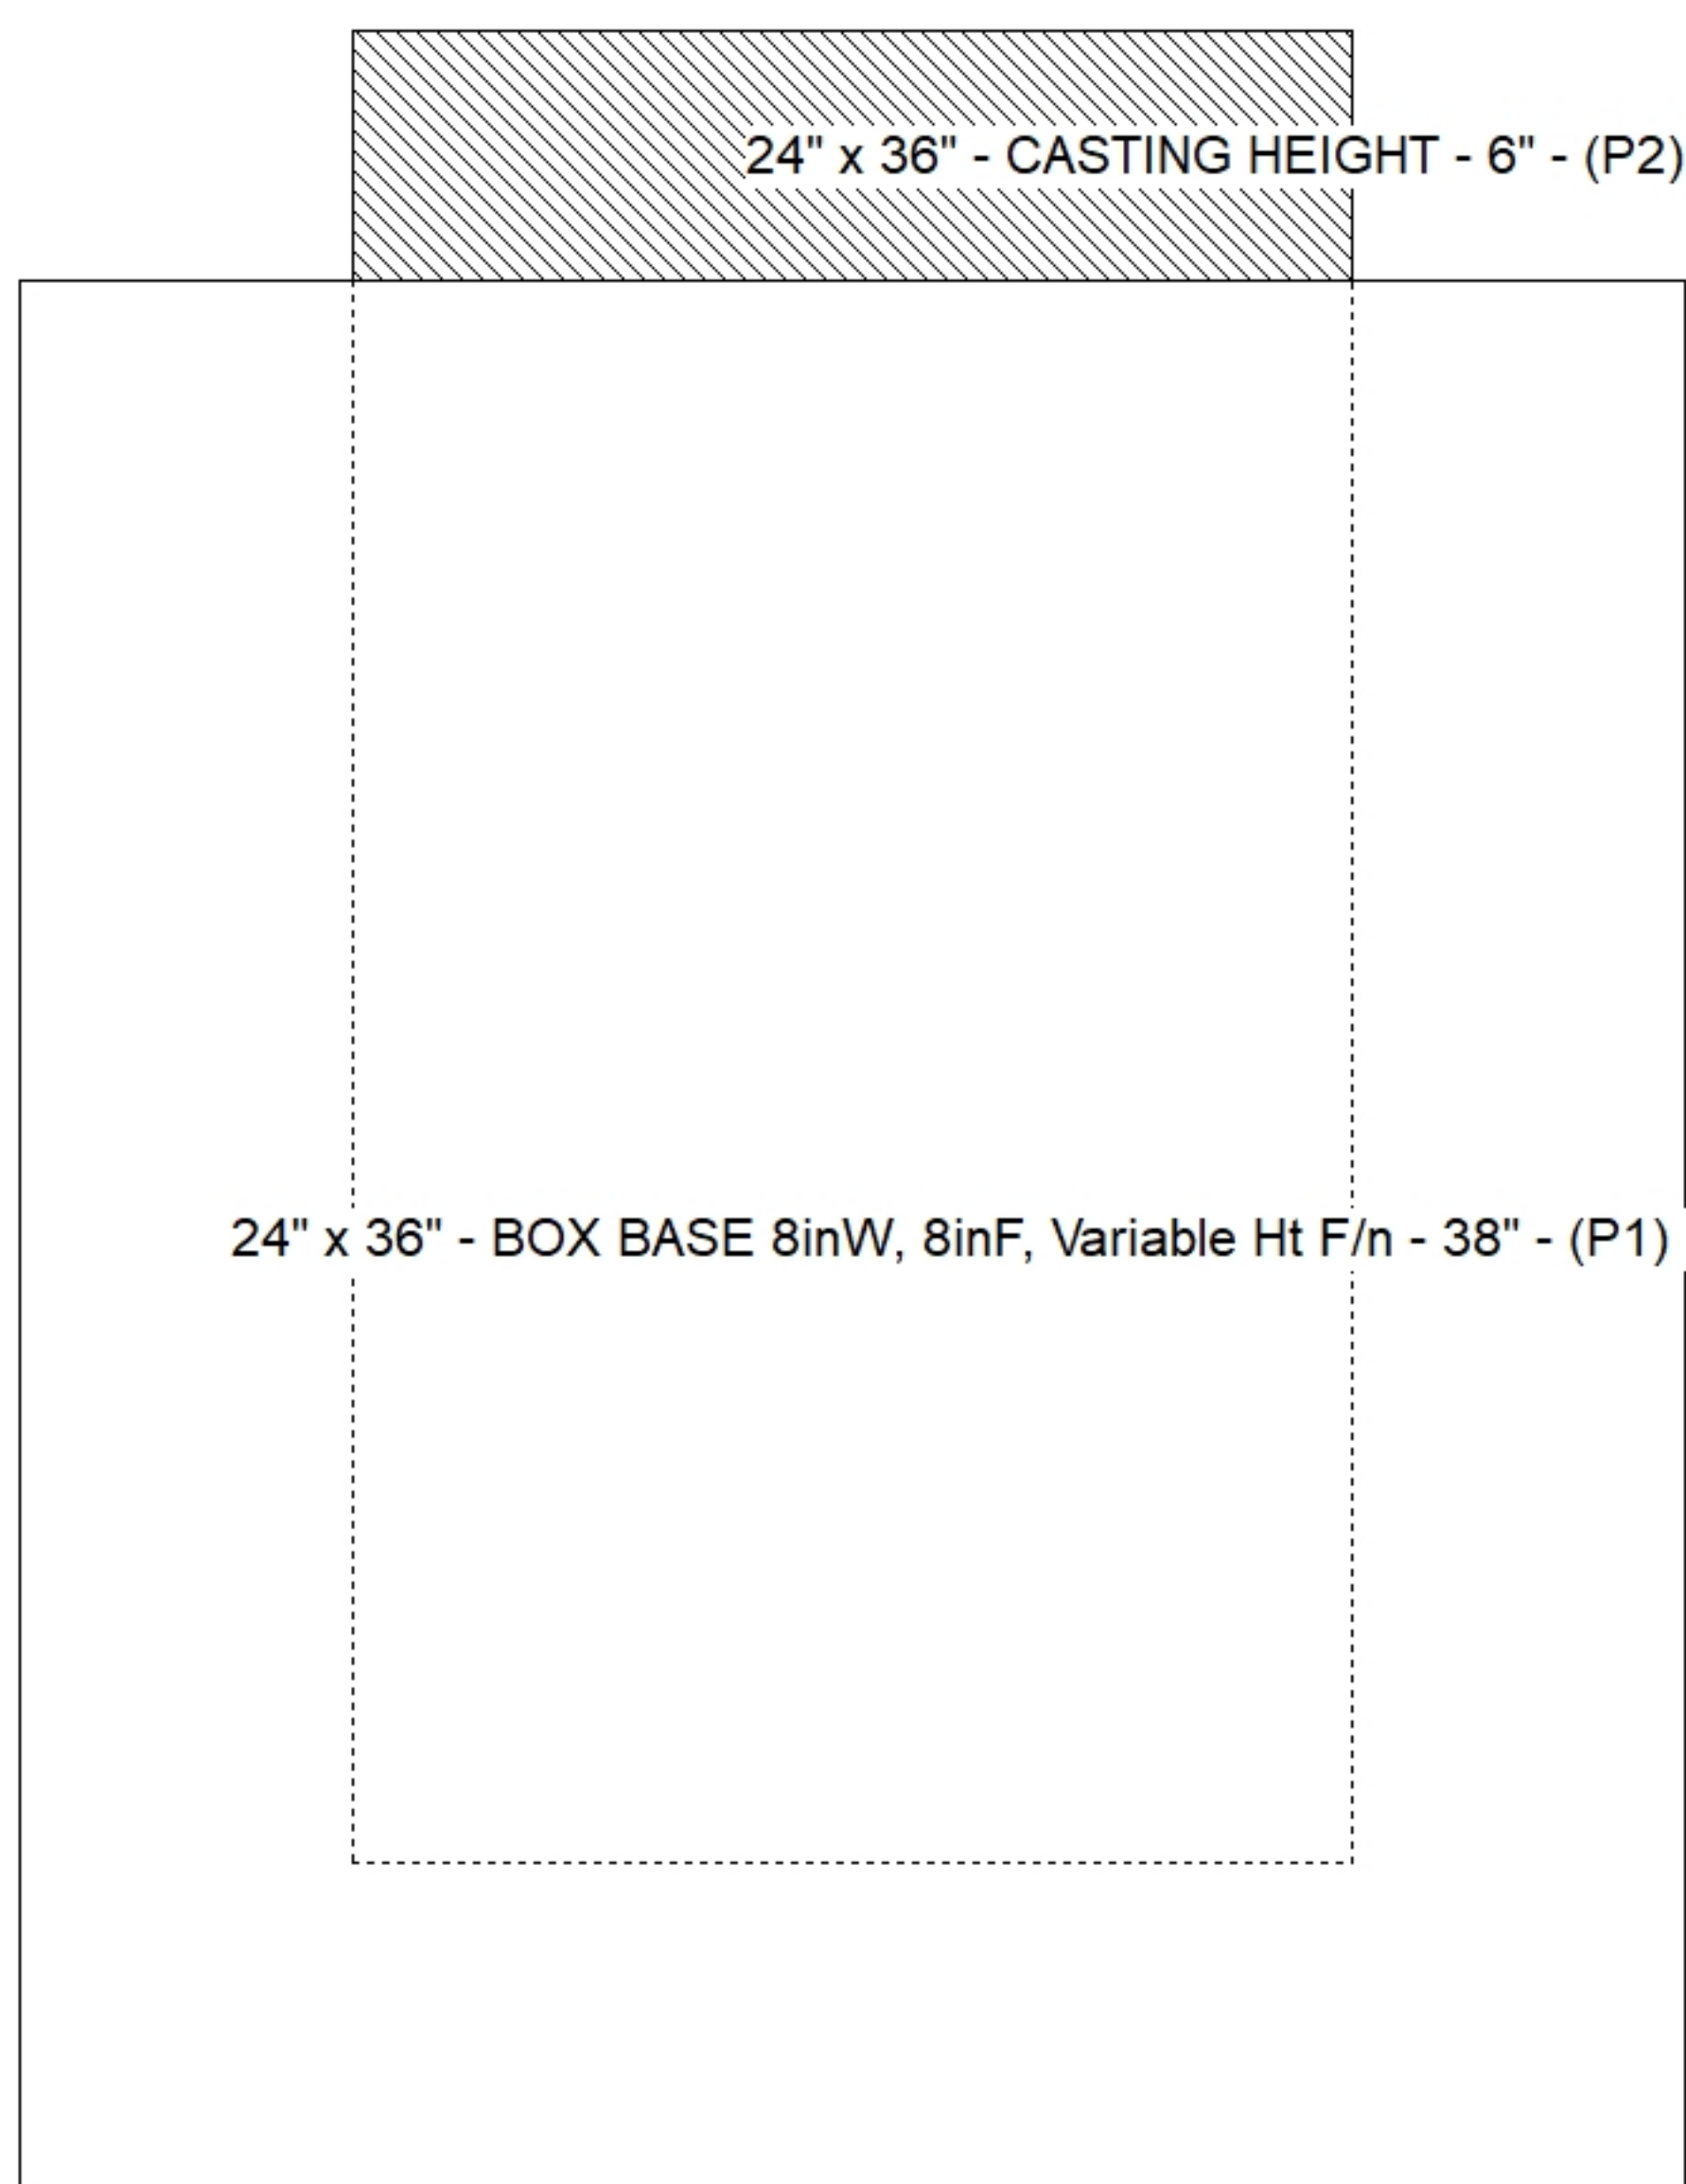

Default - Interior Dimensions

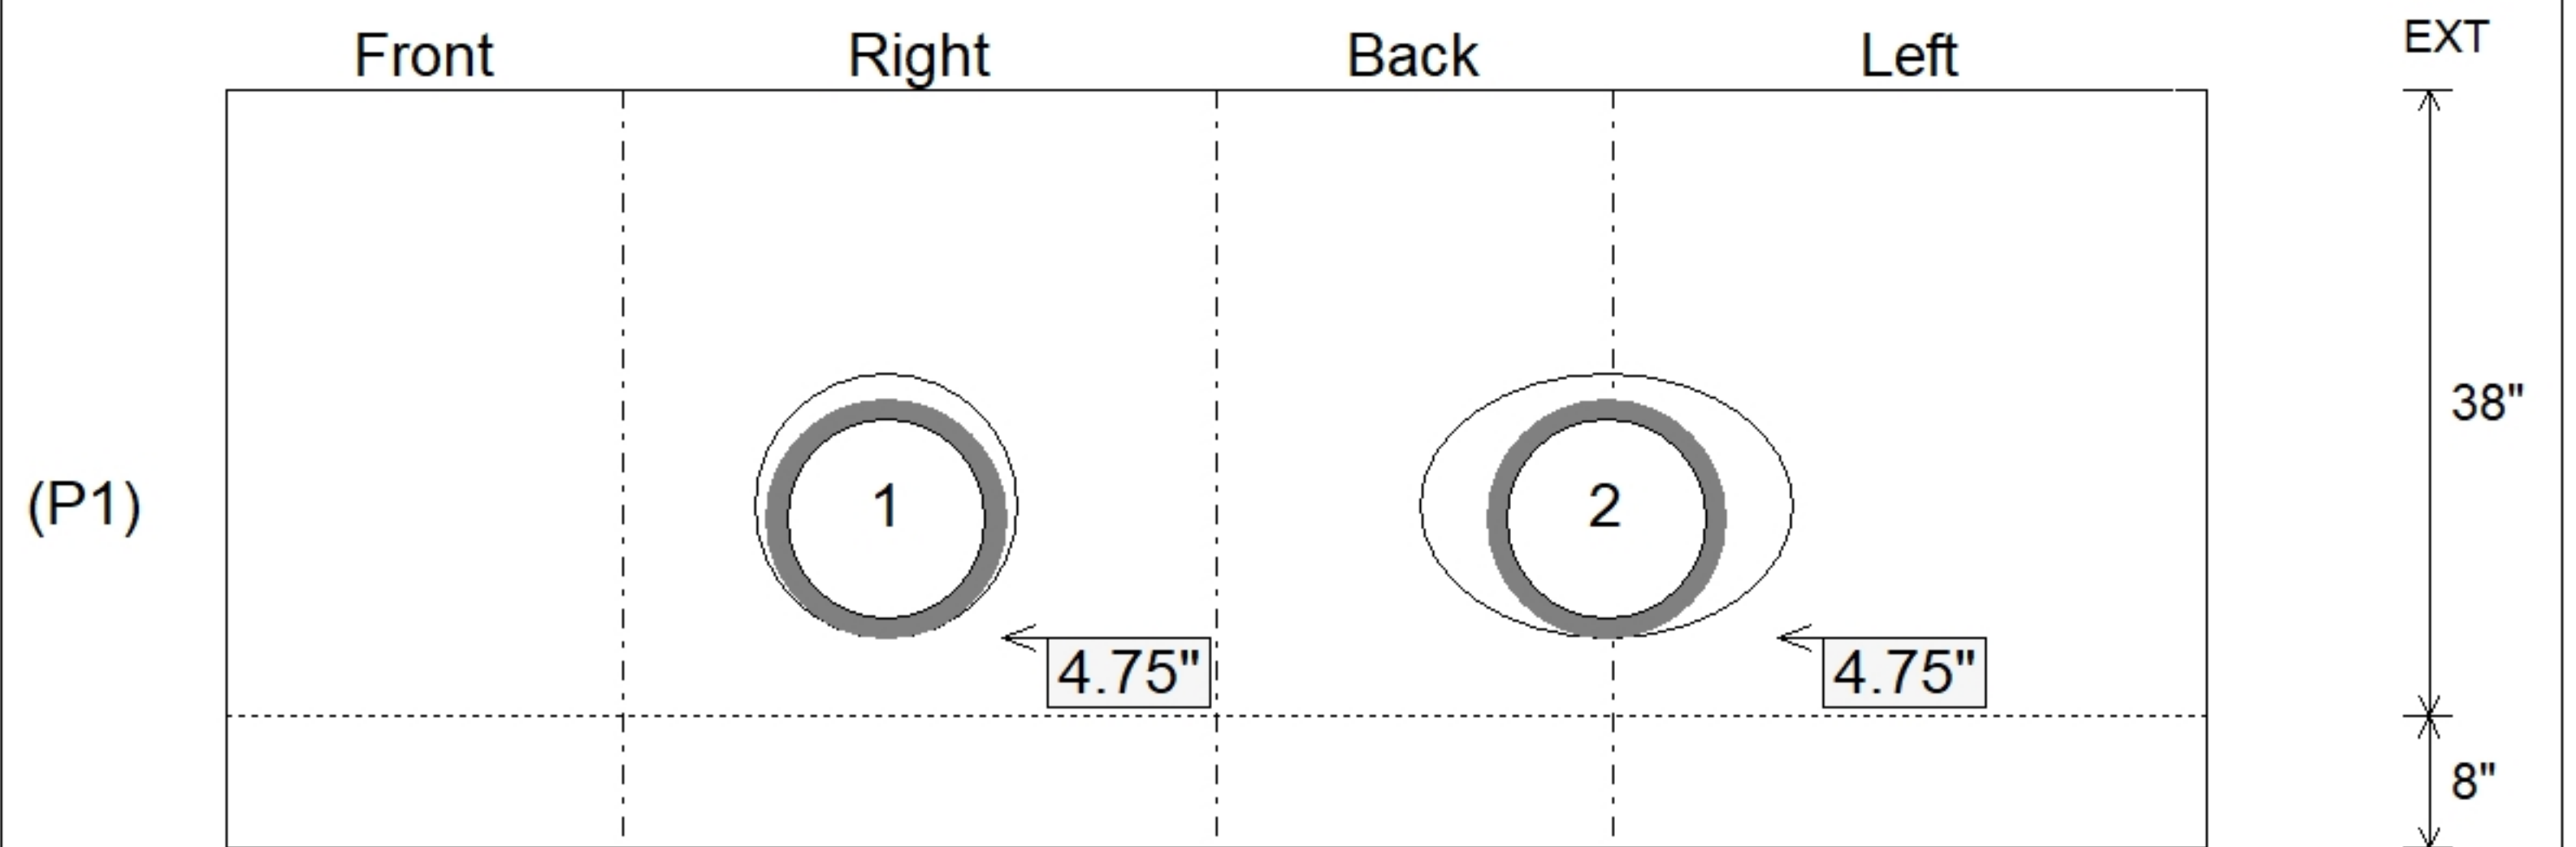

Submittal Drawing
 3/24/2026 10:18:58 AM

SUBMITTAL
 APPROVED BY:
