

Contractor: Stewart Richey

Plant: 100



Size: 60"

Rim: 547.9'
Invert: 543.98'
Rim to Invert: 3.92'

Sump: 0"
Floor (Top): 543.98'
Floor Height: 8"


Floor (Bot): 543.313'
Overall Height: 4.583'
Slack: 0.04"

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)

P2) 24" - CASTING HEIGHT - 7"
P1) 60" - MH MONOTOP (FB) w/24" Hole, Custom Ht - 48"
1) CASTING - JBS 1150 F/C STORM
2) DOGHOUSE - 32"x32"
1) Hole - 32
4) MH Step ML-10-TDS-NCR - 10"



0 lb
5017 lb
250 lb
0 lb
0 lb
0 lb

Structure Total: 5267 lb

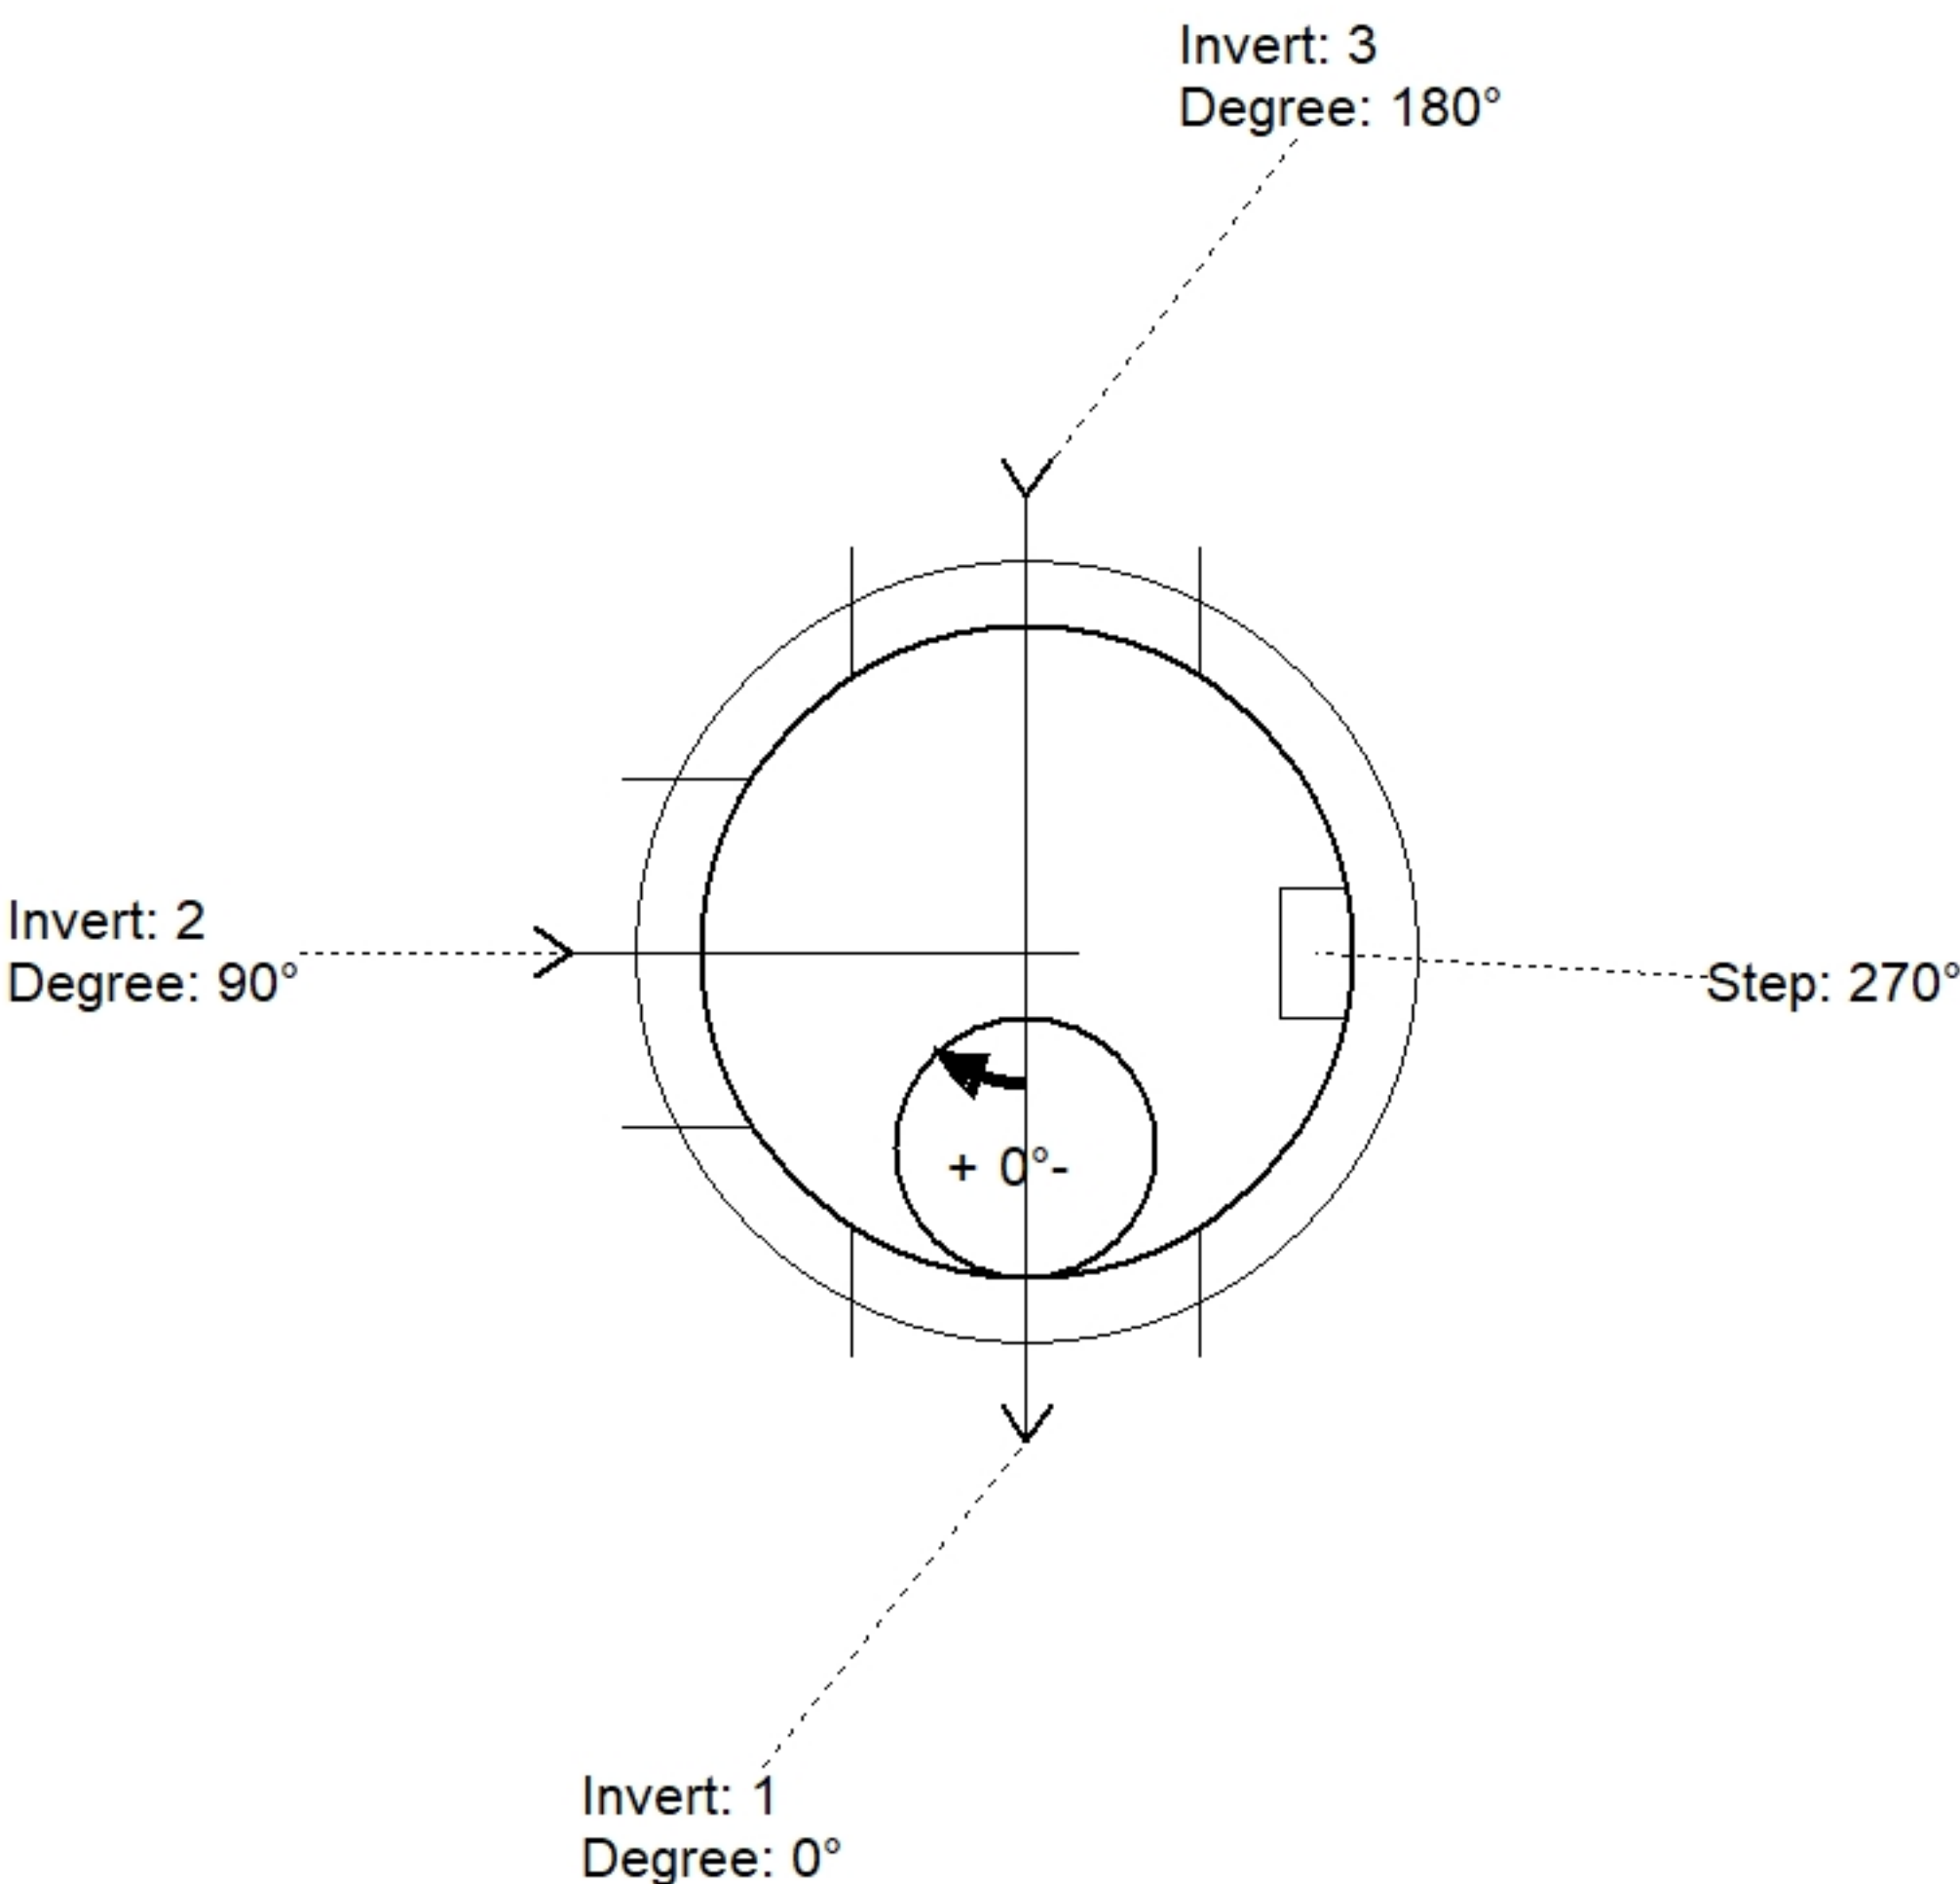

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	547.9'							
Reducer								
Invert 1	543.98'	0°	24" ADS N-12	28"	32" x 32"	DOGHOUSE 32"x32"	6"	P1
Invert 2	543.98'	90°	24" RCP B WALL	30"	32"	Hole 32	5"	P1
Invert 3	543.98'	180°	24" ADS N-12	28"	32" x 32"	DOGHOUSE 32"x32"	6"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

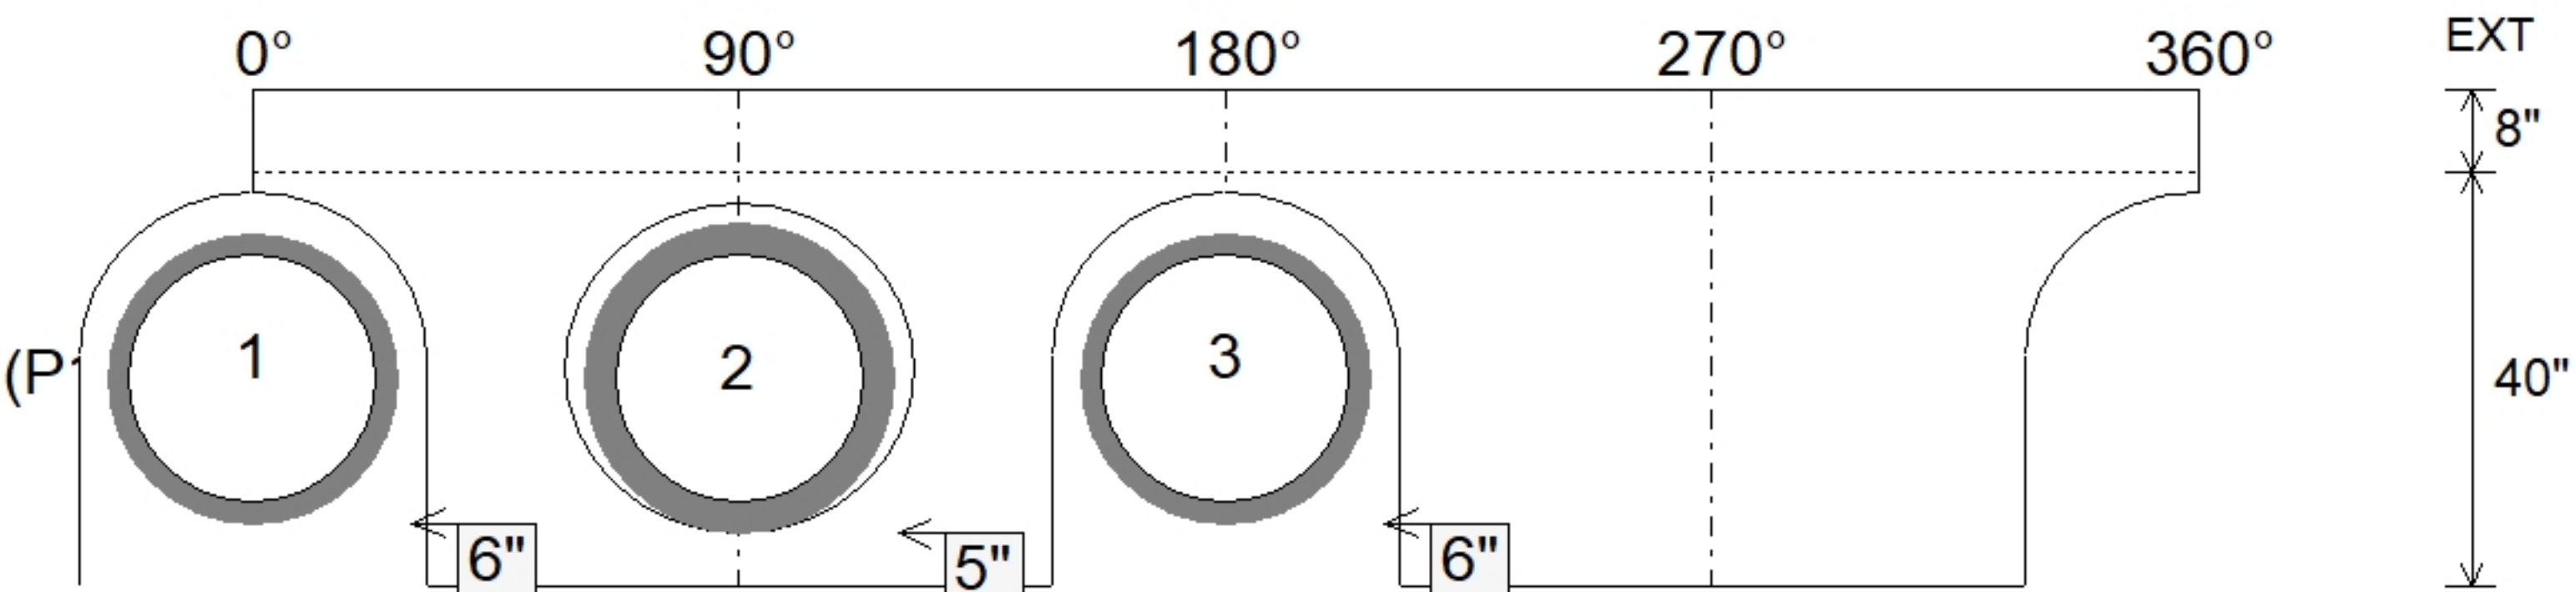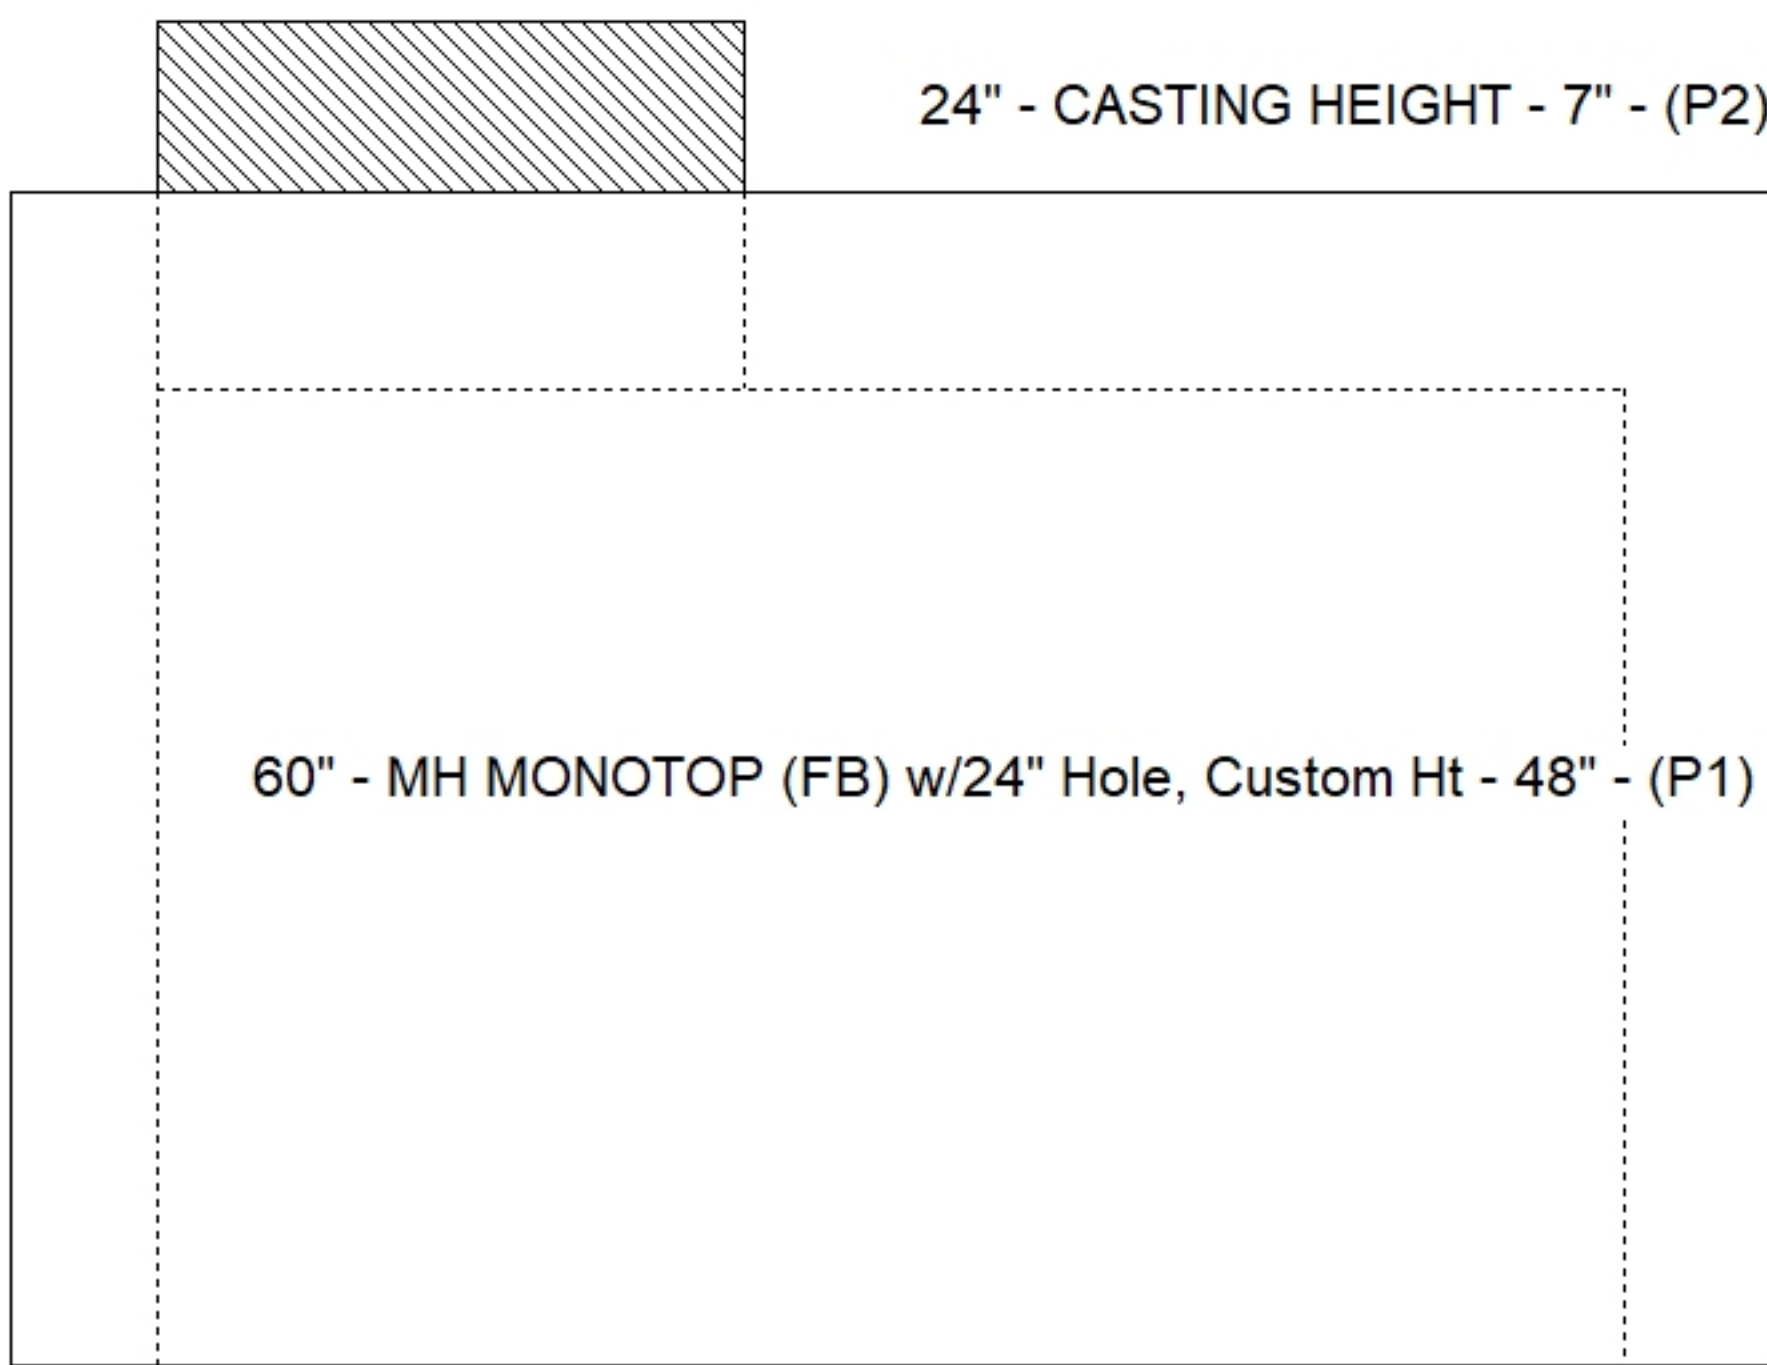

Submittal Drawing
5/4/2026 9:45:36 AM

SUBMITTAL
APPROVED BY:
