

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 5.3'


Floor Height: 8"

Slack: 3.6"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

12105 H-


Structure Total: 13195 lb

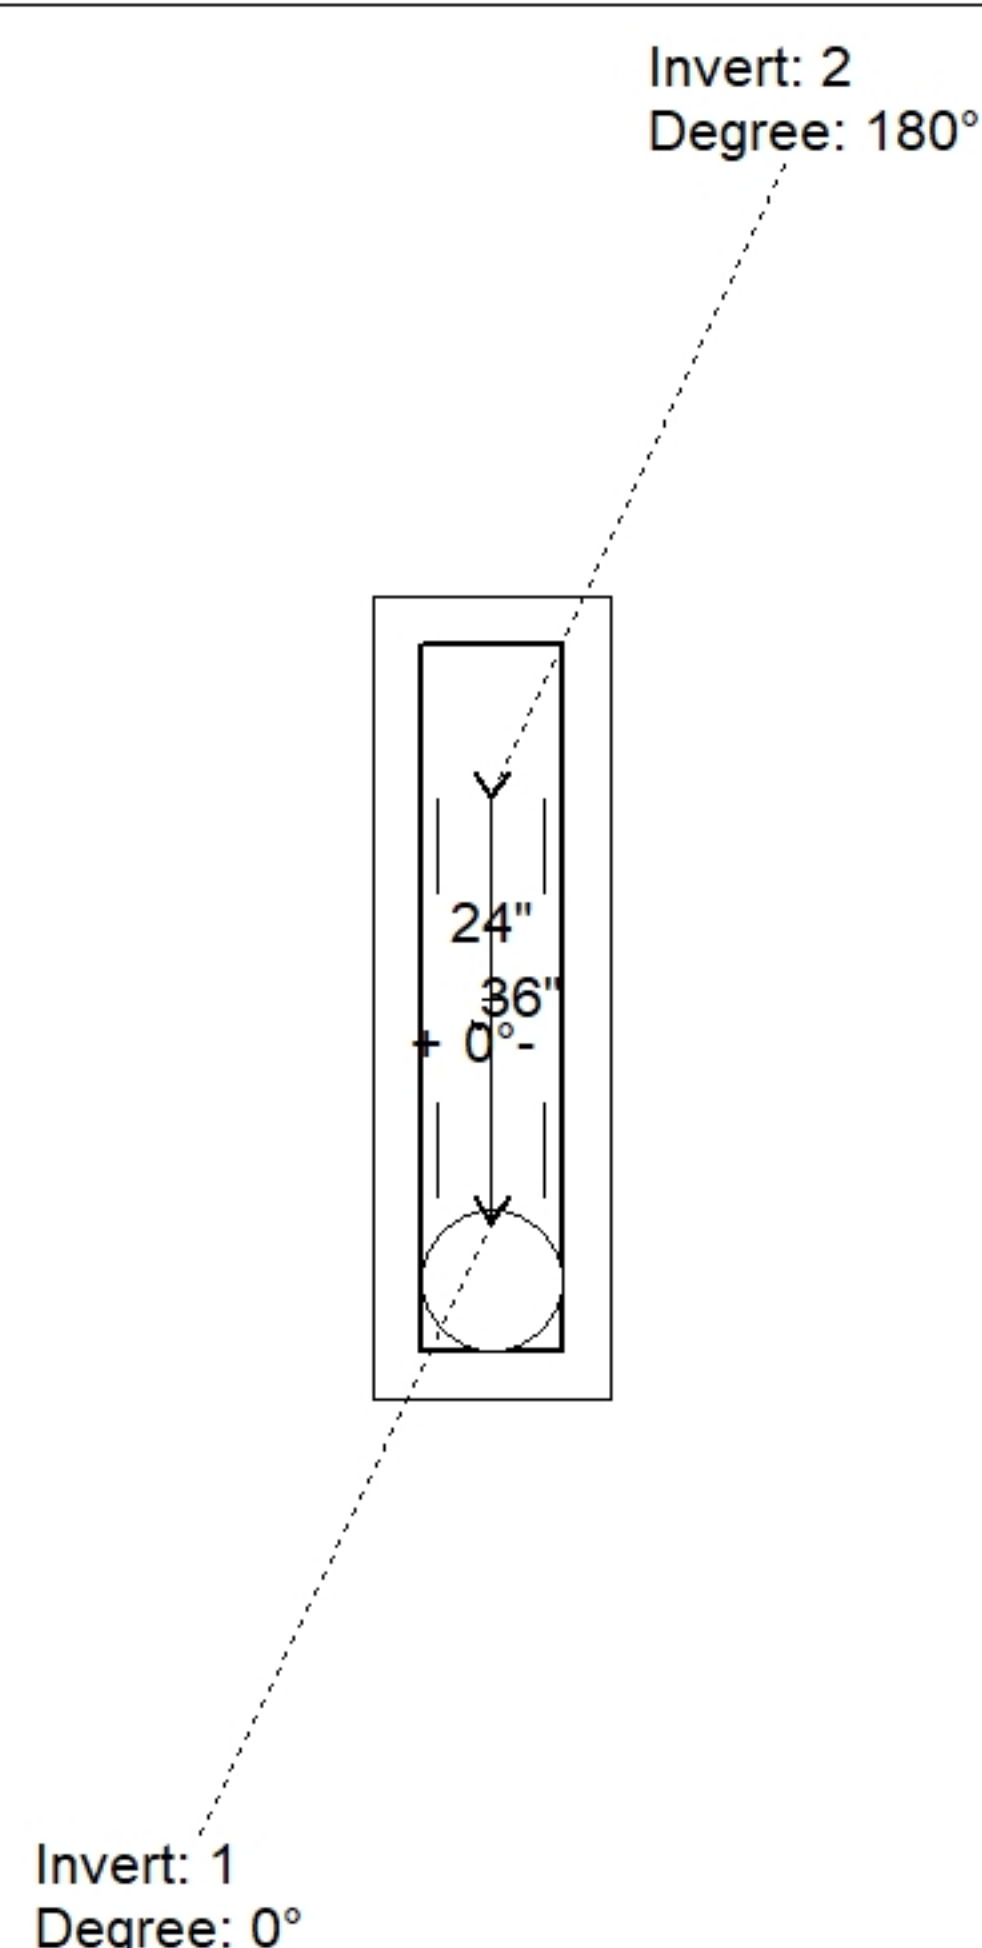

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	535.23'							
Reducer								
Invert 1	529.93'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	530.01'	180°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 32" - (P1)

Default - Interior Dimensions

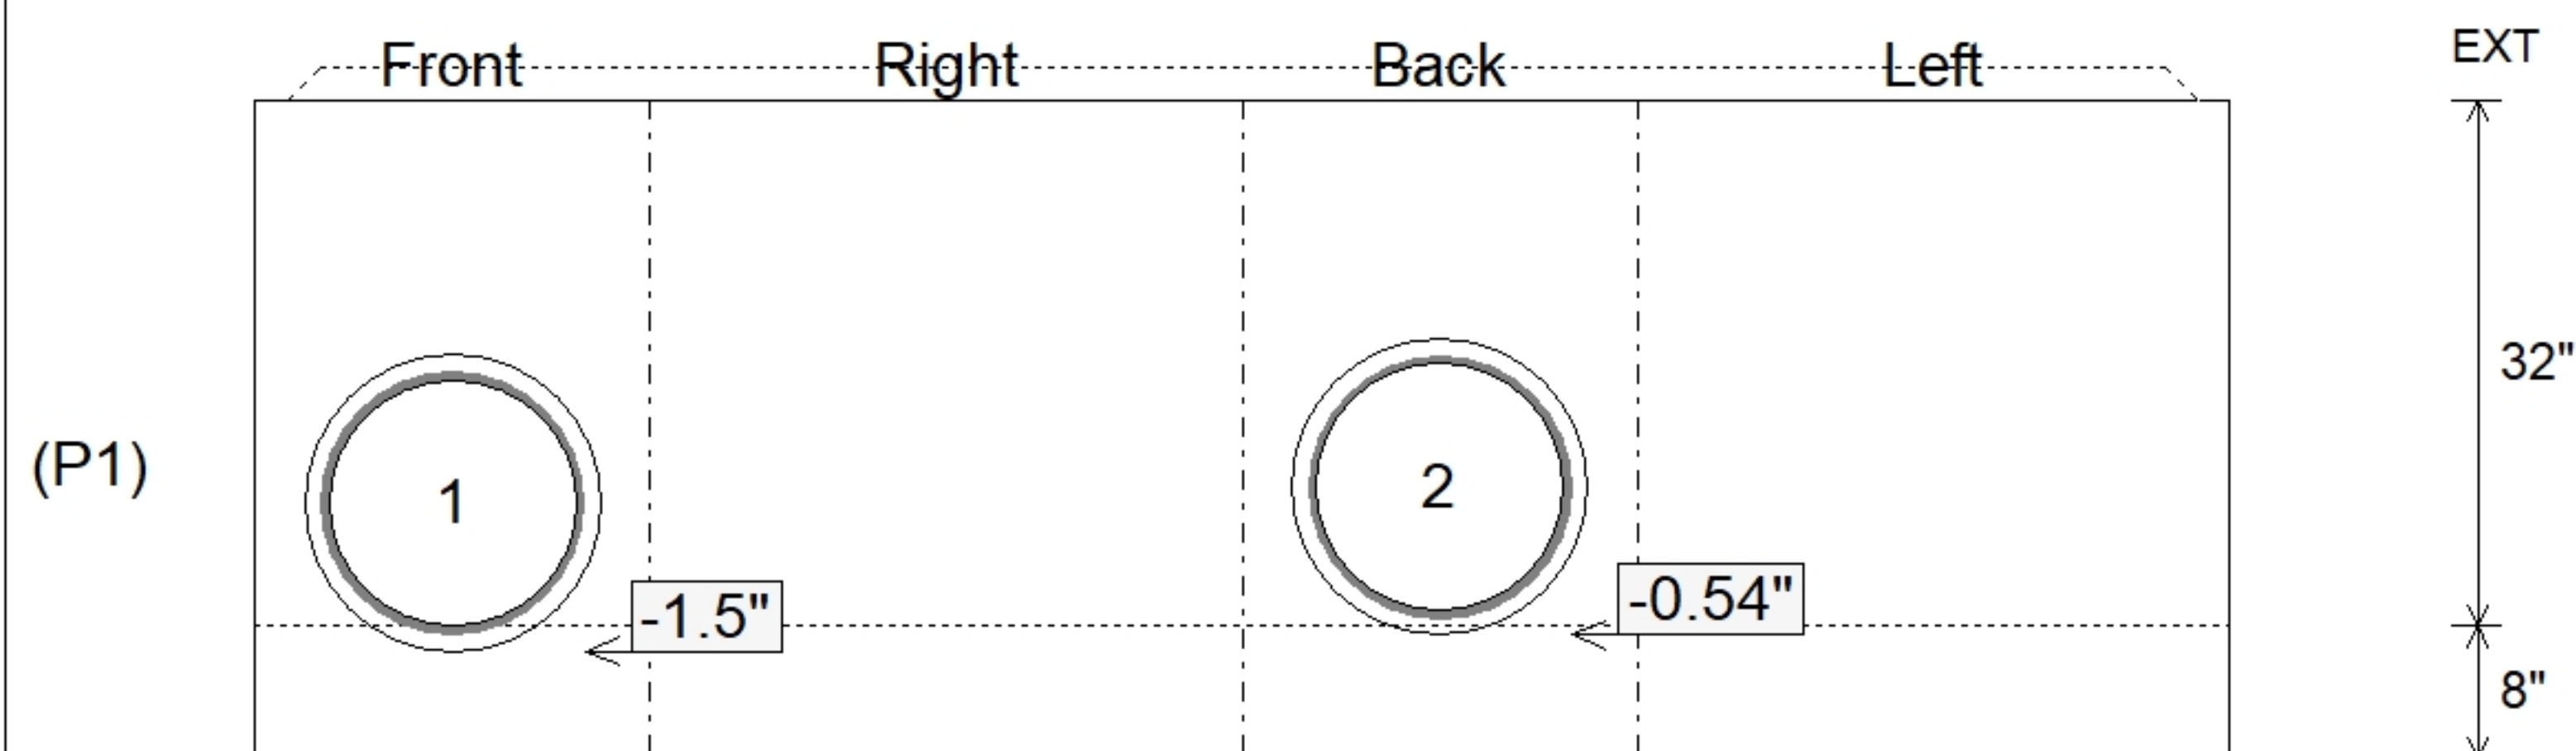

SUBMITTAL
APPROVED BY:
