

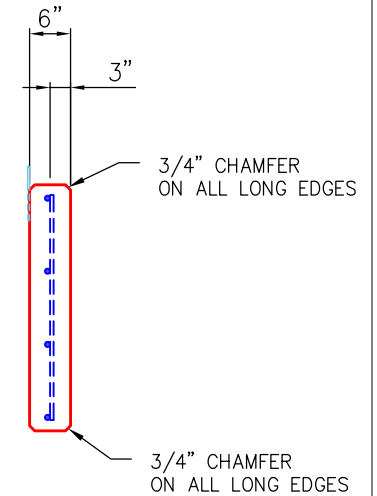
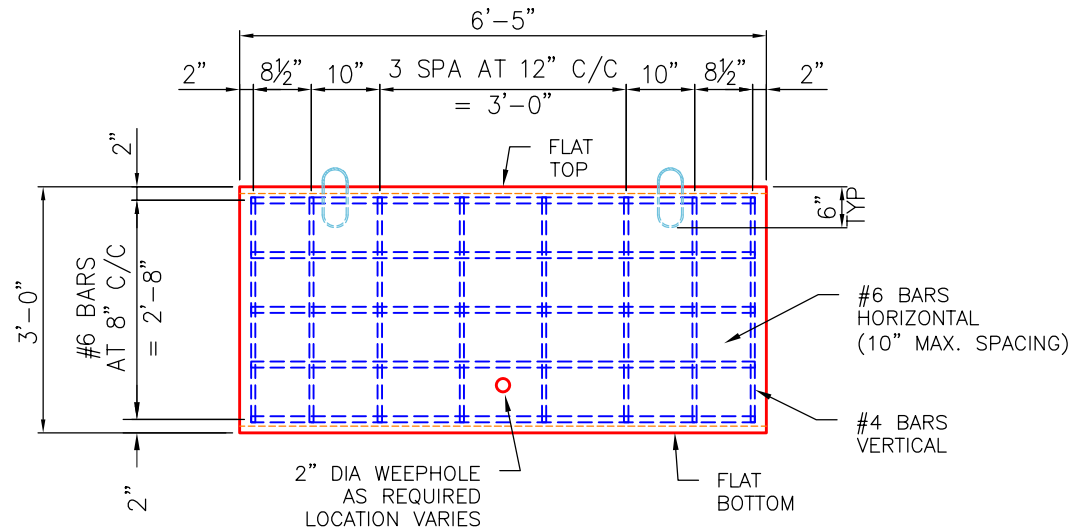


Job Name: 26-1333 - Mitchell Hill Road Project Job Location: Louisville, KY 40118 Contractor: Hall Contracting of Kentucky Inc					Plant: 100 6/16/2026 1:22:06 PM		Tech: J. Horsley PC: J. Jarvis																												
Structure ID: WALL P14-P15																																			
P1 CUSTOM WALL				WALL PANEL 6" THICK F/F																															
P4) 77" x 6" - WALL PANEL 6" THICK F/F - 2.00' HT x 6.42' LONG P3) 77" x 6" - WALL PANEL 6" THICK F/F - 2.00' HT x 6.42' LONG P2) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG P1) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG 1) Hole - 2						932 lb 932 lb 1398 lb 1398 lb ----- 0 lb Structure Total: 4659 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETER = 4,000 PSI AT 28" DAYS. 3. SMOOTH FORM FINISH ON THE FRONT SURFACE. 4. 3/4" CHAMFER ON ALL LONG EDGES. REINFORCING PER ASTM A615 (GRADE 60). -VERTICAL BARS = #4 BARS AT 12" C/C -HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)																											
Rim: 695'		Rim to Invert: 5'		Slack: 0"		Sump: 60"		Step Position:																											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset																									
Invert 1																																			
Invert 2																																			
Invert 3																																			
Invert 4																																			
Invert 5																																			
Invert 6																																			
Invert 7																																			
Invert 8																																			
RIGHT-SIDE UP VIEW (int. dimensions) (P4) (P3) (P2) (P1) <<  UPSIDE-DOWN VIEW (int. dimensions) Note: See attached typical drawing for reinforcing and lifting details. <tr><td colspan="12"> INSIDE WALL DIMENSIONS (P1) 6'-5" (77") EXT 36" </td></tr> <tr><td colspan="3">Coating (Int): Coating (Ext):</td><td colspan="2">Seam Up: Flat Seam Dn: Flat</td><td colspan="2">Wall Thickness: 0" Floor Height: 0"</td><td colspan="2">Height (Int): 36" Height (Ext): 36"</td><td colspan="3">Weight (Net): 1398 lb Volume (Net): 0.36cu.yd</td></tr>												INSIDE WALL DIMENSIONS (P1) 6'-5" (77") EXT 36"												Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: Flat		Wall Thickness: 0" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 1398 lb Volume (Net): 0.36cu.yd		
INSIDE WALL DIMENSIONS (P1) 6'-5" (77") EXT 36"																																			
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: Flat		Wall Thickness: 0" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 1398 lb Volume (Net): 0.36cu.yd																										

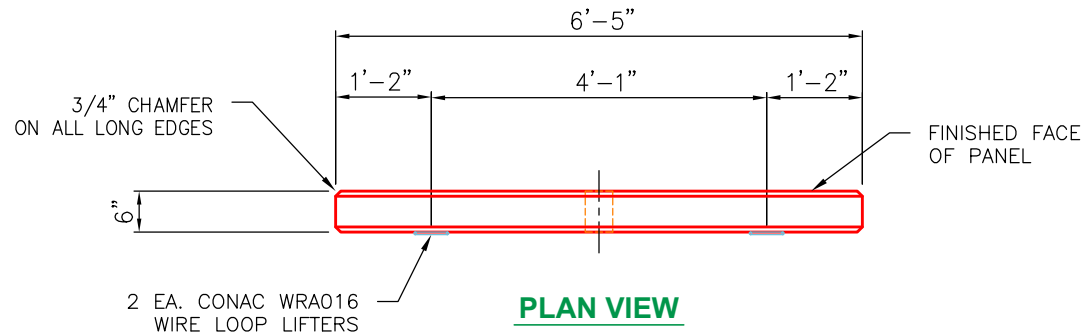

GENERAL NOTES:

1. MANUFACTURED ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI MINIMUM AT 28 DAYS.
3. REINFORCING: AS PER PLAN DESIGN (GRADE 60).
4. CONAC 5CA14 ANCHORS CAST IN FOR HANDLING.
5. WEIGHT = 1,413 LBS
6. 68 REQUIRED.

SIDE VIEW

END VIEW

REVISION INFORMATION				SUBMITTAL DESCRIPTION: WALL PANEL 6.50' LG x 6" THK.	
REV. 	DATE:	NO REVISIONS TO DATE		CUSTOMER: HALL CONTRACTING OF KY INC.	
				PROJECT: MITCHELL HILL ROAD PROJECT	
				STRUCTURE ID.: WALL PANEL 6" THK (78" LG x 36" HT)	
				SALES ORDER NO: 26-1333	
				CHECK: B. SMITH	DRAWN BY: J. HORSLEY
				DATE: 04/20/26	SCALE: NTS PG. 1 of 1
