

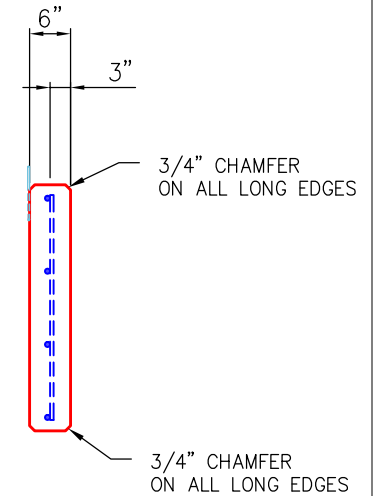
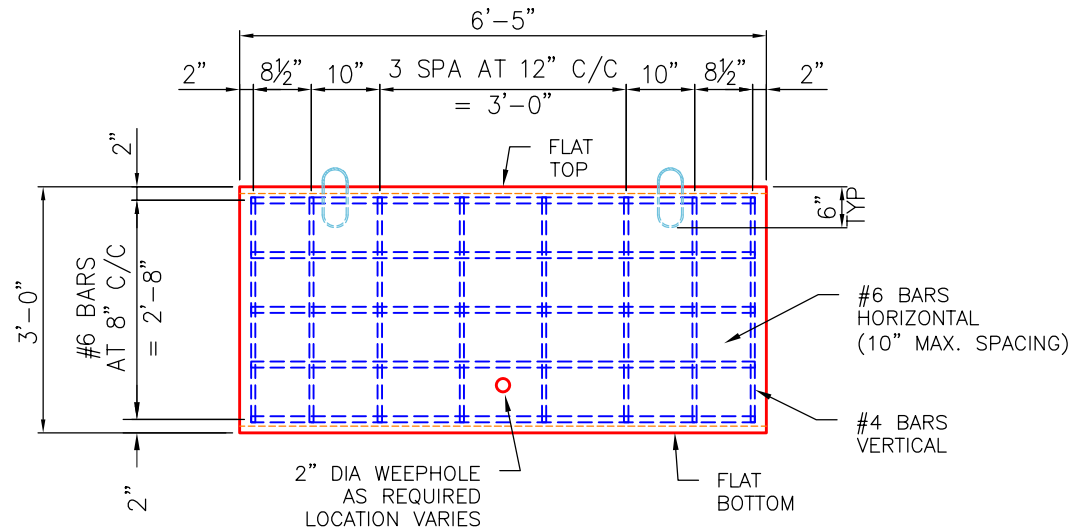


Job Name: 26-1333 - Mitchell Hill Road Project Job Location: Louisville, KY 40118 Contractor: Hall Contracting of Kentucky Inc					Plant: 100 6/16/2026 1:23:33 PM		Tech: J. Horsley PC: J. Jarvis																
Structure ID: WALL P17-P18																							
P3 CUSTOM WALL				WALL PANEL 6" THICK F/F																			
P3) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG P2) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG P1) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG 1) Hole - 2						1398 lb 1398 lb 1398 lb 0 lb ----- Structure Total: 4193 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETER = 4,000 PSI AT 28" DAYS. 3. SMOOTH FORM FINISH ON THE FRONT SURFACE. 4. 3/4" CHAMFER ON ALL LONG EDGES. REINFORCING PER ASTM A615 (GRADE 60). -VERTICAL BARS = #4 BARS AT 12" C/C -HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)															
Rim: 694' Rim to Invert: 3.5' Slack: 0" Sump: 66" Step Position:																							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset													
Invert 1																							
Invert 2																							
Invert 3																							
Invert 4																							
Invert 5																							
Invert 6																							
Invert 7																							
Invert 8																							
(P3) << (P2) (P1) RIGHT-SIDE UP VIEW (int. dimensions)  Note: See attached typical drawing for reinforcing and lifting details. INSIDE WALL DIMENSIONS 6'-5" (77") (P3)  36" <tr><td colspan="4">Coating (Int): Coating (Ext):</td><td colspan="2">Seam Up: Flat Seam Dn: Flat</td><td colspan="2">Wall Thickness: 0" Floor Height: 0"</td><td colspan="2">Height (Int): 36" Height (Ext): 36"</td><td colspan="2">Weight (Net): 1398 lb Volume (Net): 0.36cu.yd</td></tr>												Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 0" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 1398 lb Volume (Net): 0.36cu.yd	
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 0" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 1398 lb Volume (Net): 0.36cu.yd													

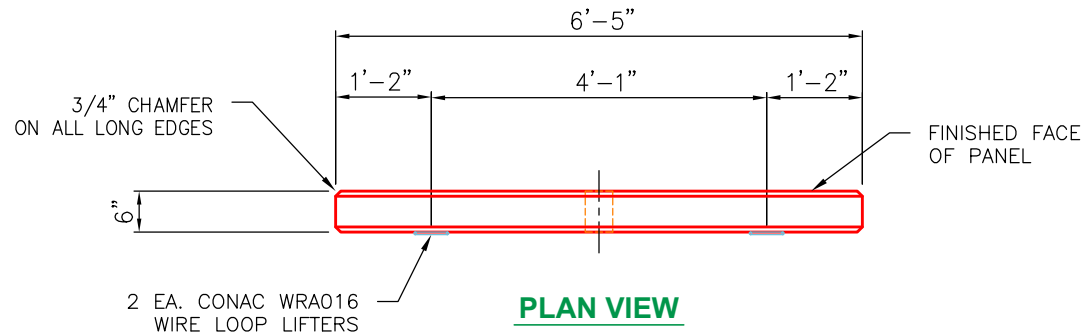

GENERAL NOTES:

1. MANUFACTURED ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI MINIMUM AT 28 DAYS.
3. REINFORCING: AS PER PLAN DESIGN (GRADE 60).
4. CONAC 5CA14 ANCHORS CAST IN FOR HANDLING.
5. WEIGHT = 1,413 LBS
6. 68 REQUIRED.

SIDE VIEW

END VIEW

REVISION INFORMATION				SUBMITTAL DESCRIPTION: WALL PANEL 6.50' LG x 6" THK.	
REV. 	DATE:	NO REVISIONS TO DATE		CUSTOMER: HALL CONTRACTING OF KY INC.	
				PROJECT: MITCHELL HILL ROAD PROJECT	
				STRUCTURE ID.: WALL PANEL 6" THK (78" LG x 36" HT)	
				SALES ORDER NO: 26-1333	
				CHECK: B. SMITH	DRAWN BY: J. HORSLEY
				DATE: 04/20/26	SCALE: NTS PG. 1 of 1
