

Job Name: 26-1333 - Mitchell Hill Road Project

Job Location: Louisville, KY 40118

Contractor: Hall Contracting of Kentucky Inc

Plant: 100

6/16/2026 1:23:37 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: WALL P24-P25

P2 CUSTOM WALL

WALL PANEL 6" THICK F/F

P2) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG

P1) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG

1) Hole - 2

1398 lb

1398 lb

0 lb

Structure Total: 2795 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28" DAYS.

3. SMOOTH FORM FINISH ON THE FRONT SURFACE.


4. 3/4" CHAMFER ON ALL LONG EDGES.




REINFORCING PER ASTM A615 (GRADE 60).

-VERTICAL BARS = #4 BARS AT 12" C/C

-HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)

|           |      |                   |           |              |         |           |      |                |        |        |
|-----------|------|-------------------|-----------|--------------|---------|-----------|------|----------------|--------|--------|
| Rim: 690' |      | Rim to Invert: 1' |           | Slack: 0"    |         | Sump: 60" |      | Step Position: |        |        |
| Position  | Elev | Angle             | Ext. (cw) | Pipe         | Pipe OD | Connector | Hole | Horz Size      | Up ( ) | Offset |
| Invert 1  | 689' | 0°                | 38.5"     | 2" WEEP HOLE | 2"      | Hole 2    | 2"   | 2"             | 24"    | 0"     |
| Invert 2  |      |                   |           |              |         |           |      |                |        |        |
| Invert 3  |      |                   |           |              |         |           |      |                |        |        |
| Invert 4  |      |                   |           |              |         |           |      |                |        |        |
| Invert 5  |      |                   |           |              |         |           |      |                |        |        |
| Invert 6  |      |                   |           |              |         |           |      |                |        |        |
| Invert 7  |      |                   |           |              |         |           |      |                |        |        |
| Invert 8  |      |                   |           |              |         |           |      |                |        |        |

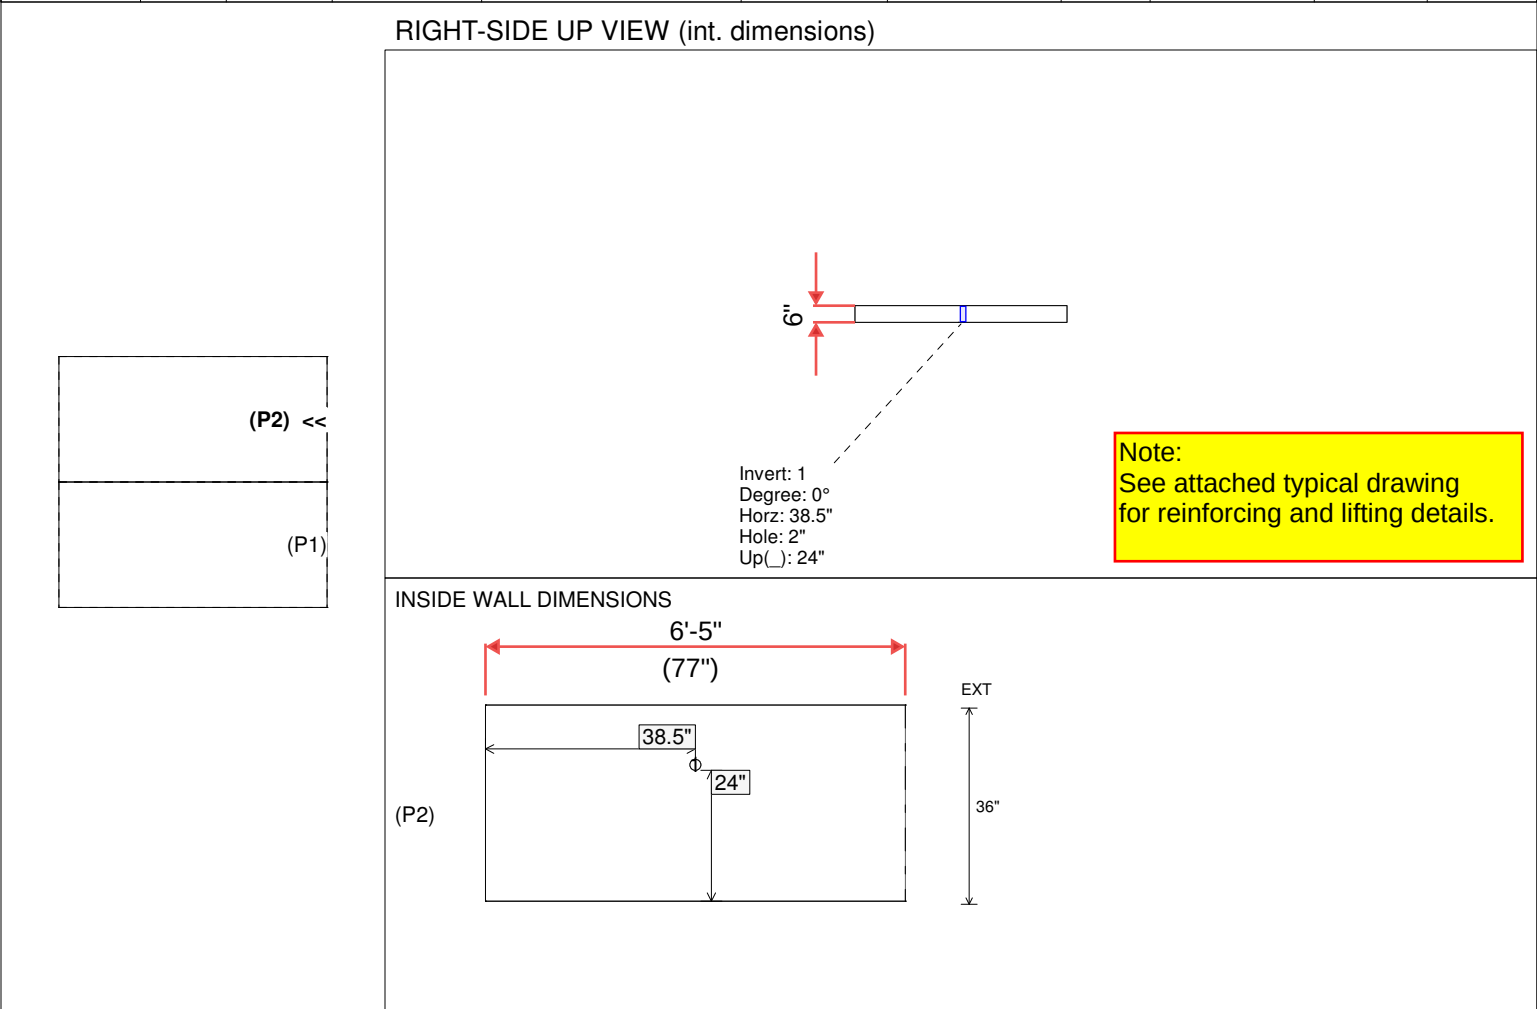

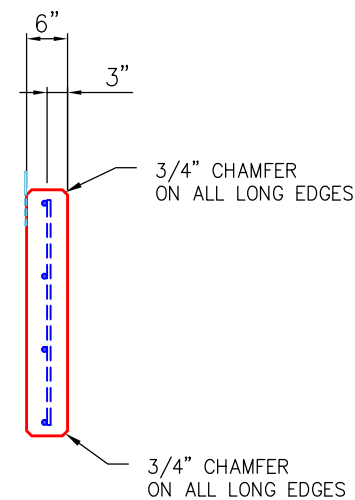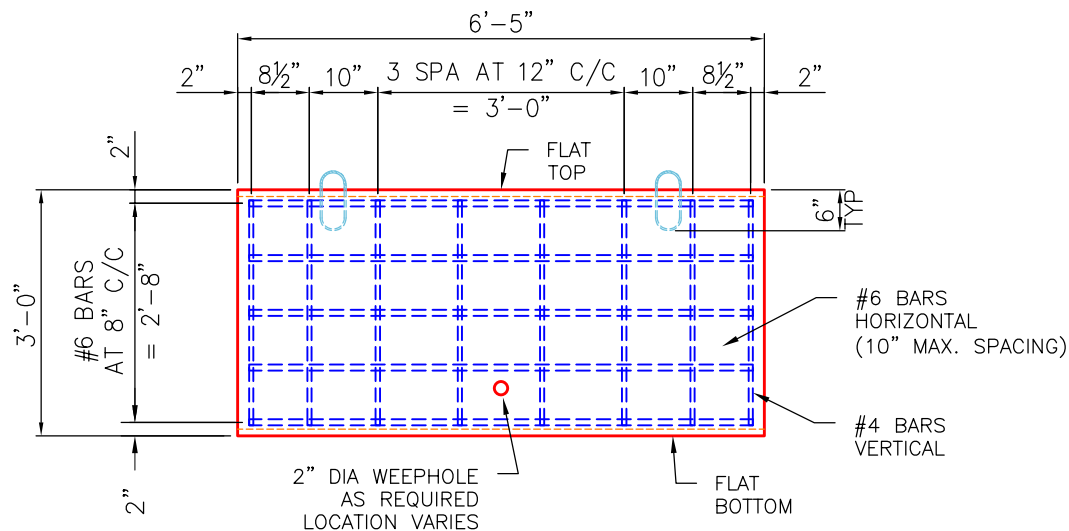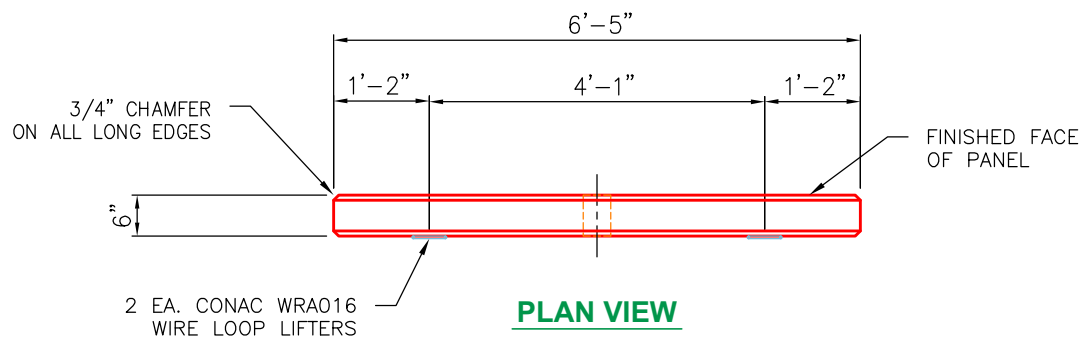

**GENERAL NOTES:**

1. MANUFACTURED ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI MINIMUM AT 28 DAYS.
3. REINFORCING: AS PER PLAN DESIGN (GRADE 60).
4. CONAC 5CA14 ANCHORS CAST IN FOR HANDLING.
5. WEIGHT = 1,413 LBS
6. 68 REQUIRED.

| REVISION INFORMATION                                                                           |                      |
|------------------------------------------------------------------------------------------------|----------------------|
| REV.  DATE: | NO REVISIONS TO DATE |
|                                                                                                |                      |
|                                                                                                |                      |
|                                                                                                |                      |
|                                                                                                |                      |
|                                                                                                |                      |



SUBMITTAL DESCRIPTION: WALL PANEL 6.50' LG x 6" THK.

CUSTOMER: HALL CONTRACTING OF KY INC.

PROJECT: MITCHELL HILL ROAD PROJECT

STRUCTURE ID.: WALL PANEL 6" THK (78" LG x 36" HT)

SALES ORDER NO: 26-1333

CHECK: B. SMITH

DRAWN BY: J. HORSLEY

DATE: 04/20/26

SCALE: NTS

PG. 1 of 1
