

Job Name: 26-1355 Sinking Creek Rd Sanitary Sewer Ext. Ph. 2 Job Location: London, KY Contractor: Endesol, Inc.	Plant: Beaver Dam 6/2/2026 2:57:49 PM	Tech: S. Felletter PC: E. Bradley	
Structure ID: B-3-8 SS-MH			
P1 MH048BA36CDARED		MH BASE w/ConBlock-CDA Red T/n	

- P3) 24" - CASTING HEIGHT - 7"
 P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42"
 P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36"
 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT
 1) CASTING - HOE MC-350 F/C Sanitary
 1) 48" - Conseal CS-102 1.00" (Double)
 1) 24" - Conseal CS-102 1.00" (Double)
 2) PSX - 12-08 NYLO
 7) MH Step ML-10-TDS-NCR - 10"

- 0 lb
 3116 lb
 3749 lb
 0 lb
 0 lb
 1440 lb
 305 lb
 0 lb
 0 lb
 16 lb
 0 lb




 Structure Total: 8627 lb
- Structure Notes:**
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. ADMIXTURE = CONBLOCK CDA RED.
 4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY").
 .
 REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 1220' Rim to Invert: 7.1' Slack: 2.2" Sump: 2" Step Position: 0°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1212.9'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	1213'	243°	122.993"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

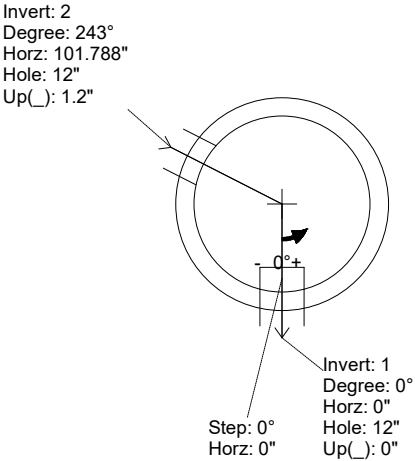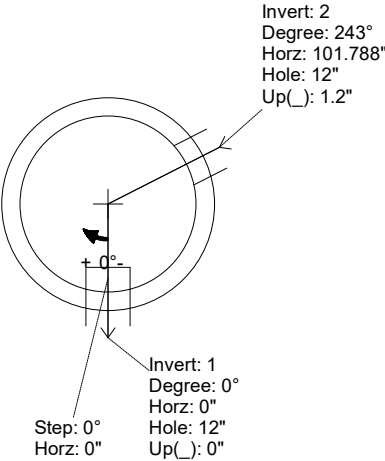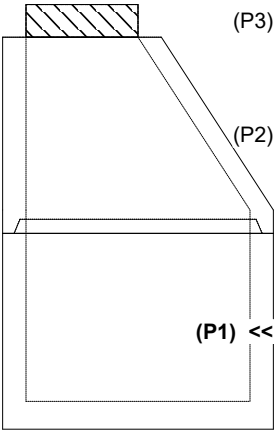

INSIDE WALL DIMENSIONS

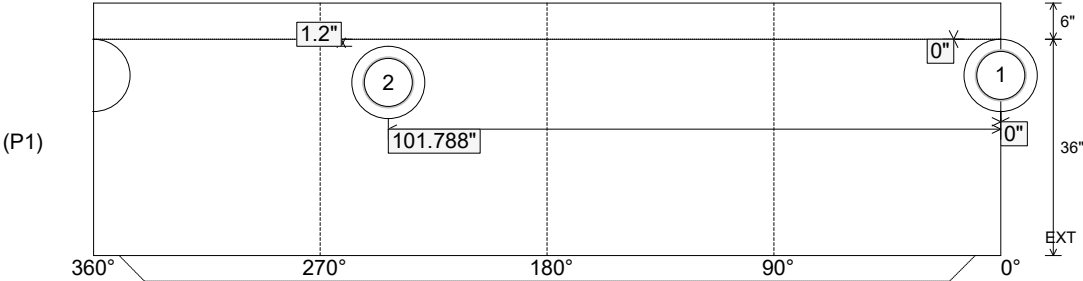

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3749 lb Volume (Net): 0.96cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-1355 Sinking Creek Rd Sanitary Sewer Ext. Ph. 2

Job Location: London, KY

Contractor: Endesol, Inc.

Plant: Beaver Dam

6/2/2026 2:57:49 PM

Tech: S. Felletter

PC: E. Bradley



Structure ID: B-3-8 SS-MH

P1 MH048BA36CDARED

MH BASE w/ConBlock-CDA Red T/n

P3) 24" - CASTING HEIGHT - 7"

P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42"

P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT

1) CASTING - HOE MC-350 F/C Sanitary

1) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 12-08 NYLO

7) MH Step ML-10-TDS-NCR - 10"

0 lb

3116 lb

3749 lb

0 lb

0 lb

1440 lb

305 lb

0 lb

0 lb

16 lb

0 lb

Structure Total: 8627 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. ADMIXTURE = CONBLOCK CDA RED.

4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY").

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 1220'

Rim to Invert: 7.1'

Slack: 2.2"


Sump: 2"

Step Position: 0°

Invert channel drawing

Full height invert

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1212.9'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	1213'	243°	122.993"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

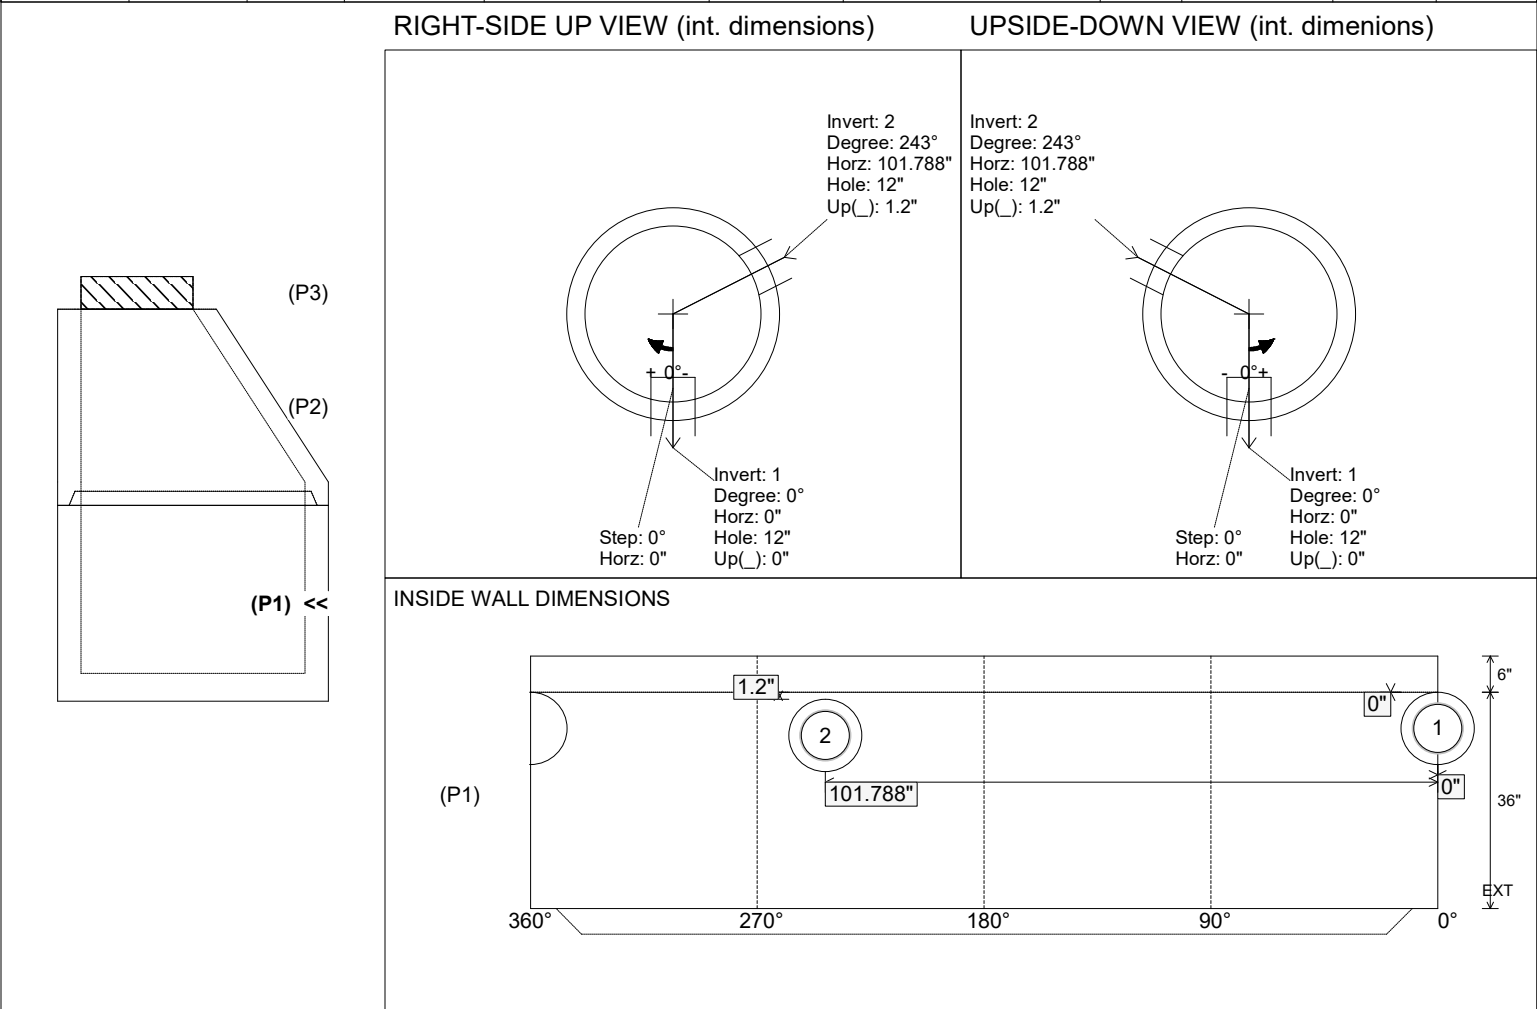

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3749 lb Volume (Net): 0.96cu.yd
----------------------------------	---------------------------------	--	--	--
