

Job Name: 26-1355 Sinking Creek Rd Sanitary Sewer Ext. Ph. 2
Job Location: London, KY
Contractor: Endesol, Inc.

Plant: Beaver Dam
6/2/2026 2:58:23 PM

Tech: S. Felletter
PC: E. Bradley



Structure ID: B-4-7 SS-MH

P3 MH048CN30CDARED

ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G

- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT
1) CASTING - HOE MC-350 F/C Sanitary
2) 48" - Con seal CS-102 1.00" (Double)
1) 24" - Con seal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
8) MH Step ML-10-TDS-NCR - 10"


0 lb
1961 lb
2515 lb
3330 lb
0 lb
0 lb
1440 lb
305 lb
0 lb
0 lb
16 lb
0 lb

Structure Total: 9568 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY").

REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

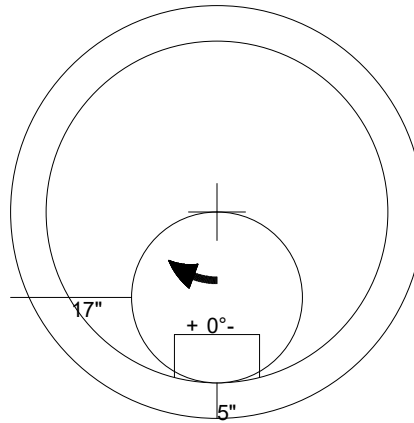

48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" - (P3)



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 30"

Weight (Net): 1961 lb
Volume (Net): 0.5cu.yd
