




Job Name: 26-1355 Sinking Creek Rd Sanitary Sewer Ext. Ph. 2					Plant: Beaver Dam		Tech: S. Felletter			
Job Location: London, KY					6/2/2026 2:57:48 PM		PC: E. Bradley			
Contractor: Endesol, Inc.										
Structure ID: B-6-5 SS-MH										
P1 MH048BA36CDARED					MH BASE w/ConBlock-CDA Red T/n					
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - HOE MC-350 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 12) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 4192 lb 3749 lb 0 lb 0 lb 1440 lb 305 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 12818 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1241' Rim to Invert: 12.1' Slack: 2.2' Sump: 2' Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1228.9'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	1229'	180°	91.106"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)

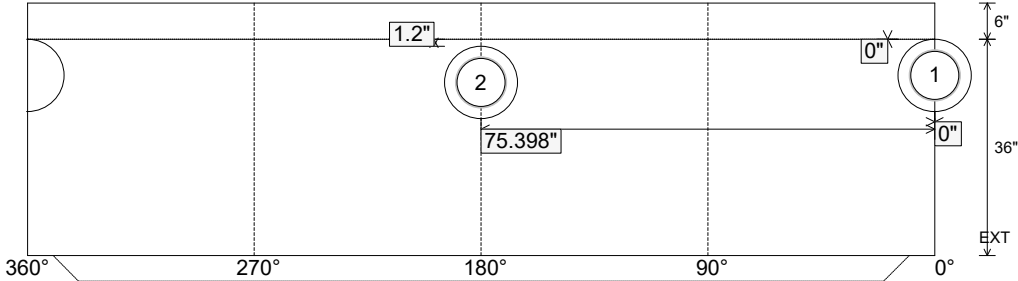

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3749 lb Volume (Net): 0.96cu.yd
----------------------------------	---------------------------------	--	--	--

Plant: Beaver Dam

6/2/2026 2:57:48 PM

P1 MH048BA36CDARED

MH BASE w/ConBlock-CDA Red T/n

0 lb
3116 lb
4192 lb
3749 lb
0 lb
0 lb
1440 lb
305 lb
0 lb
0 lb
16 lb
0 lb

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY").

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 12818 lb

Invert channel drawing




Full height invert

Rim: 1241' Rim to Invert: 12.1' Slack: 2.2" Sump: 2" Step Position: 0°


[illegible]

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

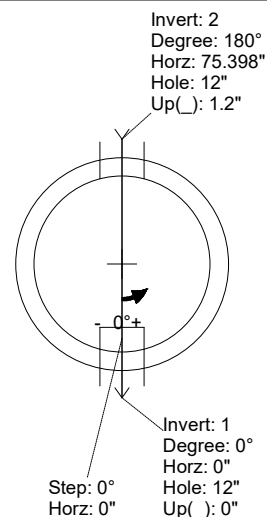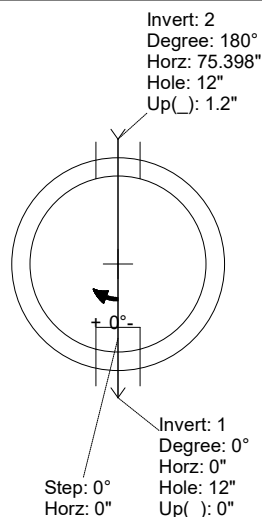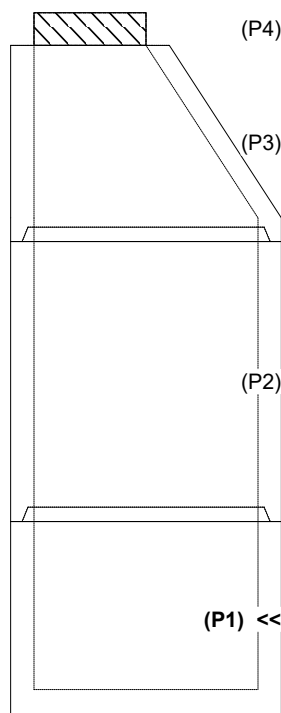

INSIDE WALL DIMENSIONS

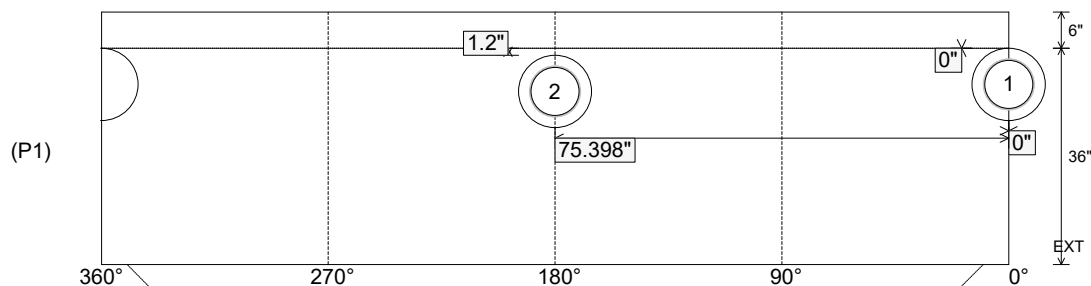

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 36"
Height (Ext): 42"

Weight (Net): 3749 lb
Volume (Net): 0.96cu.yd
