

Job Name: 26-1355 Sinking Creek Rd Sanitary Sewer Ext. Ph. 2
Job Location: London, KY
Contractor: Endesol, Inc.

Plant: Beaver Dam
6/2/2026 2:58:21 PM

Tech: S. Felletter
PC: E. Bradley



Structure ID: B-8-3 SS-MH

P4 GR3CDARED

GRADE RING w/ConBlock-CDA Red F/F

- P5) 24" - CASTING HEIGHT - 7"
P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) SPECIAL EXTERNAL COATING - GRADE RING
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT
1) CASTING - HOE MC-350 F/C Sanitary
2) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
7) MH Step ML-10-TDS-NCR - 10"

0 lb
202 lb
1961 lb
1677 lb
3330 lb
0 lb
0 lb
0 lb
1440 lb
305 lb
0 lb
0 lb
16 lb
0 lb


Structure Total: 8932 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. ADMIXTURE = CONBLOCK CDA RED.
 4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY").
 5. EXTERNAL BITUMINOUS COATING REQUIRED FOR GRADE RING.
- REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS
-CONCRETE: 4,000 PSI @ 28 DAYS
-REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
2. WEIGHT: 3" 202 LBS.
3. ADMIXTURE: CONBLOCK-CDA RED

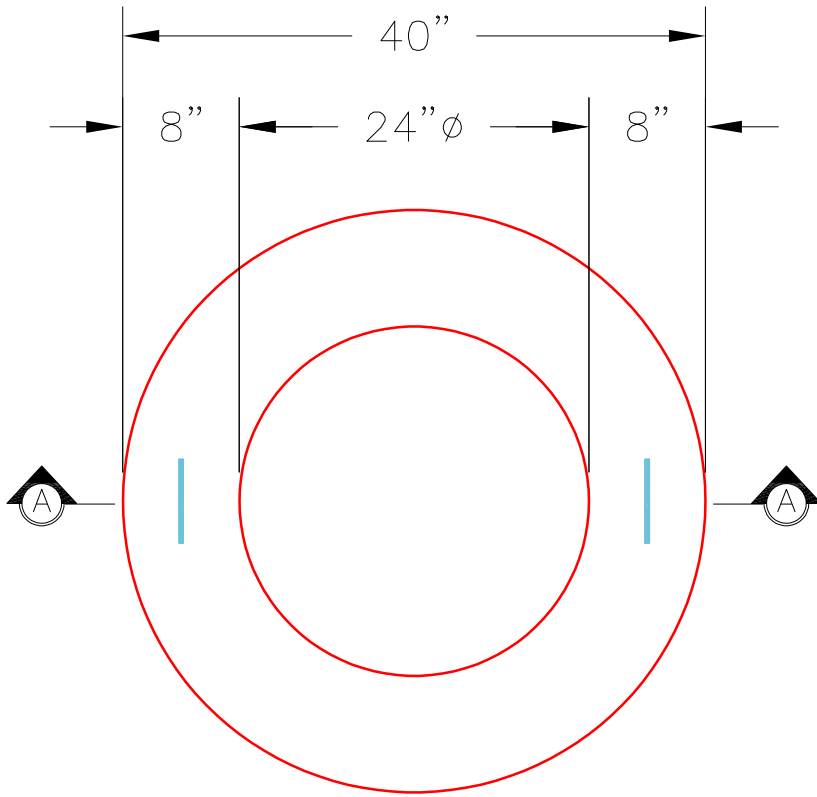

PLAN VIEW

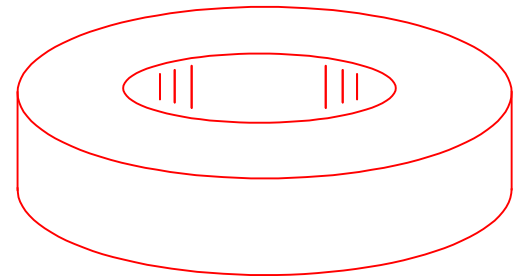

ISOMETRIC VIEW

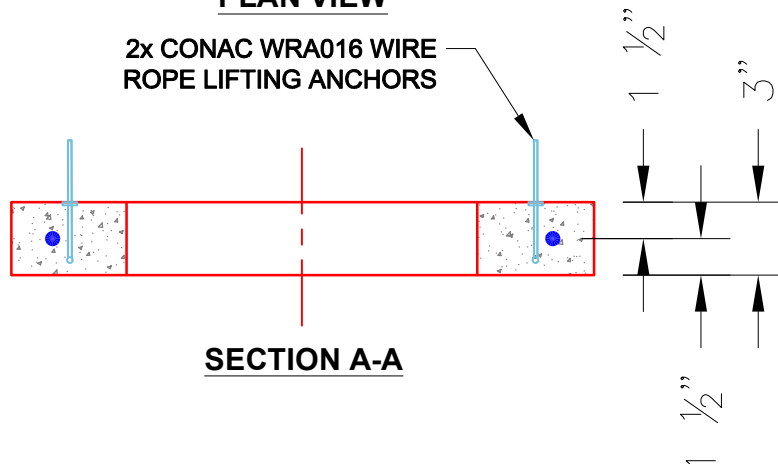

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
