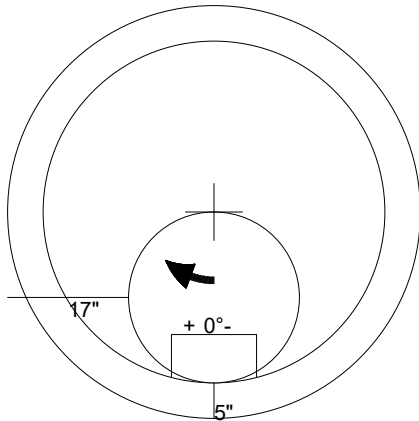



Job Name: 26-1355 Sinking Creek Rd Sanitary Sewer Ext. Ph. 2		Plant: Beaver Dam	Tech: S. Felletter	
Job Location: London, KY Contractor: Endesol, Inc.		6/2/2026 2:58:20 PM	PC: E. Bradley	
Structure ID: B-9-2 SS-MH				
P3 MH048CN36CDARED		ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 48" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - HOE MC-350 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO 9) MH Step ML-10-TDS-NCR - 10"		0 lb 2251 lb 3353 lb 3357 lb 0 lb 0 lb 1440 lb 305 lb 0 lb 0 lb 8 lb 6 lb 0 lb Structure Total: 10721 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (HOE MC-350 F/C "SANITARY"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" - (P3) 				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
