

Job Name: 26-1364 - Ollie Car Wash
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

7/17/2026 6:38:25 PM

Tech: Jared - F

PC: A. Chambers



Structure ID: 2000-GT-TANK-1

P2 BX072144-08LD06S

CB FLAT TOP 6"W w/(2) 24" HOLES F/F

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING F/F - 3"
P2) 60" x 126" - CB FLAT TOP 6"W w/(2) 24" HOLES F/F - 8"
P1) 60" x 126" - BOX BASE 6inW, 6inF, Variable Ht F/n - 72"
1) CASTING - HOE MC-315 F/C Storm
2) 24" - Conseal CS-102 1.00"
1) Hole - 10
1) Hole - 5

0 lb
202 lb
6064 lb
19308 lb
258 lb
0 lb
0 lb
0 lb

25833 lb


Structure Total:

Structure Notes:


1. PER ASTM C-890-13 SPECIFICATIONS.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. THIRD POUR REQ'D - BAFFLE WALL.
4. CASTING BY ICAST (HOE MC-315 F/C "STORM")

REINFORCING PER ASTM A615 (GRADE 60)
FOR H-20 DESIGN LOADING.

- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .47) #4 BARS AT 12" C.C.E.W.

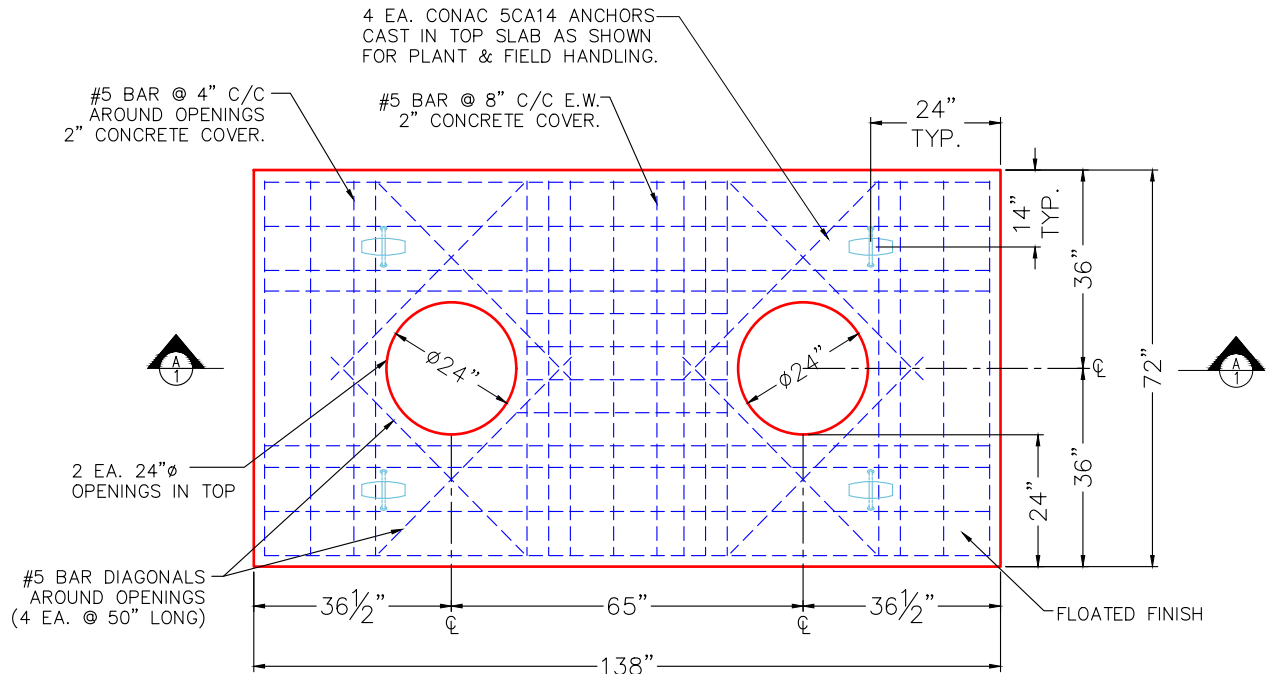

PLAN VIEW

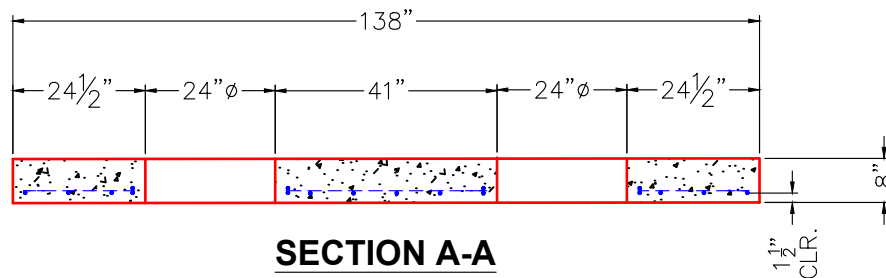

SECTION A-A

NOTES:

1. PER ASTM C-890-13 LATEST REVISION.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 8" C/C E.W. (GRADE 60).
(H-20 TRAFFIC RATED DESIGN)
4. SEALED WITH 1" CS-102 BUTYL SEALANT
5. TOP SLAB WEIGHT = 6,063 LBS.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 6064 lb
Volume (Net): 1.55cu.yd
