

Job Name: 26-1364 - Ollie Car Wash
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

7/21/2026 11:28:42 AM

Tech: Jared - F
PC: A. Chambers



Structure ID: 2000-GT-TANK-1

P3 GR3

GRADE RING

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING - 3"
P2) 60" x 126" - CB FLAT TOP 6"W w/(2) 24" HOLES - 8"
P1) 60" x 126" - BOX BASE 6inW, 6inF, Variable Ht - 72"
1) 72" x 62" - BAFFLE WALL (GT-2000 GAL.) - 4"
1) SECONDARY POUR - WALLS
1) CASTING - HOE MC-315 F/C Storm
2) 24" - Conseal CS-102 1.00"
1) Hole - 10
1) Hole - 5

Structure Total:

0 lb
202 lb
6064 lb
19308 lb
1418 lb
0 lb
258 lb
0 lb
0 lb
0 lb

27251 lb

Structure Notes:


1. PER ASTM C-890-13 SPECIFICATIONS.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. SECONDARY POUR REQ'D - BAFFLE WALL.
4. CASTING BY ICAST (HOE MC-315 F/C "STORM")

REINFORCING PER ASTM A615 (GRADE 60)
FOR H-20 DESIGN LOADING.


- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .47) #4 BARS AT 12" C.C.E.W.

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)

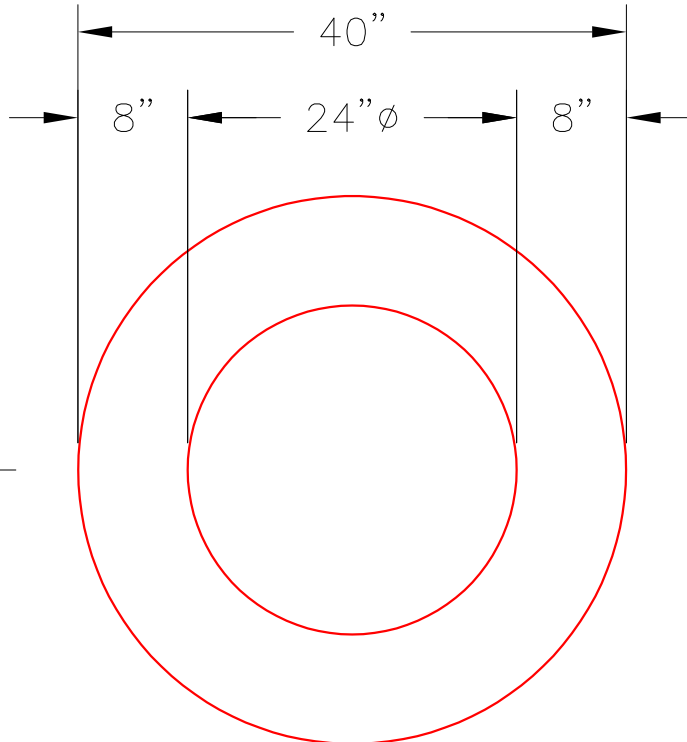

PLAN VIEW



SECTION A-A

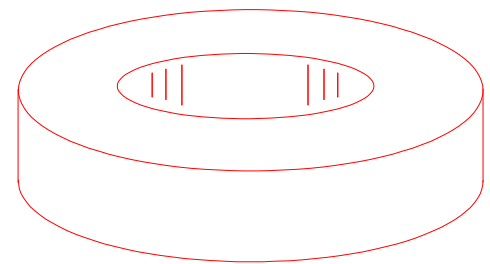

ISOMETRIC VIEW

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
