

Job Name: 26-1415 - Perdue Foods Manhole
Job Location: Cromwell, KY
Contractor: Industrial Service Company

PC: J. Jarvis
 TECH: J. Horsley
 Plant: 100



Structure ID: 1 SS-MHDH

Spec: Sanitary
 Type: SAN.MH (OPEN BTM)
 Size: 60"

Rim: 462.75'
 Invert: 462.75'
 Rim to Invert: 0'

Sump: 116.16"
 Floor (Top): 453.07'
 Floor Height: 0"


Floor (Bot): 453.07'
 Overall Height: 9.667'
 Slack: 0.16"

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING/GRATE BY OTHERS.
 4. CONFTRACTOR TO FIELD CORE HOLES IN RISER.
- REINFORCING PER ASTM A615 (GRADE 60).
 - RISER/WALLS (As .18)


STRUCTURE SUMMARY:

| | |
|-----------------------------------------------|-----------------|
| P3) 60" - CASTING HEIGHT - 0" | 0 lb |
| P2) 60" - MH RISER SPECIAL F/G - 60" | 6264 lb |
| P1) 60" - MH DH RISER Custom Ht T/F - 56" | 5846 lb |
| 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 | 0 lb |
| 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) | 0 lb |
| 2) 60" - Conseal CS-102 1.00" (Double) | 0 lb |
| 10) MH Step ML-10-TDS-NCR - 10" | 0 lb |
| Structure Total: | 12110 lb |




| Position | Elev | Angle | Pipe | Pipe OD | Hole | Connector | Up () | Ref |
|----------|---------|-------|------|---------|------|-----------|--------|-----|
| Rim | 462.75' | | | | | | | |
| Reducer | | | | | | | | |
| Invert 1 | | | | | | | | |
| Invert 2 | | | | | | | | |
| Invert 3 | | | | | | | | |
| Invert 4 | | | | | | | | |
| Invert 5 | | | | | | | | |
| Invert 6 | | | | | | | | |
| Invert 7 | | | | | | | | |
| Invert 8 | | | | | | | | |

Cast (Int. Dim.) - Interior Dimensions

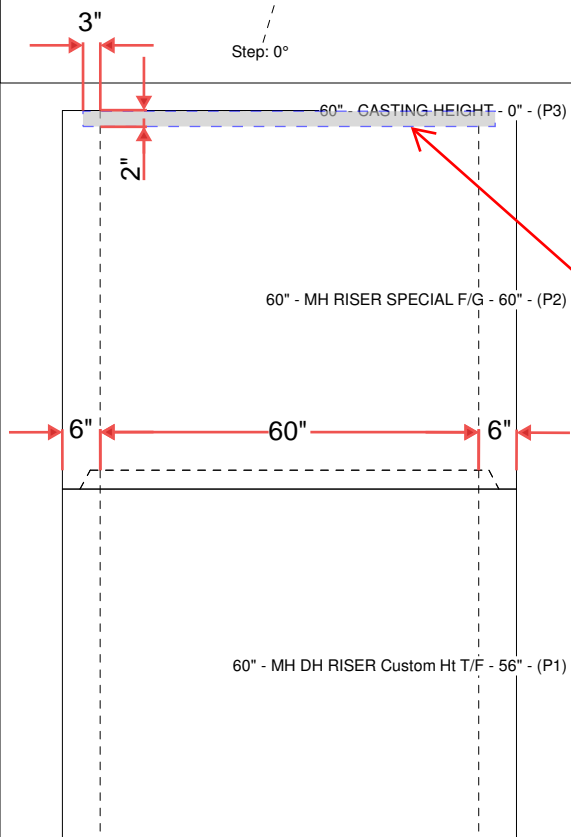

**3" WD x 2" DEEP RECESS
 IN TOP OF RISER
 FOR FIBERGLASS GRATE**



Submittal Drawing
 2/23/2026 2:22:58 PM

SUBMITTAL
 APPROVED BY:
