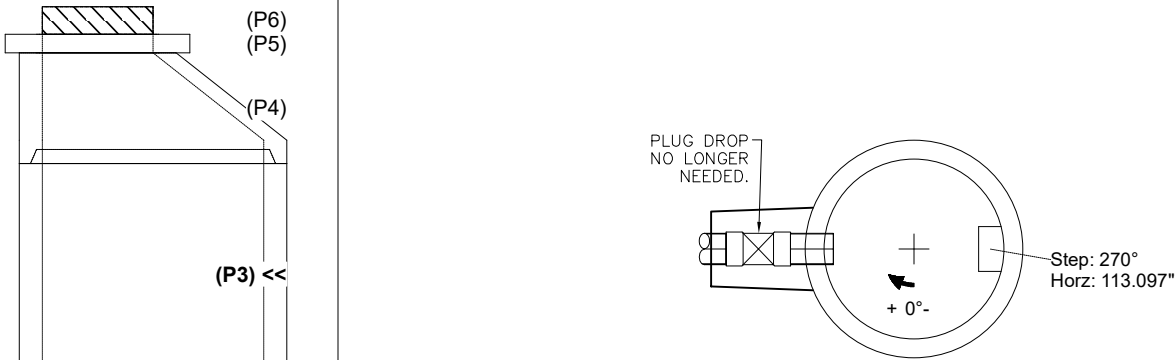
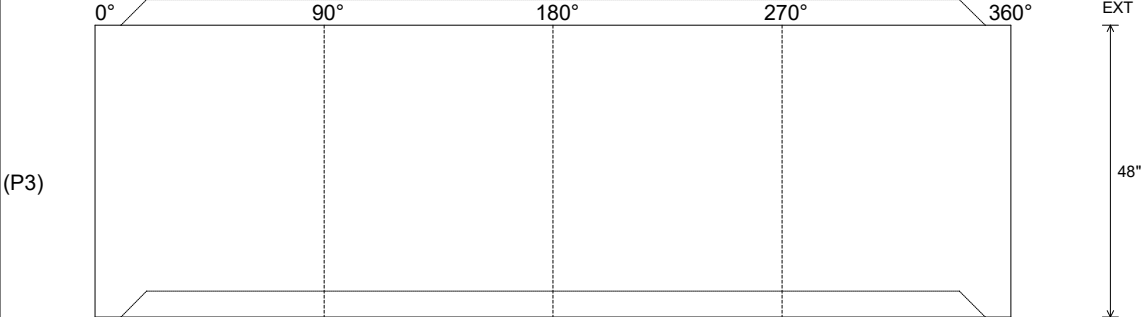


Job Name: 26-1453 Clarksville, TN SPC13A Job Location: Clarksville, TN Contractor: Cleary Construction, Inc.	Plant: Beaver Dam 6/23/2026 9:10:58 AM	Tech: J. Coppage PC: C. Goff	
Structure ID: 13A-PS-MH-002			
P3	MH048RS48CDARED	MH RISER w/ConBlock-CDA Red	

P6) 24" - CASTING HEIGHT - 6" P5) 24" - GRADE RING w/ConBlock-CDA Red - 4" P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 24" P3) 48" - MH RISER w/ConBlock-CDA Red - 48" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 72" P1) 48" - MH BASE w/DROP Cust. Ht/ConBlock-CDA Red - 27" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0410 14) MH Step ML-10-TDS-NCR - 10"	0 lb 270 lb 1738 lb 3353 lb 5030 lb 3090 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 2 lb 0 lb Structure Total: 14924 lb	Structure Notes: 1. JBS-1155 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 5. BASE AND RISERS OF STRUCTURE HAVE BEEN PREVIOUSLY PRODUCED STRUCTURE ID PS-MH-002-3SS-MHD. EXTERNAL DROP NO LONGER NEEDED TO BE PLUGGED. CONE NEEDS TO BE PRODUCED AS PREVIOUS CONE WAS 30".
Rim: 542.44' Rim to Invert: 14.94' Slack: 0.28" Sump: 2" Step Position: 270		

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)				
				
INSIDE WALL DIMENSIONS				
				
Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
