

Job Name: 26-1453 Clarksville, TN SPC13A
Job Location: Clarksville, TN
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam

Tech: J. Coppage

6/23/2026 8:57:34 AM

PC: C. Goff



Structure ID: 13A-PS-MH-004



P4 MH048CN30CDARED

ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red

- P6) 24" - CASTING HEIGHT - 6"
- P5) 24" - GRADE RING w/ConBlock-CDA Red - 3"
- P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30"
- P3) 48" - MH RISER w/DROP/ConBlock-CDA Red - 36"
- P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 60"
- P1) 48" - MH BASE w/DROP Cust. Ht/ConBlock-CDA Red - 35"
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
- 3) 48" - Conseal CS-102 1.00" (Double)
- 2) 24" - Conseal CS-102 1.00" (Double)
- 1) A-Lok - 0410
- 1) Drop Tee - 6" PVC
- 1) Drop Elbow - 6" PVC
- 14) MH Step ML-10-TDS-NCR - 10"

- 0 lb Structure Notes: 1. JBS-1155 SANITARY PROVIDED BY ICAST.
- 202 lb 2. PER ASTM C478 SPECIFICATIONS.
- 1961 lb 3. CONCRETE = 4,000 PSI AT 28 DAYS.
- 2501 lb 4. REINFORCING PER ASTM A615 (GRADE 60).
- 4192 lb - CONE (As .12)
- 3698 lb - RISER/WALLS (As .12)
- 0 lb - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
- 2962 lb 5. BASE AND 60" RISER OF STRUCTURE HAVE BEEN PREVIOUSLY PRODUCED STRUCTURE ID PS-MH-004-5SS-MHD. INVERT 2 OF EXISTING BASE TO BE PLUGGED AS INVERT IS NO LONGER NEEDED.
- 0 lb
- 0 lb
- 1 lb
- 0 lb
- 0 lb
- 0 lb

Structure Total: 15518 lb

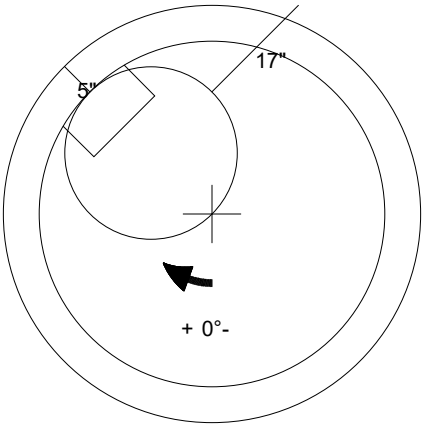

48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30" - (P4)

Coating (Int):	Seam Up: Flat	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 1961 lb
Coating (Ext):	Seam Dn: Groove			Volume (Net): 0.5cu.yd
