

Job Name: 26-1453 Clarksville, TN SPC13A
Job Location: Clarksville, TN
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam

Tech: J. Coppage

6/18/2026 7:40:18 AM

PC: C. Goff



Structure ID: 13A-SS-MH-004

P5 MH060LD13CDARED

MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red

- P6) 24" - CASTING HEIGHT - 6"
P5) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red - 13"
P4) 60" - MH RISER w/ConBlock-CDA Red - 36"
P3) 60" - MH RISER SPECIAL w/ConBlock-CDA Red - 72"
P2) 60" - MH RISER w/ConBlock-CDA Red - 48"
P1) 60" - MH BASE w/ConBlock-CDA Red - 30"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
4) 60" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) A-Lok - 0285
1) A-Lok - 0410
2) A-Lok - 0200
15) MH Step ML-10-TDS-NCR - 10"

0 lb
2800 lb
3758 lb
7440 lb
5011 lb
5752 lb
0 lb
0 lb
2962 lb
0 lb
0 lb
2 lb
1 lb
2 lb
0 lb



Structure Total: 27728 lb

Structure Notes:

1. JBS-1155 SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. CONBLOCK CDA RED ADMIXTURE REQUIRED.
4. REINFORCING: #4 BAR @ 6" O.C. E.W. (GRADE 60).

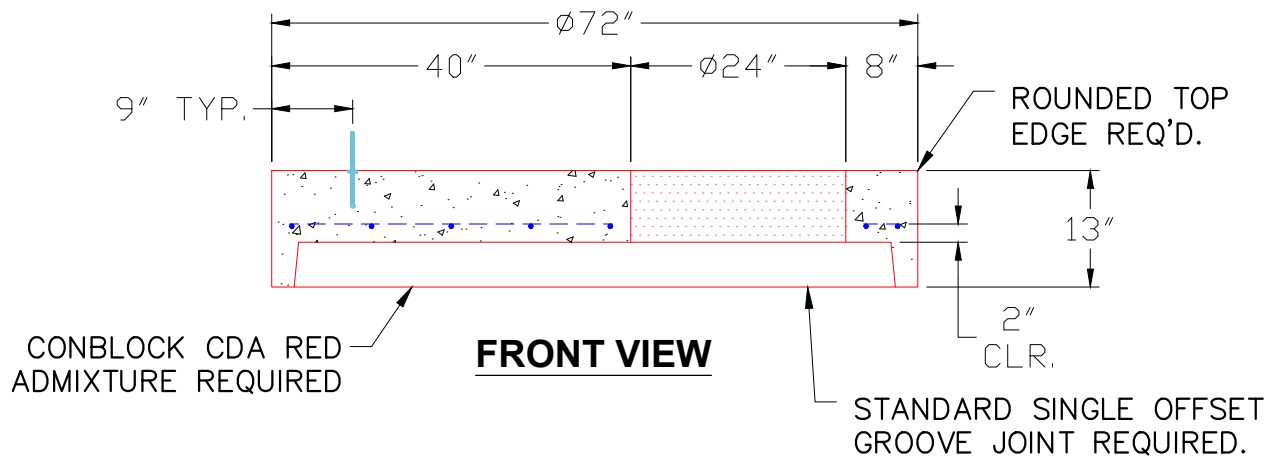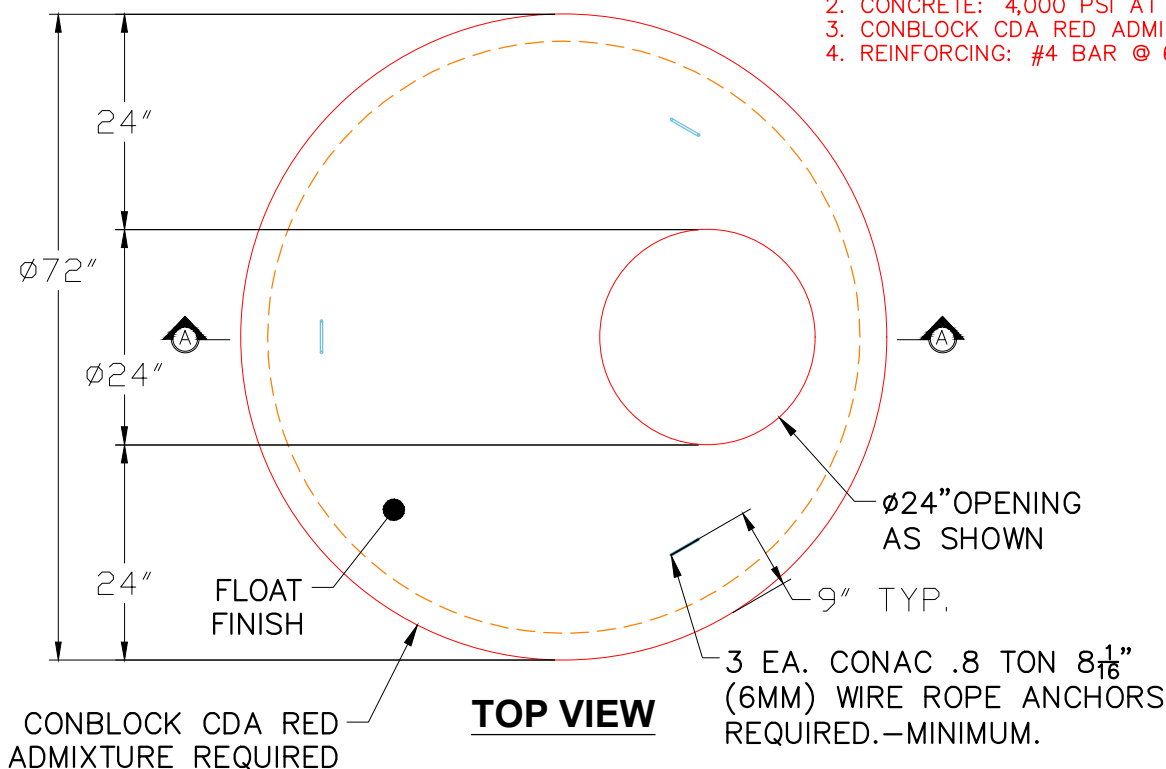

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2800 lb
Volume (Net): 0.69cu.yd
