



Job Name: 26-1466 - Lower Mill Creek HWDW Protection					Plant: 100		Tech: Jared - F			
Job Location: Cincinnati, OH					7/23/2026 10:26:03 AM		PC: E. Bradley			
Contractor: Sunesis Construction										
Structure ID: 210-16 ST-MH										
P1 MH084BAVF		MH BASE Custom Ht T/n								
P6) 24" - CASTING HEIGHT - 7.25" P5) 48" - CON CONE w/24" HOLE F/G - 36" P4) 48" - MH RISER T/G - 72" P3) 48" - MH RISER T/G - 72" P2) 84" - MH Trans. Slab - 48" Hole ECC T/G - 17" P1) 84" - MH BASE Custom Ht T/n - 82" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 84" - Hamilton Kent MH Gasket 3) 48" - Hamilton Kent MH Gasket 2) Hole - 62 18) MH Step ML-10-TDS-NCR - 10"					0 lb 2252 lb 5030 lb 5030 lb 5869 lb 16716 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER CINCINNATI MSD / ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING - RISER/WALLS (As .18) - TRANS SLAB #5 BARS AT 6" C.C.E.W. (DBL MAT) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 496' Rim to Invert: 23.47' Slack: 0.394" Sump: 5.004" Step Position: 90°					Structure Total: 36337 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	472.53'	0°	0"	48" RCP B WALL	58"	Hole 62	62"	69.74"	0"	0"
Invert 2	472.53'	180°	157.125"	48" RCP B WALL	58"	Hole 62	62"	69.74"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

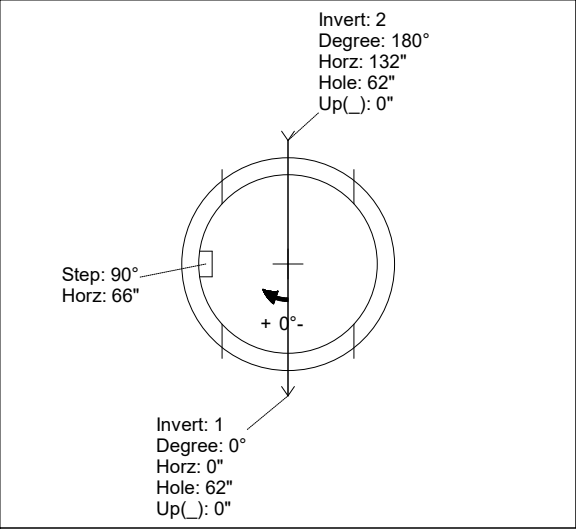

UPSIDE-DOWN VIEW (int. dimensions)

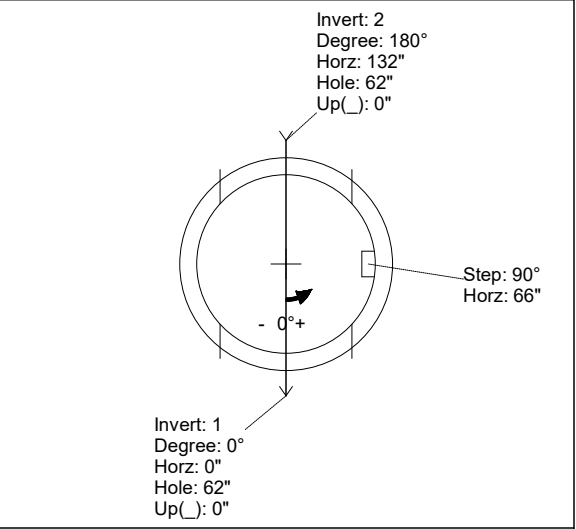

INSIDE WALL DIMENSIONS

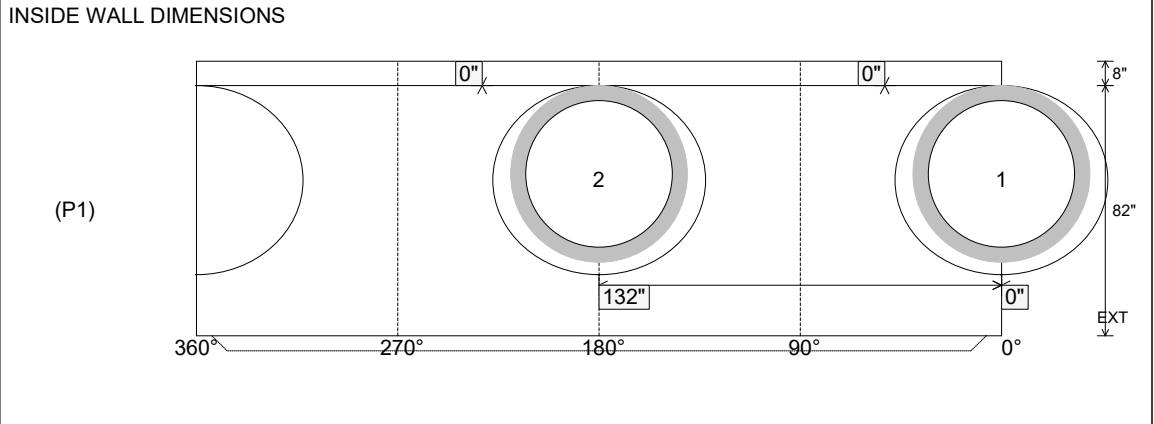

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 82" Height (Ext): 90"	Weight (Net): 16716 lb Volume (Net): 4.27cu.yd
----------------------------------	---------------------------------	--	--	---
