



Structure ID: CV-2			
Spec: Box Culvert	Rim: 43.75'	Sump: 0"	Floor (Bot): 0'
Type: Box Culvert (08W/08F/08T)	Invert: 43.75'	Floor (Top): 0'	Overall Height: 43.75'
Size: 48" x 60"	Rim to Invert: 0'	Floor Height: 0"	Slack: 0"

STRUCTURE SUMMARY:	
P8) 48" x 60" - BOX CULVERT (08W/08F/08T) F/G - 54"	9723 lb
P7) 48" x 60" - BOX CULVERT (08W/08F/08T) T/G - 69"	12423 lb
P6) 48" x 60" - BOX CULVERT (08W/08F/08T) T/G - 69"	12423 lb
P5) 48" x 60" - BOX CULVERT (08W/08F/08T) T/G - 69"	12423 lb
P4) 48" x 60" - BOX CULVERT (08W/08F/08T) T/G - 69"	12423 lb
P3) 48" x 60" - BOX CULVERT (08W/08F/08T) T/G - 69"	12423 lb
P2) 48" x 60" - BOX CULVERT (08W/08F/08T) T/G - 69"	12423 lb
P1) 48" x 60" - BOX CULVERT (08W/08F/08T) T/F - 57"	10263 lb
1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
8) 48" x 60" - Conseal CS-102 1.00"	0 lb


Structure Total:	94524 lb

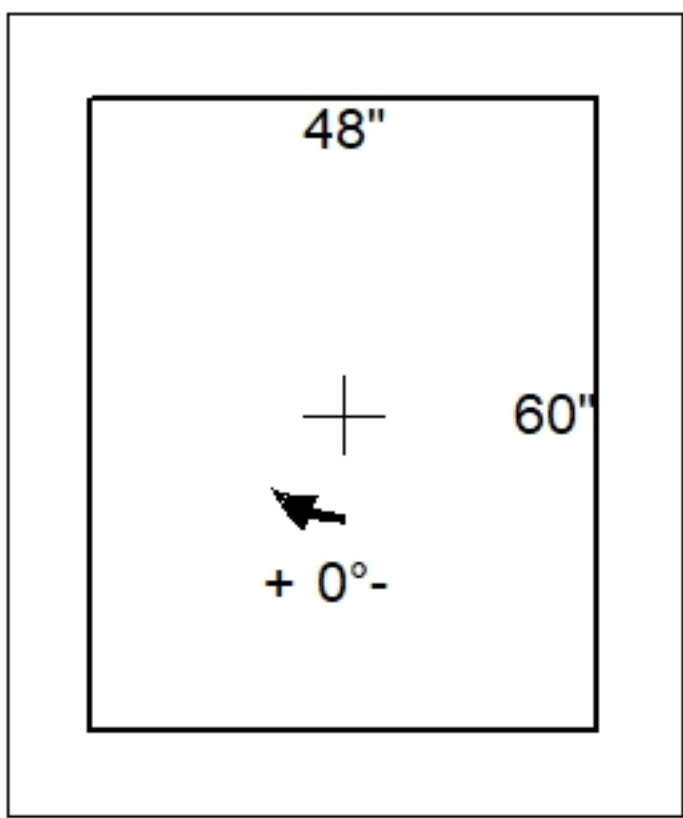

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	43.75'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

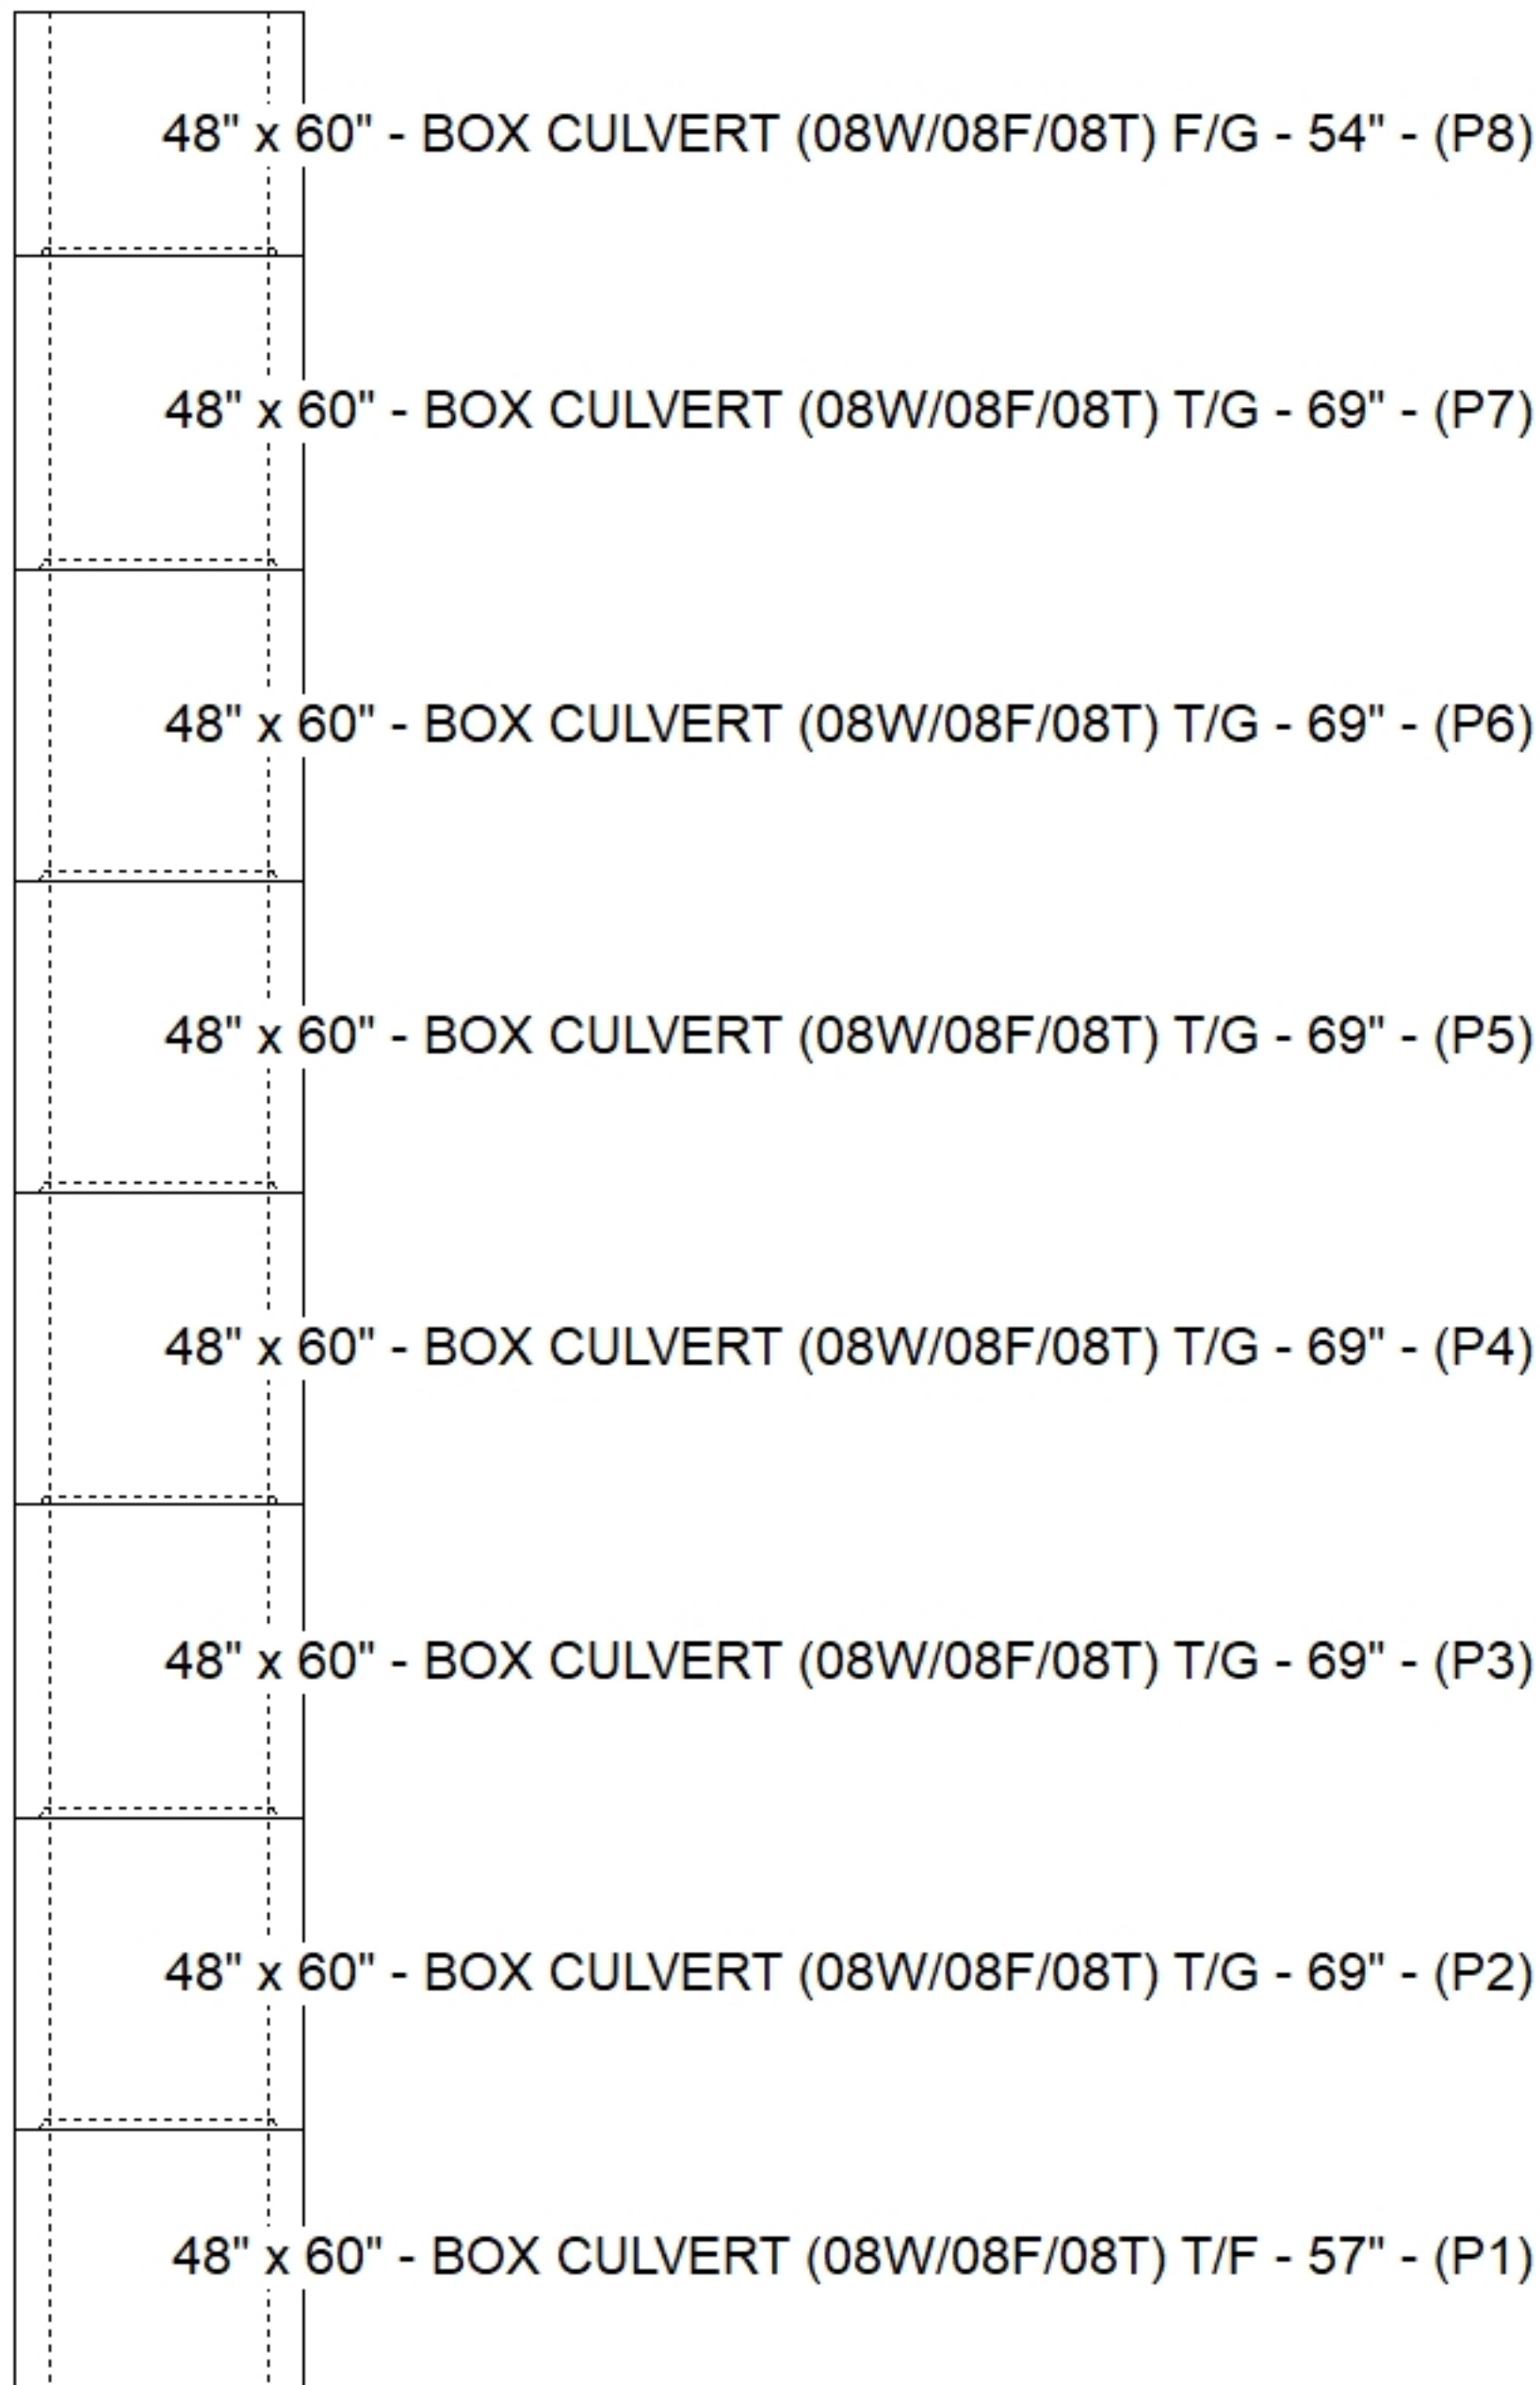

Default - Interior Dimensions

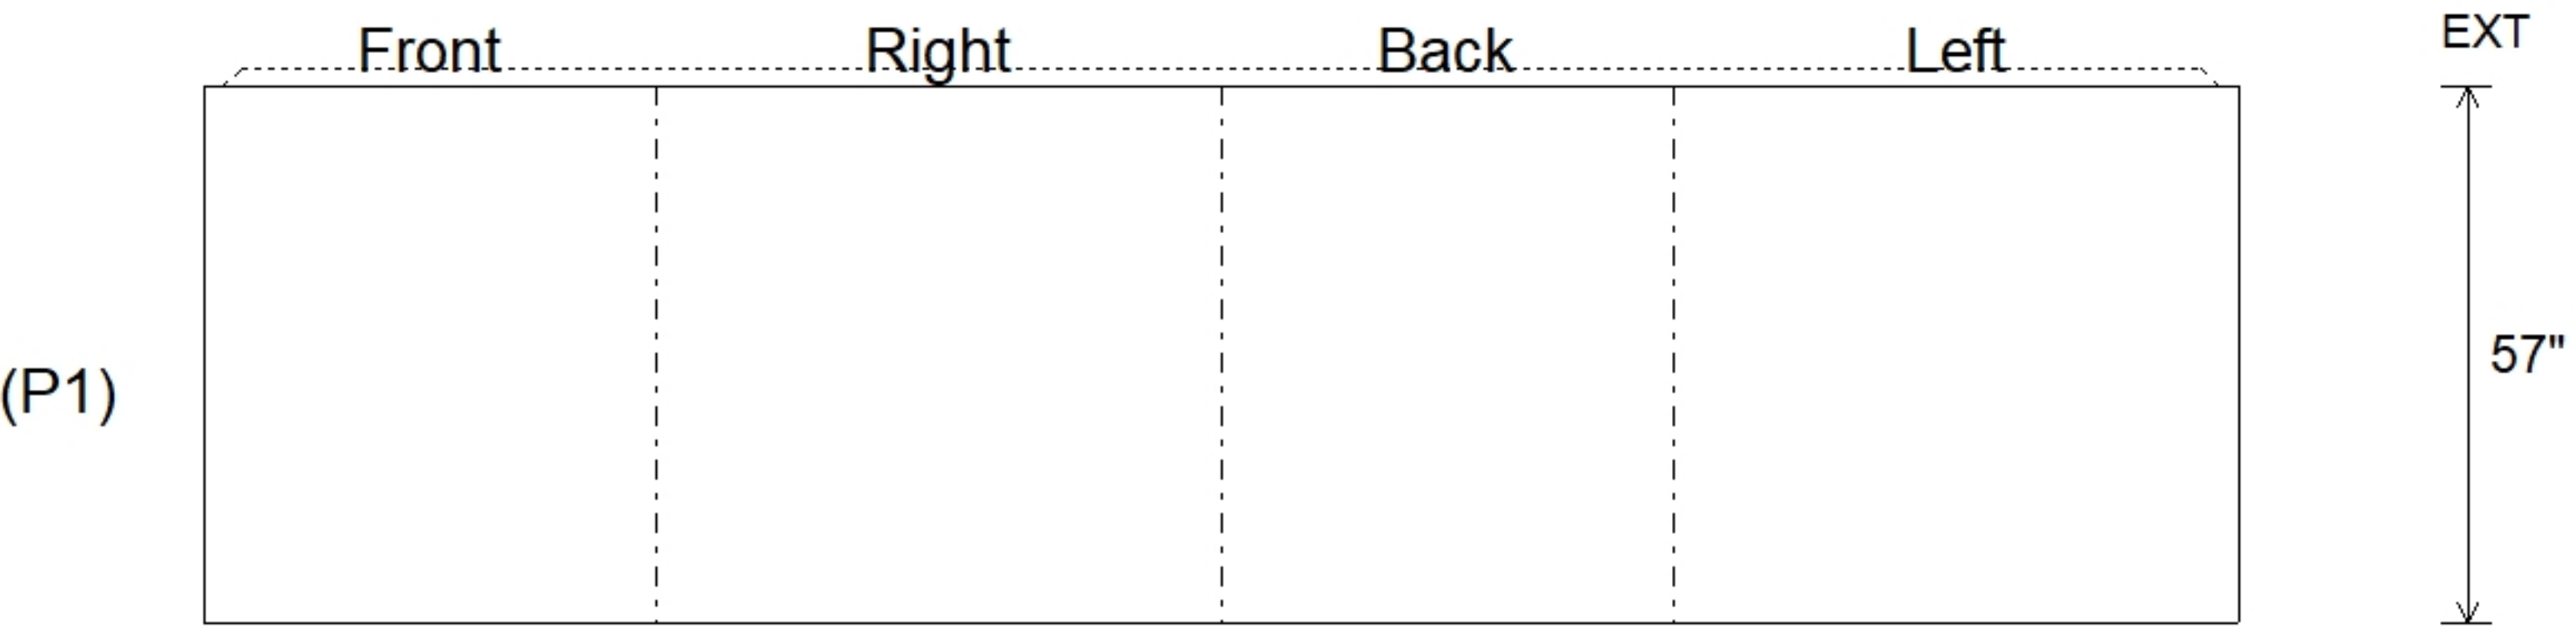

Submittal Drawing 10/5/2026 12:28:05 PM	SUBMITTAL APPROVED BY:
--	---------------------------
