

Job Name: 26-1510 West Railroad Ave
Job Location: Elizabethtown, KY
Contractor: Schroeder Construction, Inc.

Plant: 100

5/5/2026 7:45:16 AM

Tech: Jared - A
PC: Celina Goff



Structure ID: 11 (2)

P1 CSWBF

Custom Sidewalk Bridge Footer F/n

P1) 72" x 36" - Custom Sidewalk Bridge Footer F/n - 12"
1) SECONDARY POUR

Structure Total:





4060 lb
0 lb
4060 lb

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 5,000 PSI AT 28 DAYS
3. REINFORCEMENT - 2" MIN. REBAR CLEARANCE (TYP):
 - SHORT BARS: #4 BAR @ 12" C.C. E.W. (GRADE 60)
 - LONG BARS: #5 BAR @ 12" C.C. E.W. (GRADE 60)
 - ALL BARS TO BE EPOXY COATED
4. WET STICK DOUBLE MAT OF 12" X 30" #4 L-BARS SPACED @ 12" C.C. E.W. (GRADE 60) FOR VERTICAL WALL POUR TIE-IN (SEE L-BAR DETAIL) - L-BARS TO BE EPOXY COATED
5. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN

FIRST POUR (FOOTER): 2,610 LBS

SECOND POUR (VERTICAL WALL): 1,450 LBS

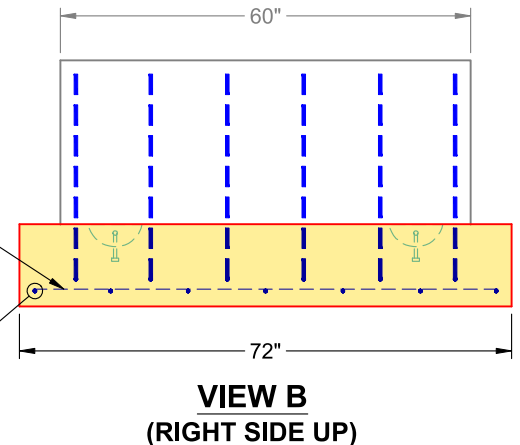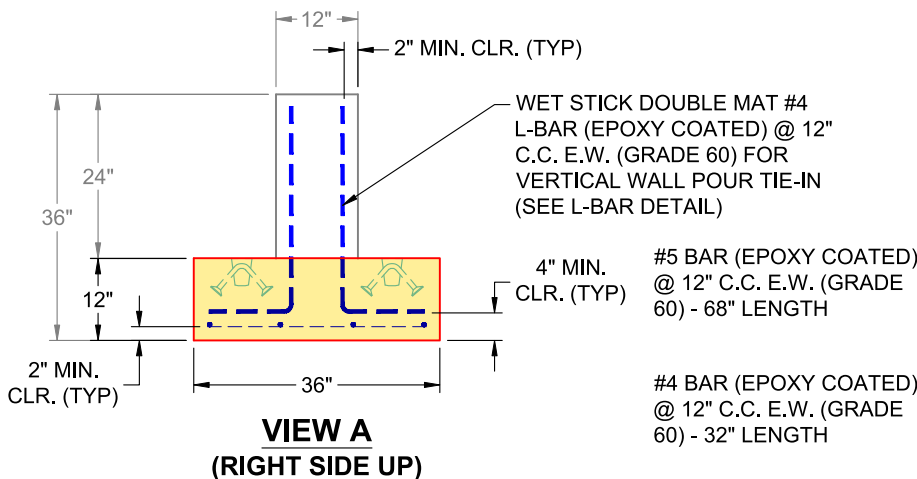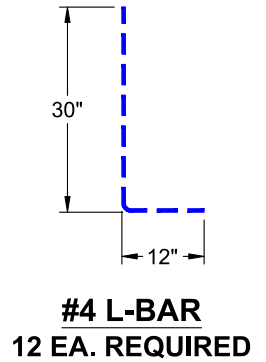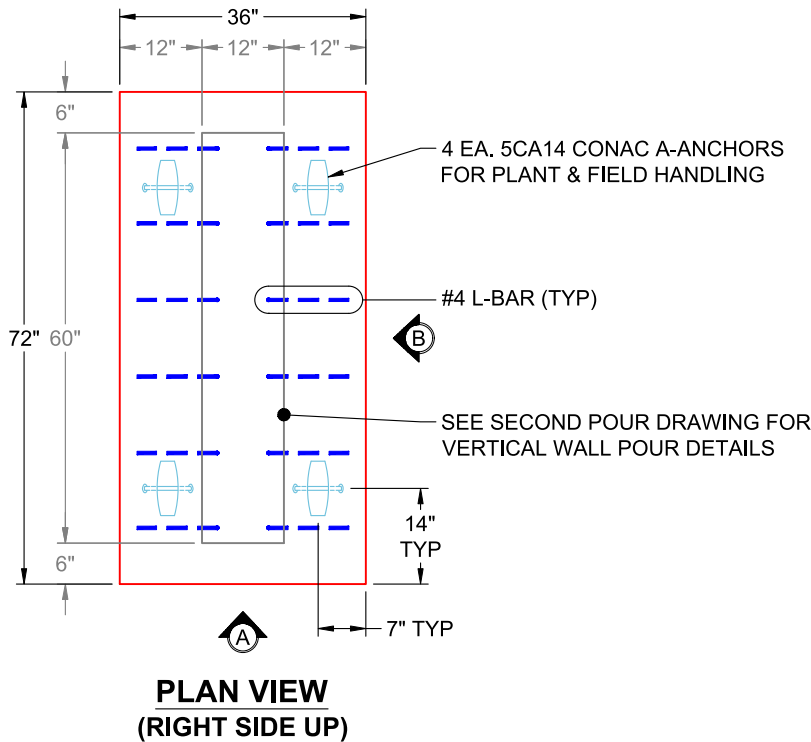


Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 0"
Floor Height: 12"

Height (Int): 0"
Height (Ext): 0"

Weight (Net): 4060 lb
Volume (Net): 1.04cu.yd

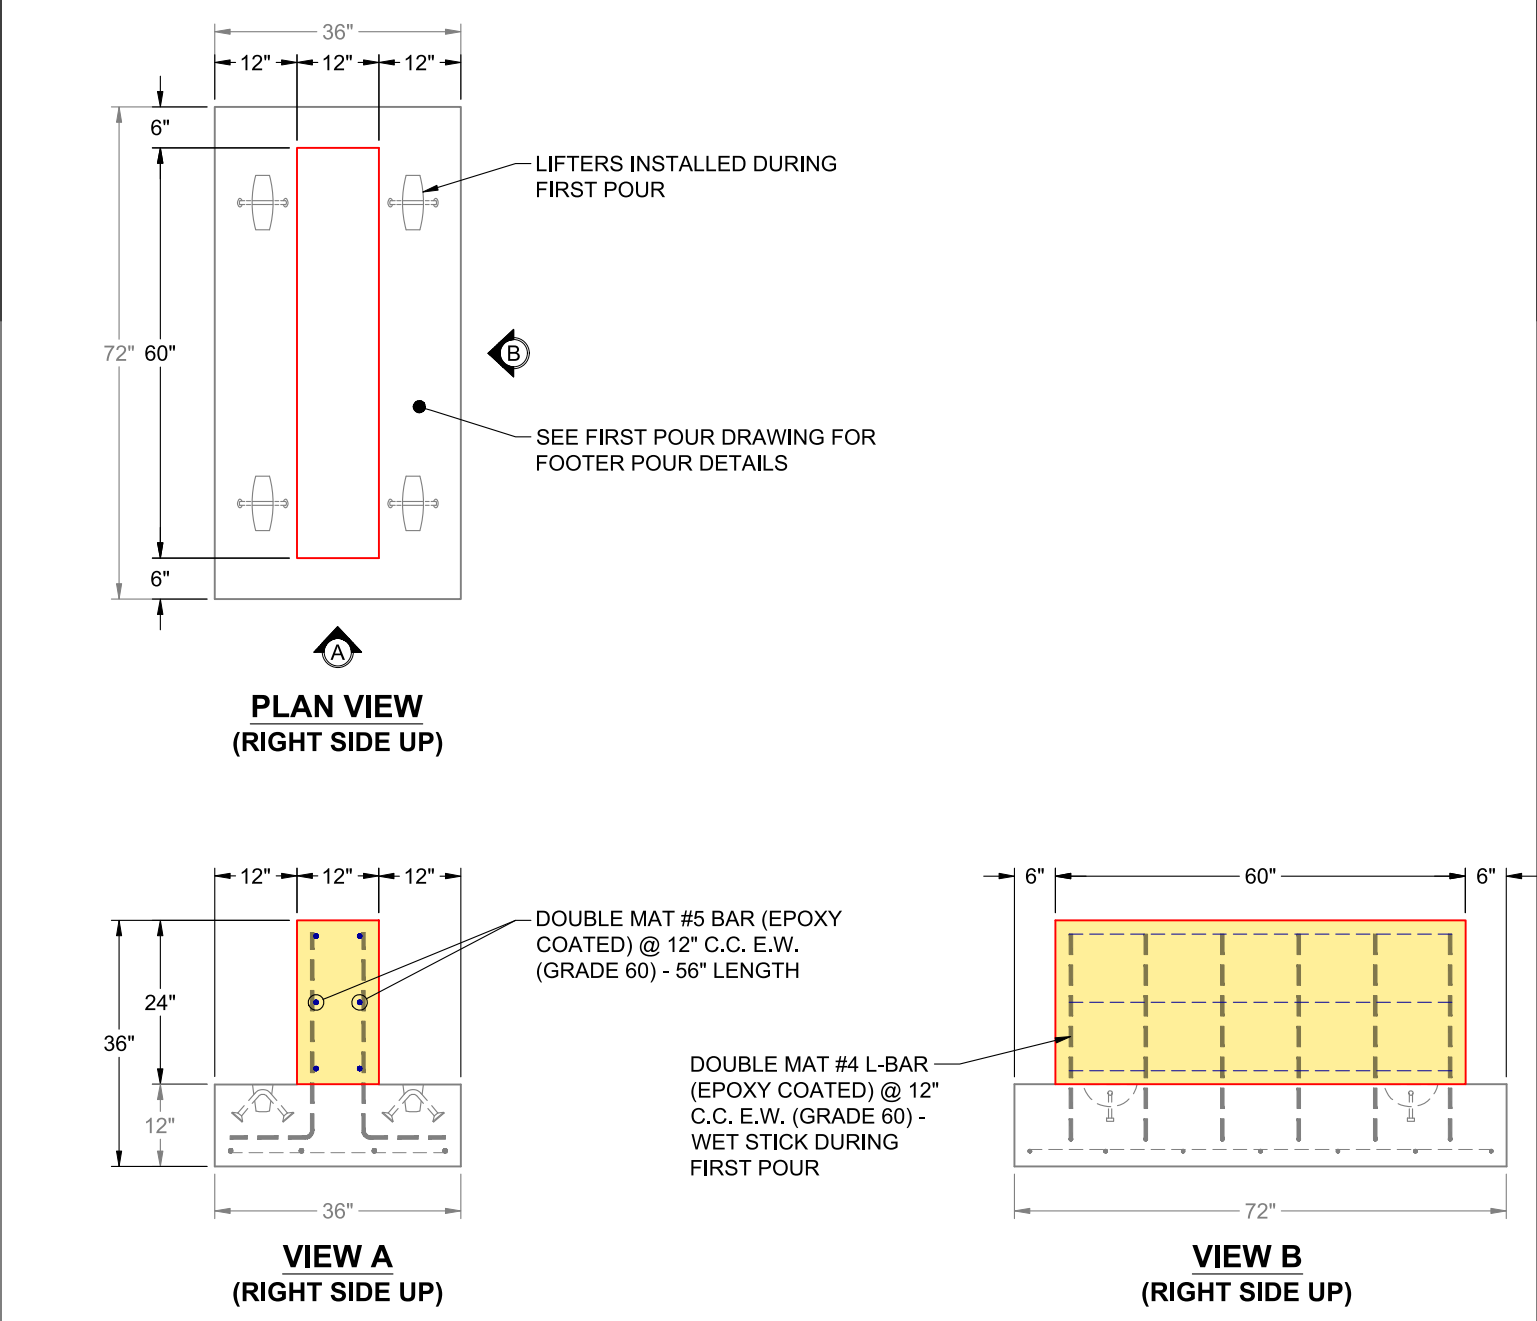Job Name: 26-1510 West Railroad Ave Job Location: Elizabethtown, KY Contractor: Schroeder Construction, Inc.	Plant: 100 5/5/2026 7:45:16 AM	Tech: Jared - A PC: Celina Goff	
Structure ID: 11 (2)			
P1 CSWBF Custom Sidewalk Bridge Footer F/n			
P1) 72" x 36" - Custom Sidewalk Bridge Footer F/n - 12" 1) SECONDARY POUR Structure Total: 4060 lb 0 lb 4060 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 5,000 PSI AT 28 DAYS 3. REINFORCEMENT - 2" MIN. REBAR CLEARANCE (TYP): - VERTICAL BARS: DOUBLE MAT #4 L-BAR @ 12" C.C. E.W. (GRADE 60) - WET STICK DURING FLOOR POUR - HORIZONTAL BARS: DOUBLE MAT #5 BAR @ 12" C.C. E.W. (GRADE 60) - ALL BARS TO BE EPOXY COATED 5. LIFTERS INSTALLED DURING FLOOR POUR	
FIRST POUR (FOOTER): 2,610 LBS SECOND POUR (VERTICAL WALL): 1,450 LBS			
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 0" Floor Height: 12"	Height (Int): 0" Height (Ext): 0" Weight (Net): 4060 lb Volume (Net): 1.04cu.yd
