

Contractor: Lawrence Construction & Leasing, Inc.

TECH: J.Horsley

Plant: 100



Size: 24" x 24"

Rim to Invert: 3.4'

Floor Height: 8"


Slack: 2.8"

- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

⇒ There is

4000 Hz

Structure Total: 4286 lb

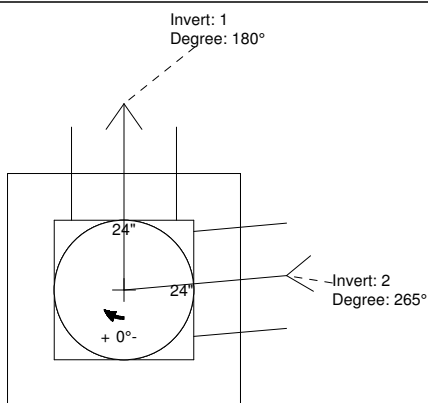


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	878.92'							
Reducer								
Invert 1	875.52'	180°	12" HDPE	14.5"	18"	Hole 18	-3"	P1
Invert 2	875.52'	265°	12" HDPE	14.5"	18"	Hole 18	-3"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 24" - BX FLAT LID 8inW SPEC. (KY JB-B1) F/F - 8" - (P2)

24" x 24" - BOX BASE 8inW, 8inF F/n - 30" - (P1)

Cast (Int. Dim.) - Interior Dimensions

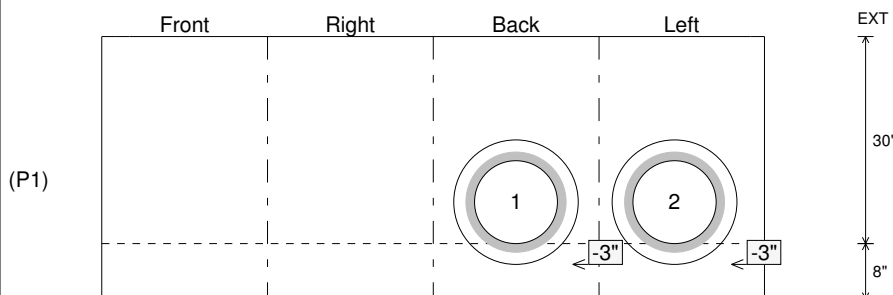

Submittal Drawing
5/19/2026 9:20:54 PM

SUBMITTAL
APPROVED BY:
