

Contractor: Garney Companies, Inc.

TECH: Jared - A

Plant: 100



Size: 60"

Rim to Invert: 28.39'

Floor Height: 8"


Slack: 0.68"

1. JBS 1150 F/C SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = XYPEX C-1000 RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
6. DOUBLE BANDS FOR BOOTS
7. ANY REQUIRED INTERIOR EPOXY COATING TO BE SUPPLIED & INSTALLED BY OTHERS
8. **NO STEPS**


P7) 24" - CASTING HEIGHT - 7"	0 lb
P6) 60" - XYPEX MH FLAT TOP w/24" CC Hole - 13"	2701 lb
P5) 60" - MH RISER w/XYPEX SPECIAL - 36"	3758 lb
P4) 60" - MH RISER w/XYPEX SPECIAL - 72"	7516 lb
P3) 60" - MH RISER w/XYPEX SPECIAL - 72"	7516 lb
P2) 60" - MH RISER w/XYPEX SPECIAL - 72"	7516 lb
P1) 60" - MH BASE EF (08F/07EF) XYPEX - 70"	10274 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) ADMIXTURE XYPEX C-1000 RED	0 lb
1) 60" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT	2962 lb
1) SECONDARY POUR - EXT. FLANGE	0 lb
1) CASTING - JBS 1150 F/C SANITARY	250 lb
5) 60" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
2) A-Lok - 1040	2 lb

Structure Total:	42496 lb


Structure Total: 42496 lb

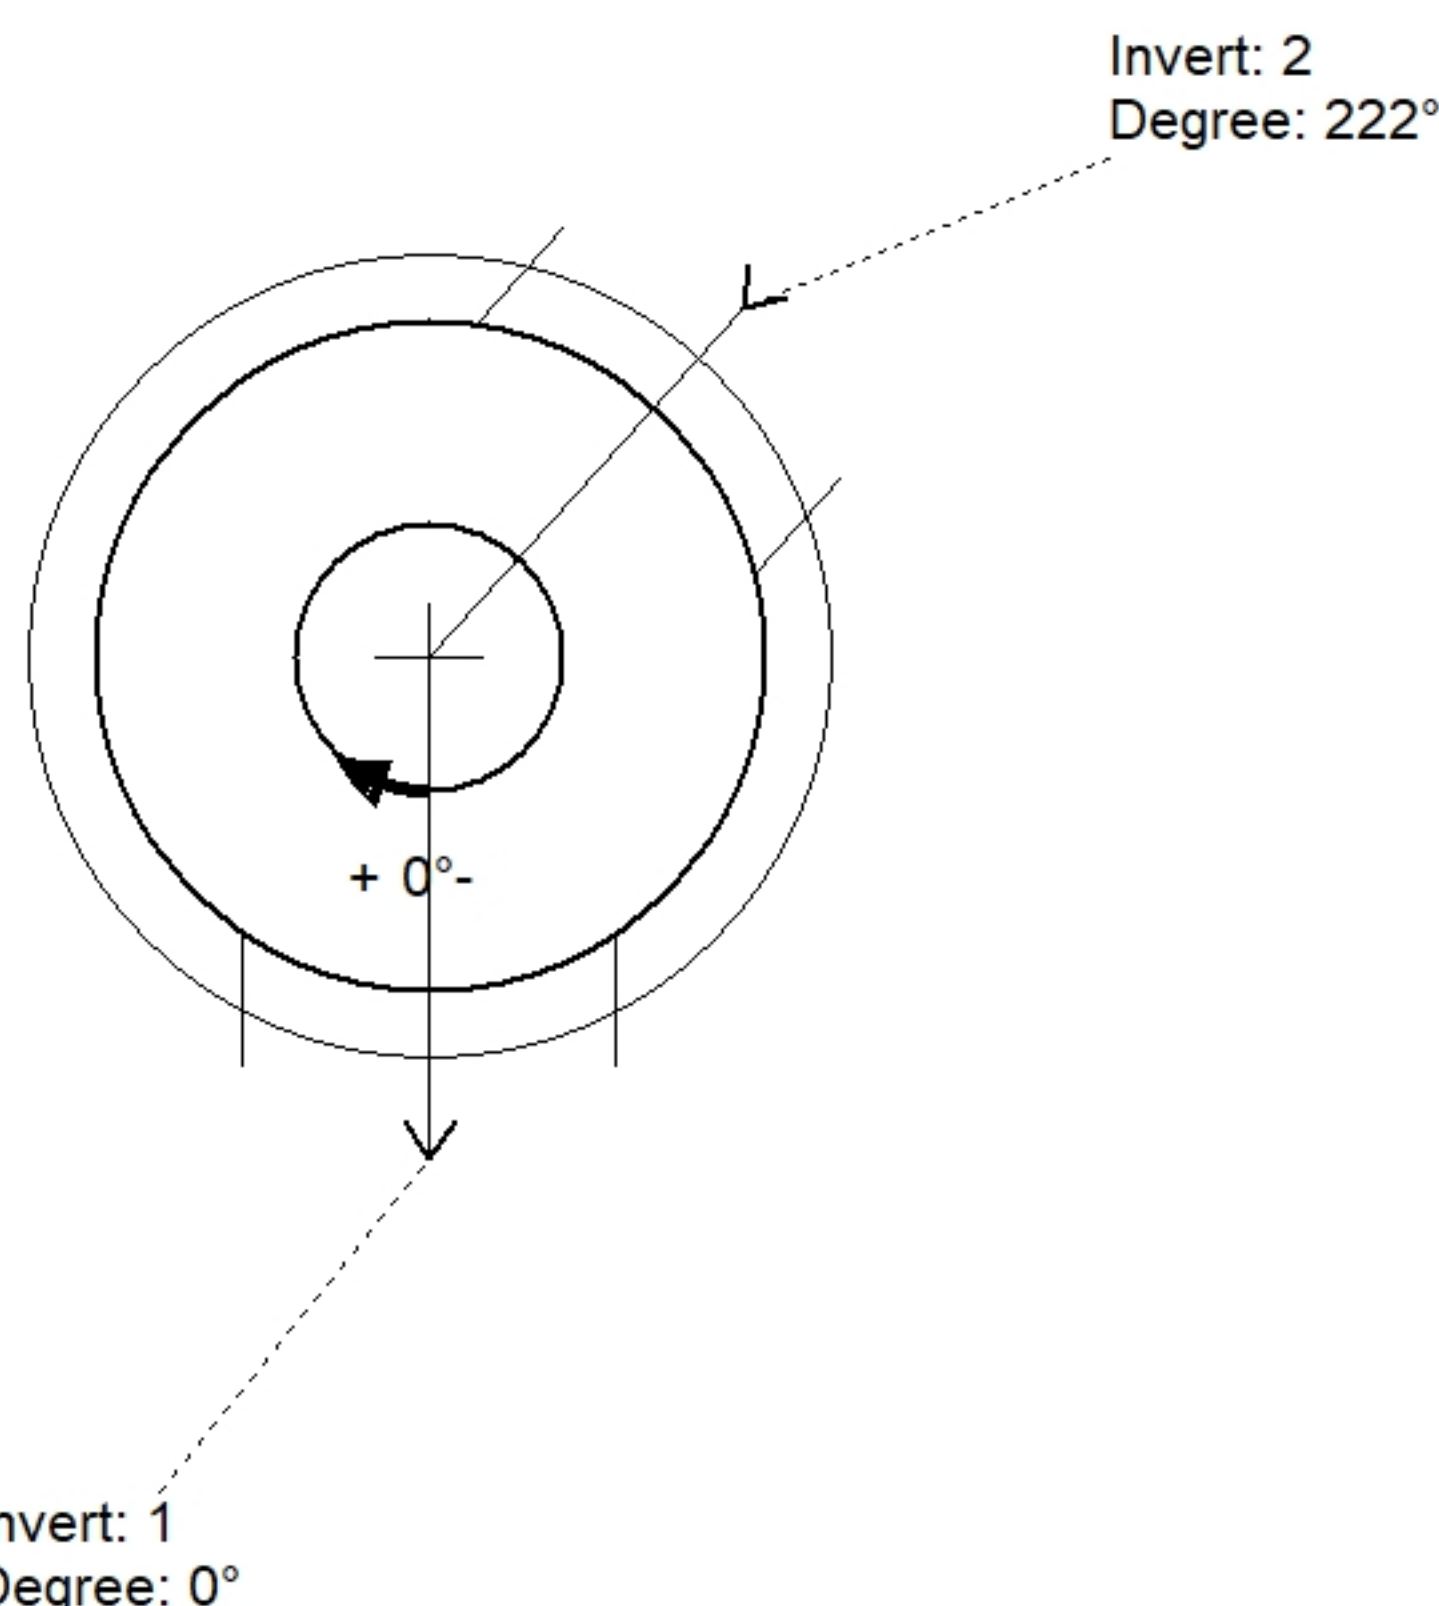

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	414.72'							
Reducer								
Invert 1	386.33'	0°	30" DI	32"	33.5"	A-Lok 1040	0.25"	P1
Invert 2	387.1'	222°	30" DI	32"	33.5"	A-Lok 1040	9.49"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

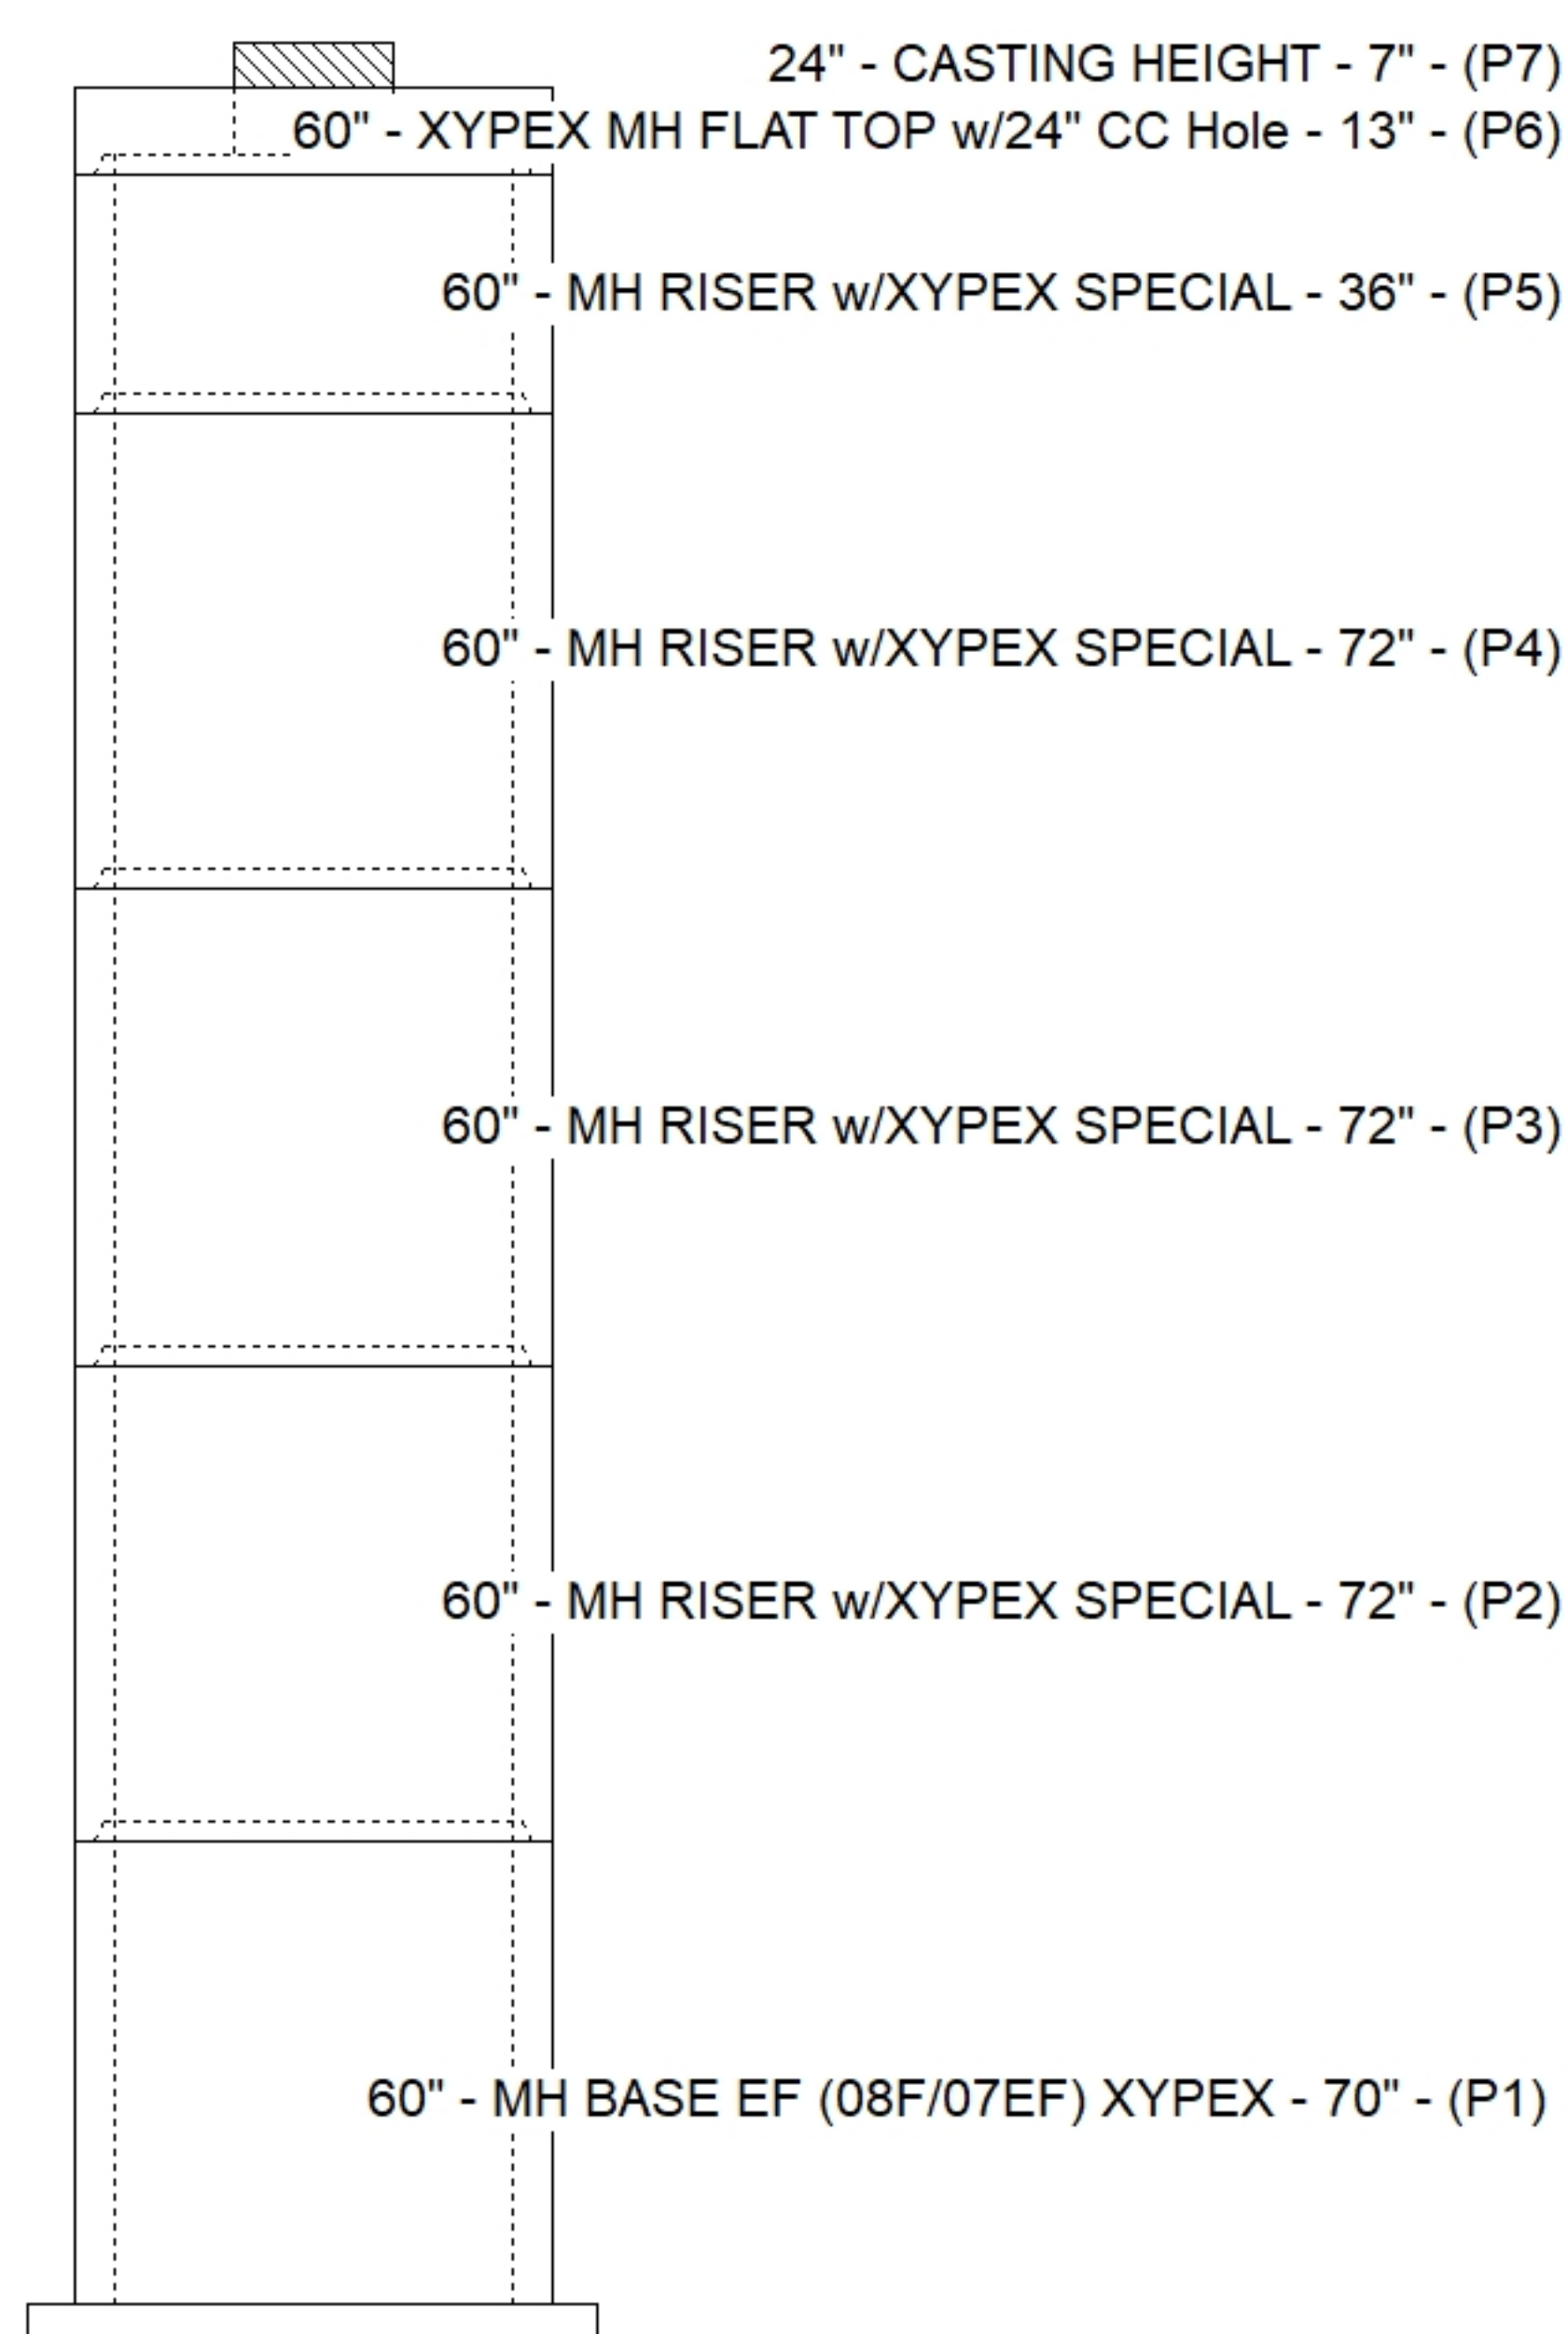

Default - Interior Dimensions

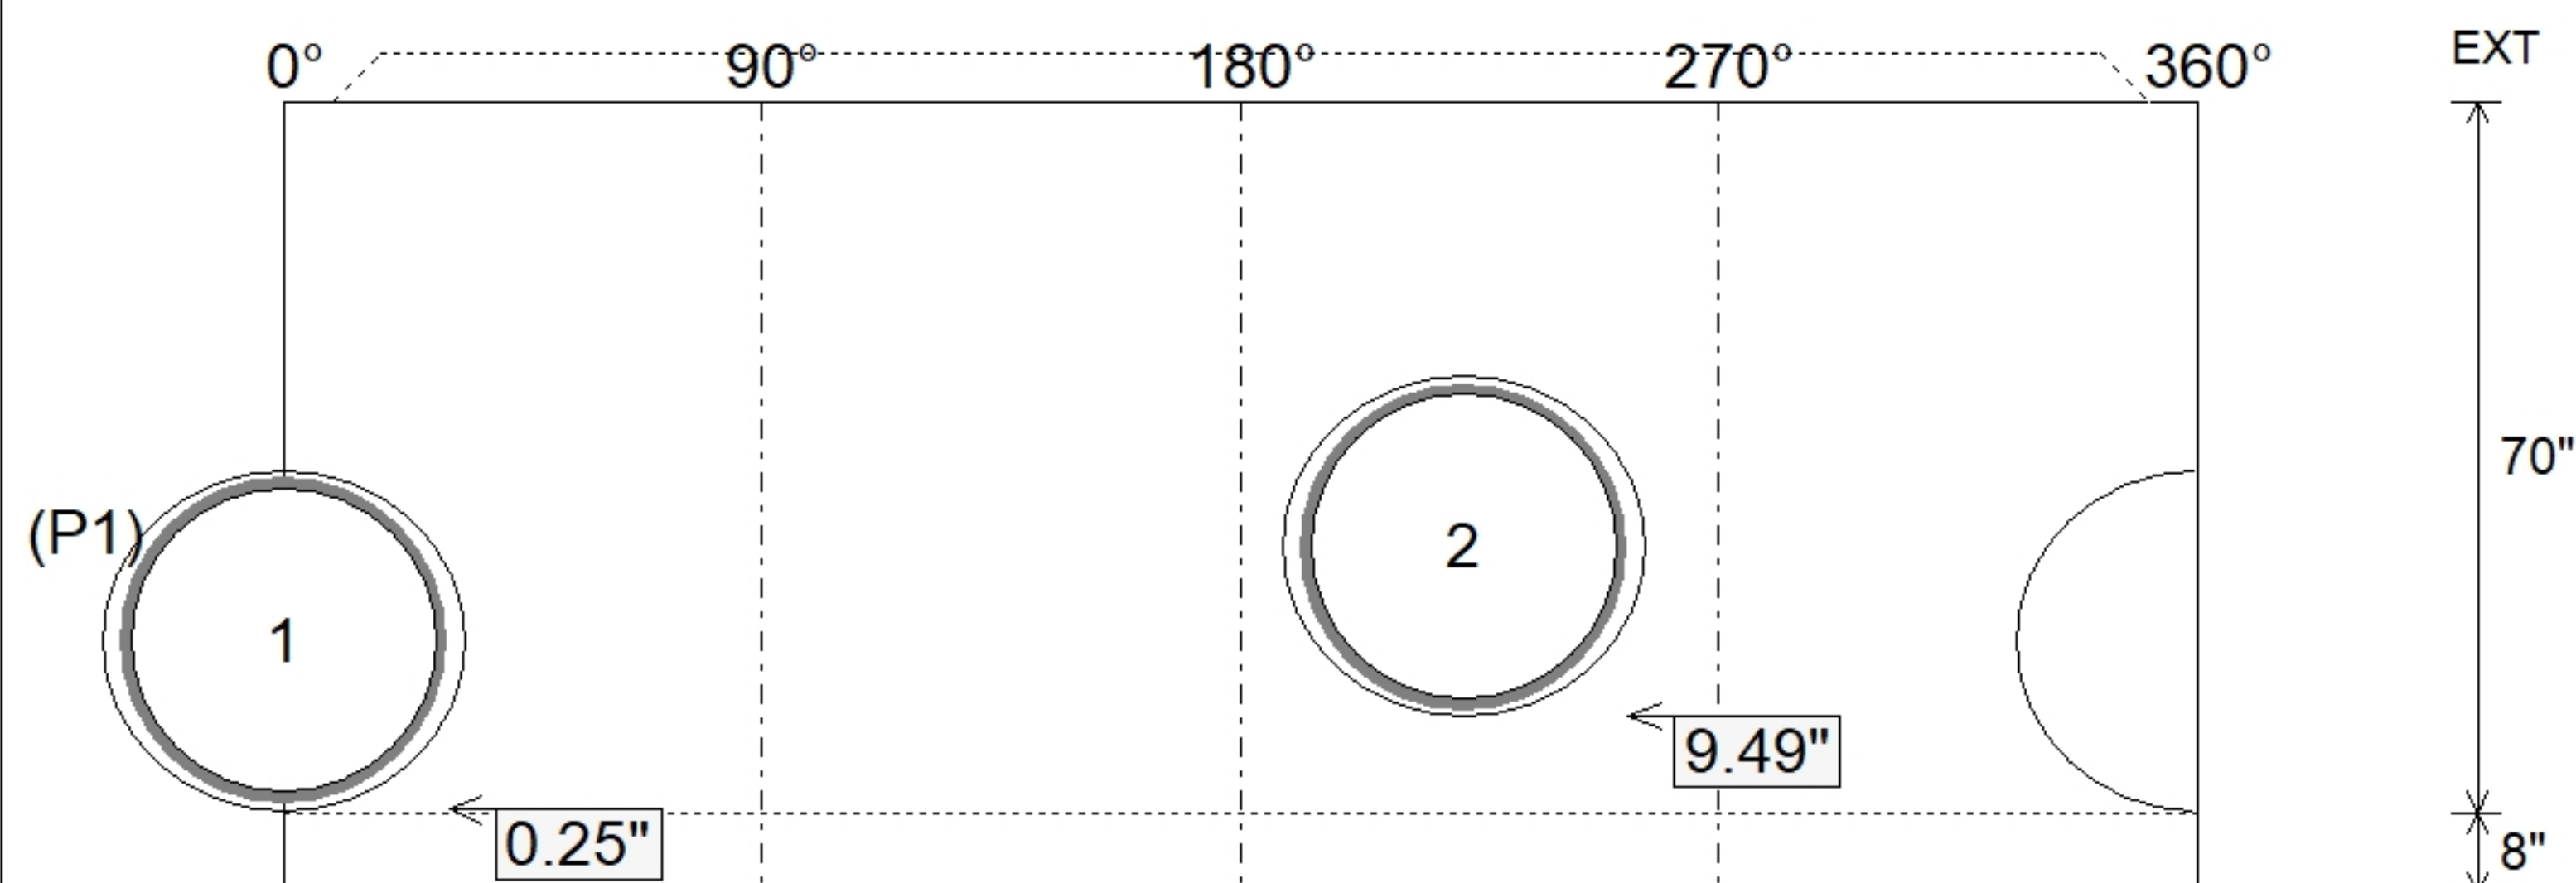

Submittal Drawing
8/5/2026 2:57:24 PM

SUBMITTAL
APPROVED BY:
