




Job Name: 26-1549 Cowan St. Trunk Sewer Job Location: Nashville, TN Contractor: Garney Companies, Inc.					Plant: 100 8/24/2026 11:21:08 AM		Tech: Jared - A PC: Jay Ross Jarvis				
Structure ID: MH-1-2 SS-MH											
P3 MH084RS96X			MH RISER w/XYPEX								
P7) 30" - CASTING HEIGHT - 6" P6) 84" - MH FLAT TOP w/2X 30" Holes ECC w/XYPEX - 17" P5) 84" - MH RISER Custom Ht, w/XYPEX - 43" P4) 84" - MH RISER w/XYPEX - 96" P3) 84" - MH RISER w/XYPEX - 96" P2) 84" - MH RISER w/XYPEX - 96" P1) 84" - MH BASE w/FLANGE (12F/14EF) w/XYPEX - 84" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE XYPEX C-1000 RED 1) SECONDARY POUR - EXT. FLANGE 2) CASTING - JBS 1312 F/C SANITARY 5) 84" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1840						0 lb 6992 lb 8343 lb 18626 lb 18626 lb 18626 lb 25257 lb 0 lb 0 lb 0 lb 0 lb 600 lb 0 lb 2 lb ----- 97073 lb		Structure Notes: PLAN LABEL: MH-1 1. JBS 1312 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = XYPEX C-1000 RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .24) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W. 6. ANY REQUIRED INTERIOR COATINGS TO BE SUPPLIED & APPLIED BY OTHERS. 7. **NO STEPS**			
Rim: 418.4' Rim to Invert: 36.35' Slack: 0.7" Sump: 2.5" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

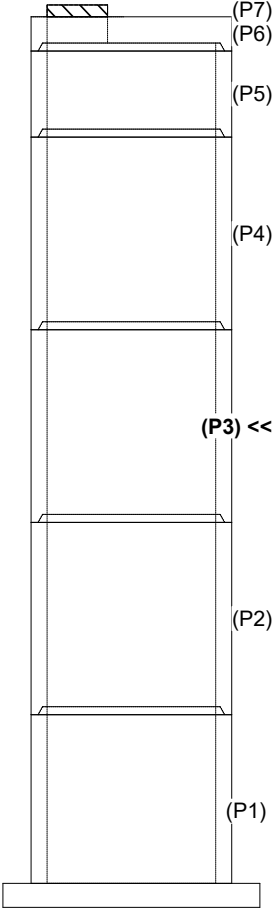

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

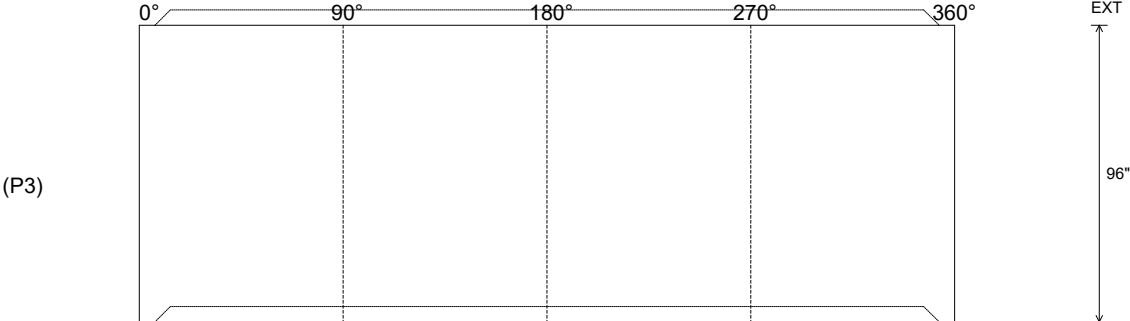

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 96" Height (Ext): 96"	Weight (Net): 18626 lb Volume (Net): 4.76cu.yd
----------------------------------	------------------------------------	--	--	---
