


Job Name: 26-1549 Cowan St. Trunk Sewer Job Location: Nashville, TN Contractor: Garney Companies, Inc.				Plant: 100 8/24/2026 11:21:30 AM		Tech: Jared - A PC: Jay Ross Jarvis				
Structure ID: MH-11-14 SS-MH										
P3 MH048RS72XS			MH RISER w/XYPEX/NO STEP							
P7) 24" - CASTING HEIGHT - 7.50" P6) 24" - XYPEX GRADE RING - 3" P5) 48" - CON XYPEX CONE w/24" HOLE-SPECIAL - 36" P4) 48" - MH RISER w/XYPEX/NO STEP - 36" P3) 48" - MH RISER w/XYPEX/NO STEP - 72" P2) 48" - MH RISER w/XYPEX/NO STEP - 72" P1) 48" - MH BASE EF/Xypex Cust. Ht. 08"F (08"EF =74"OD) - 48" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE XYPEX C-1000 RED 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1123 WT F/C Sanitary 4) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12M DD (DBL Bands)						0 lb 202 lb 2251 lb 2515 lb 5030 lb 5030 lb 6145 lb 0 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb		Structure Notes: . PLAN LABEL: MH-11 1. JBS 1123 WT F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = XYPEX C-1000 RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 6. DOUBLE BANDS FOR BOOTS 7. **NO STEPS**		
Rim: 414.43'		Rim to Invert: 22.95'		Slack: 2.9"		Sump: 2'		Structure Total: 22879 lb Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



(P7)
(P6)

(P5)


(P4)

(P3) <<

(P2)


(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



+ 0°-

INSIDE WALL DIMENSIONS

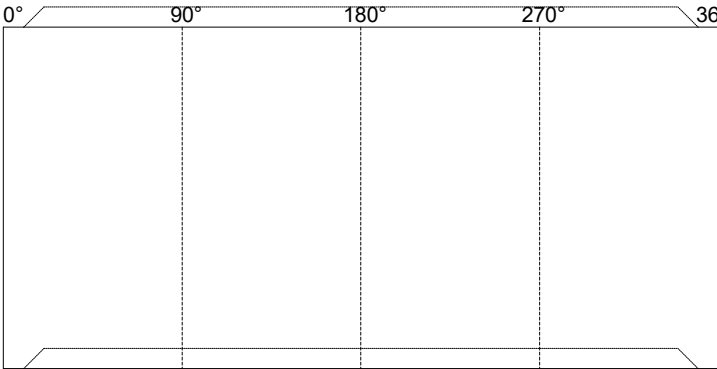

0° 90° 180° 270° 360°

EXT

72"

(P3)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 5030 lb Volume (Net): 1.28cu.yd
----------------------------------	------------------------------------	--	--	--
