



Job Name: 26-1549 Cowan St. Trunk Sewer Job Location: Nashville, TN Contractor: Garney Companies, Inc.					Plant: 100 8/24/2026 11:21:10 AM		Tech: Jared - A PC: Jay Ross Jarvis					
Structure ID: MH-2-3 SS-MH												
P2 MH108RS96X			MH RISER w/XYPEX									
P7) 30" - CASTING HEIGHT - 6" P6) 108" - MH FLAT TOP w/2X 30" Holes ECC w/XYPEX - 17" P5) 108" - MH RISER w/XYPEX - 72" P4) 108" - MH RISER w/XYPEX - 96" P3) 108" - MH RISER w/XYPEX - 96" P2) 108" - MH RISER w/XYPEX - 96" P1) 108" - MH BASE EF Cust. Ht. 12'F (21"EF =170"OD) w/XYPEX - 80" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE XYPEX C-1000 RED 1) SECONDARY POUR - EXT. FLANGE 2) CASTING - JBS 1312 F/C SANITARY 5) 108" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1840						0 lb 12344 lb 22397 lb 29863 lb 29863 lb 29863 lb 42930 lb 0 lb 0 lb 0 lb 0 lb 600 lb 0 lb 2 lb ----- Structure Total: 167860 lb		Structure Notes: . PLAN LABEL: MH-2 1. JBS 1312 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = XYPEX C-1000 RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .24) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W. 6. ANY REQUIRED INTERIOR COATINGS TO BE SUPPLIED & APPLIED BY OTHERS. 7. **NO STEPS**				
Rim: 420.67'		Rim to Invert: 38.4'		Slack: 0.3"		Sump: 2.5"		Step Position:				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

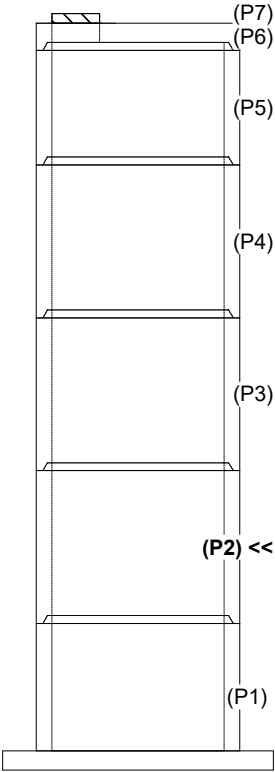

INSIDE WALL DIMENSIONS

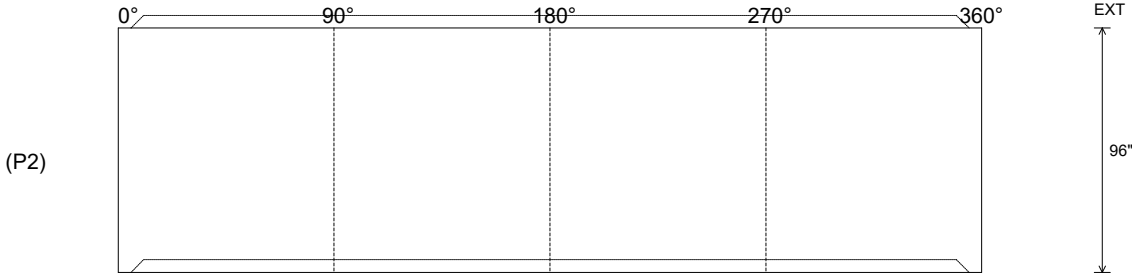

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 10" Floor Height: 0"	Height (Int): 96" Height (Ext): 96"	Weight (Net): 29863 lb Volume (Net): 7.63cu.yd
----------------------------------	------------------------------------	---	--	---
