

Job Name: 26-1549 Cowan St. Trunk Sewer
Job Location: Nashville, TN
Contractor: Garney Companies, Inc.

Plant: 100
8/5/2026 9:32:23 AM

Tech: Jared - A
PC: Jay Ross Jarvis



Structure ID: MH-4-5 SS-MH

P3 MH084RS96X

MH RISER w/XYPEX

- P6) 30" - CASTING HEIGHT - 6"
P5) 84" - MH FLAT TOP w/2X 30" Holes ECC w/XYPEX - 17"
P4) 84" - MH RISER w/XYPEX - 84"
P3) 84" - MH RISER w/XYPEX - 96"
P2) 84" - MH RISER w/XYPEX - 96"
P1) 84" - MH BASE w/FLANGE (12F/14EF) w/XYPEX - 95"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) ADMIXTURE XYPEX C-1000 RED
1) SECONDARY POUR - EXT. FLANGE
2) CASTING - JBS 1312 WT F/C SANITARY
4) 84" - Conseal CS-102 1.00" (Double)
2) A-Lok - 1840

- 0 lb
6992 lb
16298 lb
18626 lb
18626 lb
27392 lb
0 lb
0 lb
0 lb
0 lb
600 lb
0 lb
2 lb



88536 lb
- Structure Notes: .
PLAN LABEL: MH-4
1. JBS 1312 WT F/C SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = XYPEX C-1000 RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .24)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.
6. ANY REQUIRED INTERIOR COATINGS TO BE SUPPLIED & APPLIED BY OTHERS.
7. **NO STEPS**

Structure Total: 88536 lb


Rim: 416.22' Rim to Invert: 32.66' Slack: 0.42" Sump: 2.5" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

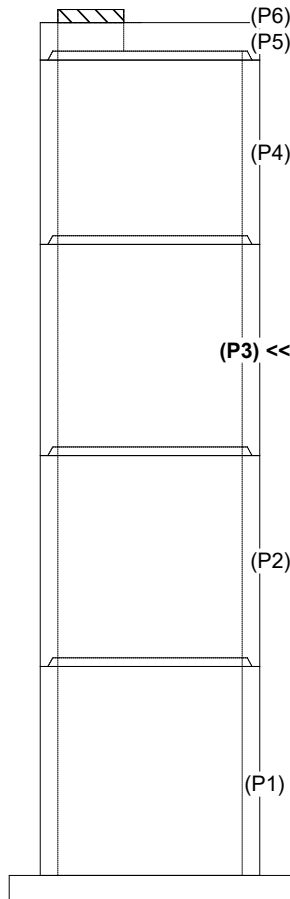

INSIDE WALL DIMENSIONS

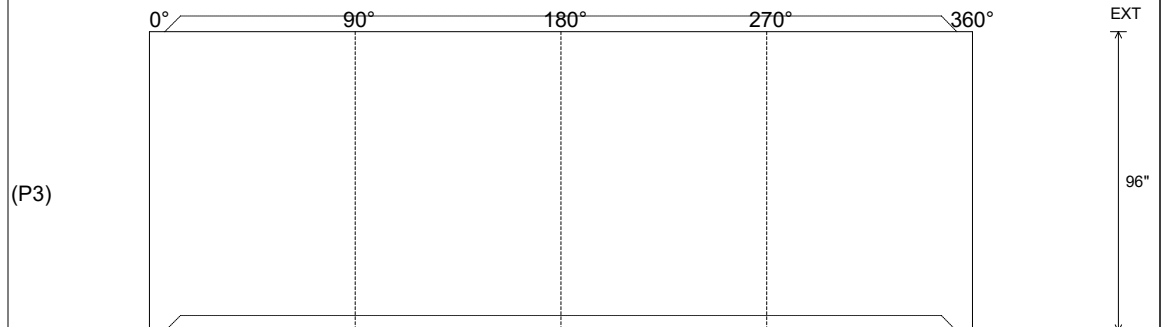

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 96" Height (Ext): 96"	Weight (Net): 18626 lb Volume (Net): 4.76cu.yd
----------------------------------	------------------------------------	--	--	---
