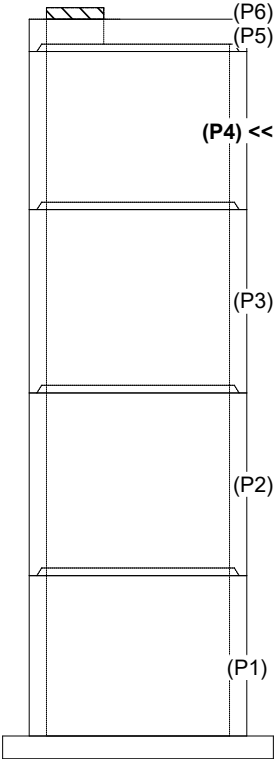

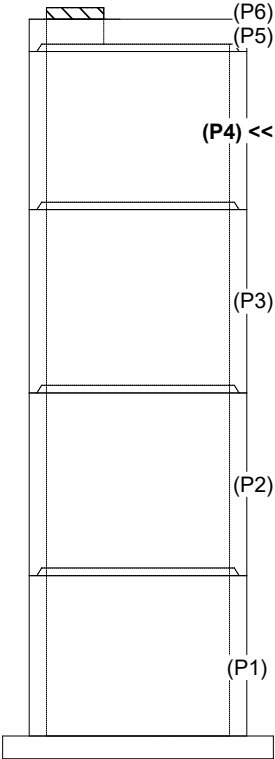
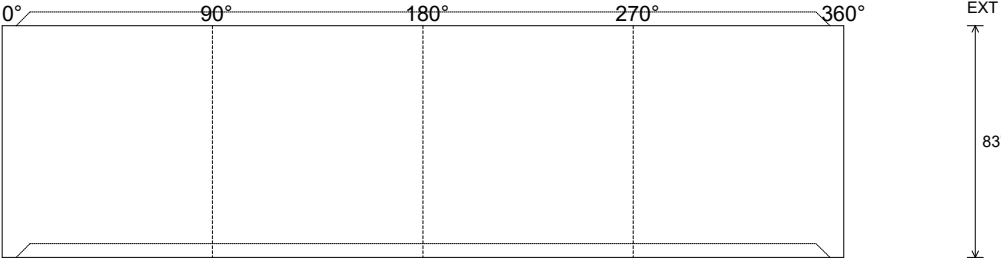


Job Name: 26-1549 Cowan St. Trunk Sewer Job Location: Nashville, TN Contractor: Garney Companies, Inc.					Plant: 100 8/24/2026 11:21:16 AM		Tech: Jared - A PC: Jay Ross Jarvis				
Structure ID: MH-6-8 SS-MH											
P4 MH096RSVFX		MH RISER Custom Ht, w/XYPEX									
P6) 30" - CASTING HEIGHT - 6" P5) 96" - MH FLAT TOP w/2X 30" Holes ECC w/XYPEX - 17" P4) 96" - MH RISER Custom Ht, w/XYPEX - 83" P3) 96" - MH RISER w/XYPEX - 96" P2) 96" - MH RISER w/XYPEX - 96" P1) 96" - MH BASE EF Cust. Ht. 12"F (14"EF =142"OD) w/XYPEX - 84" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE XYPEX C-1000 RED 1) SECONDARY POUR - EXT. FLANGE 2) CASTING - JBS 1312 F/C SANITARY 4) 96" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1840 1) A-Lok - 1040					0 lb 9502 lb 20677 lb 23915 lb 23915 lb 31801 lb 0 lb 0 lb 0 lb 0 lb 600 lb 0 lb 2 lb 1 lb		Structure Notes: . PLAN LABEL: MH-6 1. JBS 1312 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = XYPEX C-1000 RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .24) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W. 6. DOUBLE BANDS FOR BOOTS 7. ANY REQUIRED INTERIOR COATINGS TO BE SUPPLIED & APPLIED BY OTHERS. 8. **NO STEPS**				
Rim: 415.85' Rim to Invert: 31.68' Slack: 0.66" Sump: 2.5" Step Position:					Structure Total: 110413 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 9" Floor Height: 0"		Height (Int): 83" Height (Ext): 83"		Weight (Net): 20677 lb Volume (Net): 5.28cu.yd		
