

Contractor: Garney Companies, Inc.

Plant: 100



Size: 84"

Rim to Invert: 27.25'


Floor Height: 12"

Slack: 0.5"


1. JBS 1312 WT F/C SANITARY PROVIDED BY ICAT.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = XYPEX C-1000 RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .24)
 - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.
6. ANY REQUIRED INTERIOR COATINGS TO BE SUPPLIED & APPLIED BY OTHERS.
7. ****NO STEPS****

P6) 30" - CASTING HEIGHT - 6"	0 lb
P5) 84" - MH FLAT TOP w/2X 30" Holes ECC w/XYPEX - 17"	6992 lb
P4) 84" - MH RISER w/XYPEX - 96"	18626 lb
P3) 84" - MH RISER w/XYPEX - 36"	6985 lb
P2) 84" - MH RISER w/XYPEX - 96"	18626 lb
P1) 84" - MH BASE w/FLANGE (12F/14EF) w/XYPEX - 78"	24093 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) ADMIXTURE XYPEX C-1000 RED	0 lb
1) SECONDARY POUR - EXT. FLANGE	0 lb
2) CASTING - JBS 1312 WT F/C SANITARY	600 lb
4) 84" - Conseal CS-102 1.00" (Double)	0 lb
2) A-Lok - 1840	2 lb


Structure Total:	75924 lb

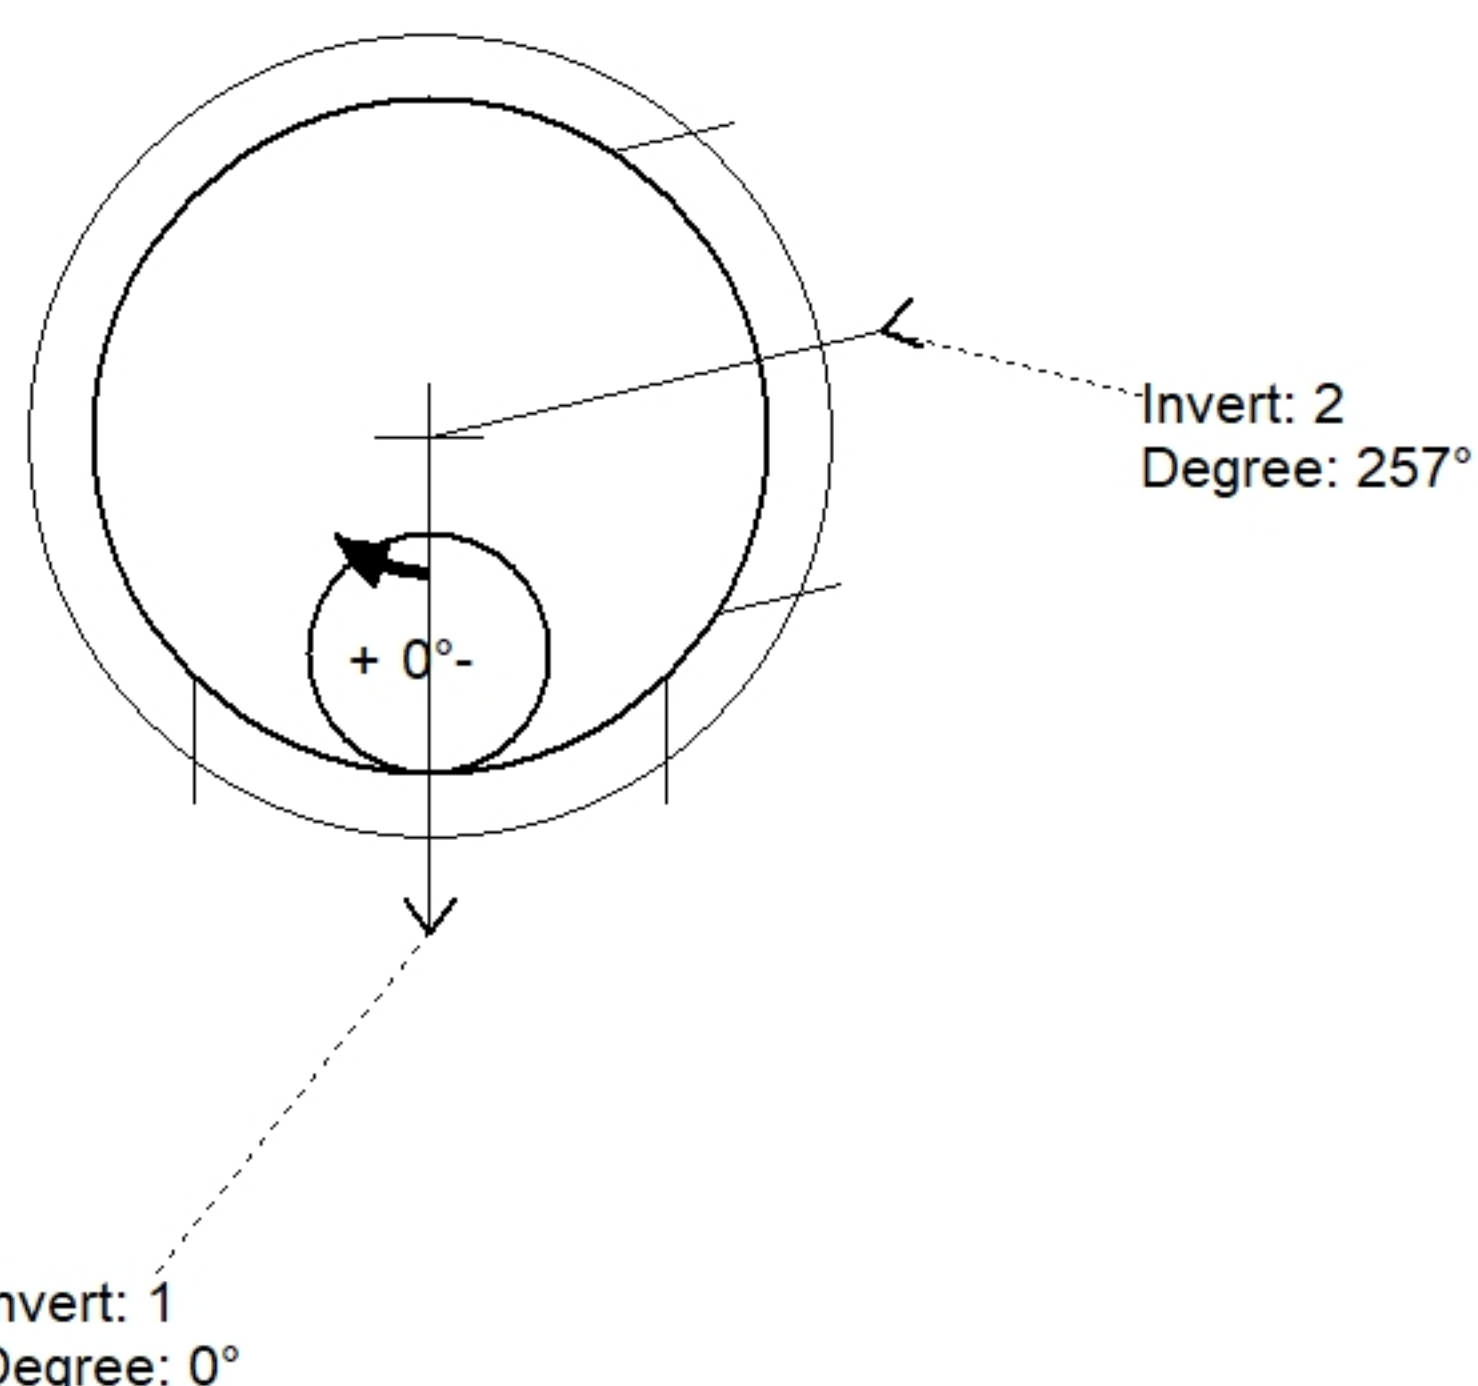

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	412.61'							
Reducer								
Invert 1	385.36'	0°	54" DI	57.5"	59"	A-Lok 1840	0"	P1
Invert 2	385.46'	257°	54" DI	57.5"	59"	A-Lok 1840	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

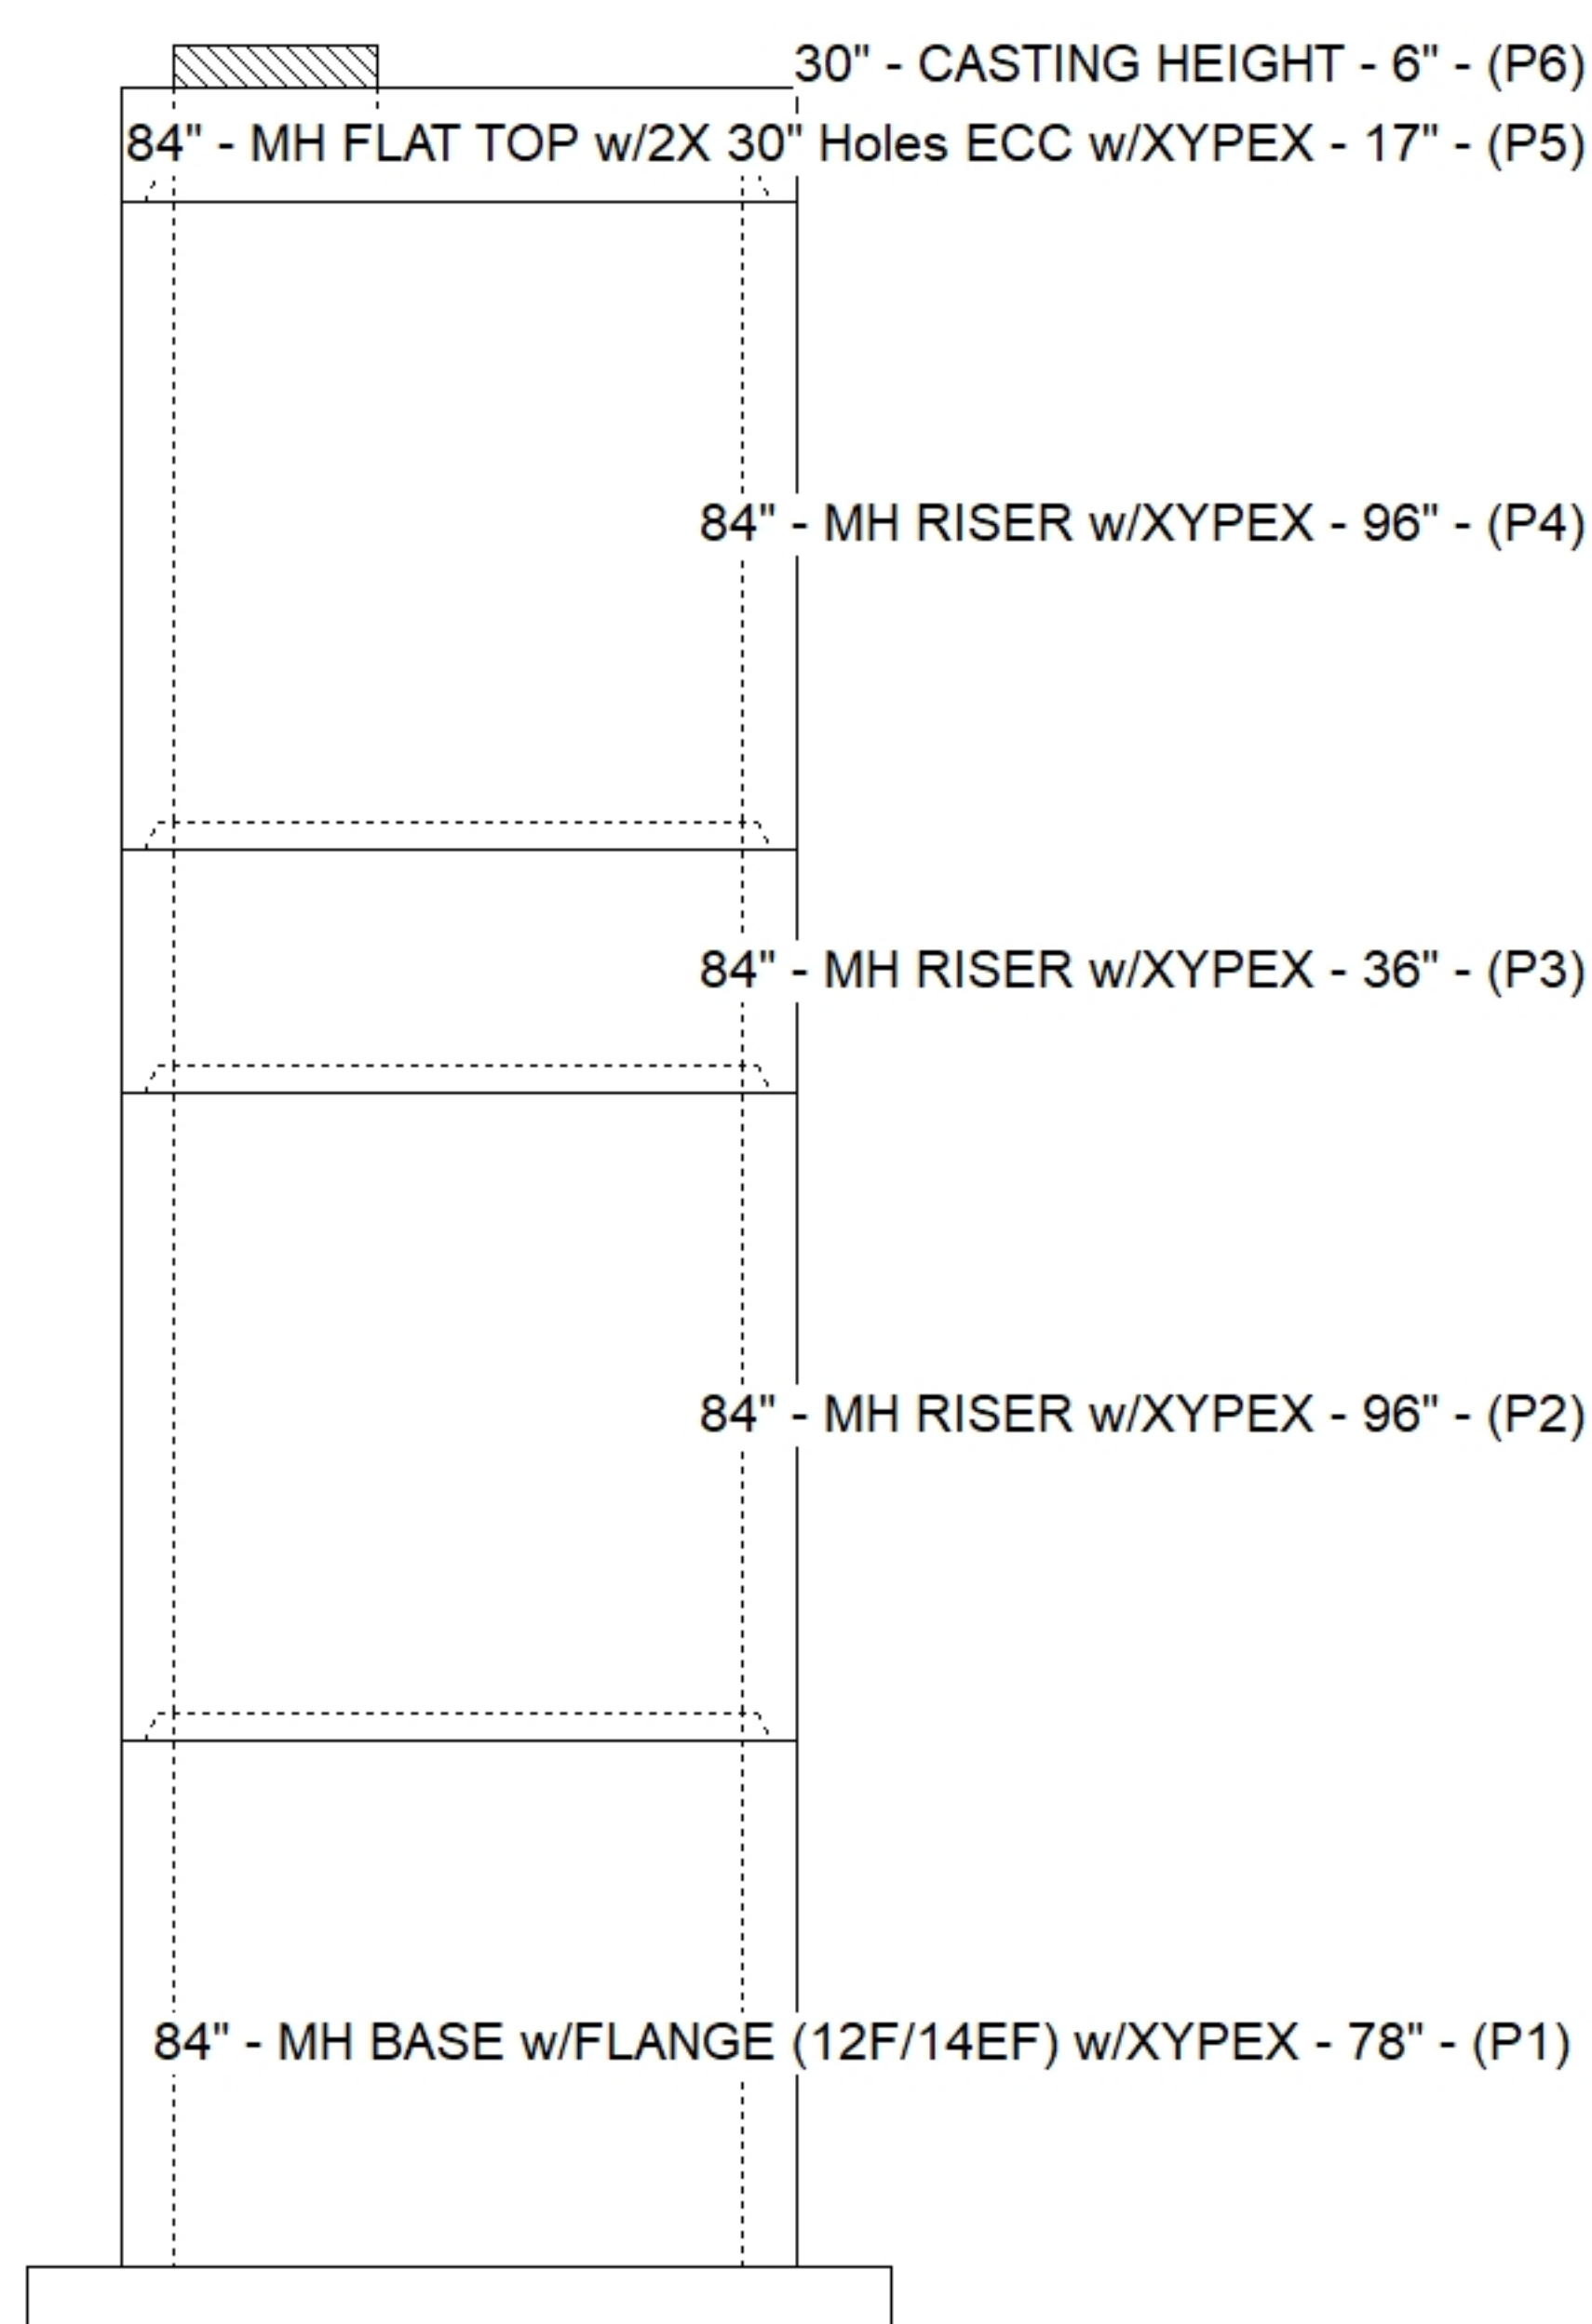

Default - Interior Dimensions

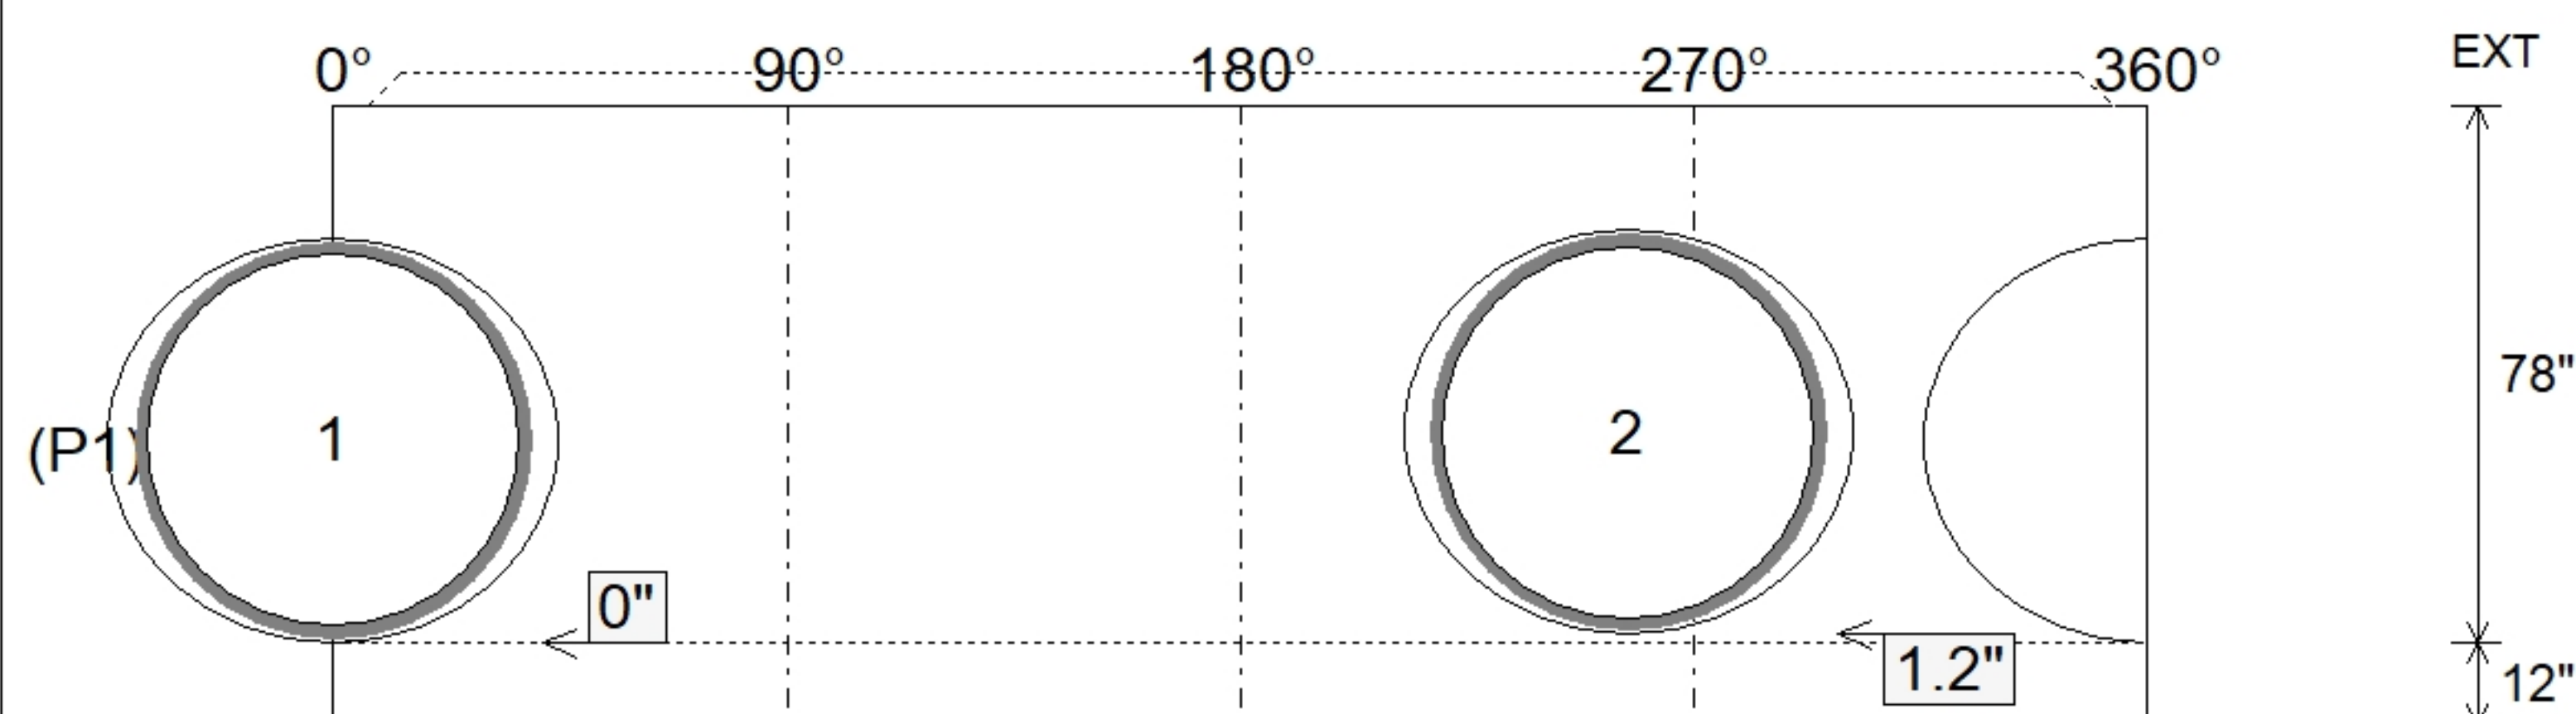

SUBMITTAL
APPROVED BY:
