

Job Name: 26-1555 - Berry Global East Parking Lot Consolidation  
 Job Location: Evansville, IN  
 Contractor: Deig Bros Lumber & Construction Co, Inc.

Plant: 100  
 4/10/2026 12:21:17 PM

Tech: Jared - F  
 PC: A. Chambers



**Structure ID: CI 101-2 ST-IN**

**P1 BX2436-08BVF**

**BOX BASE 8inW, 8inF, Variable Ht F/n**

- P3) 24" - CASTING HEIGHT - 10"
- P2) 24" x 36" - CB FLAT TOP 8"W w/24"Hole F/F - 8"
- P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 56"
- 1) CASTING - BMP SNOOT 18F w/ KIT
- 1) CASTING - HOE R-3305 TYPE 3 F/C
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 18

0 lb  
 1093 lb  
 6934 lb  
 25 lb  
 443 lb  
 0 lb  
 0 lb  
 -----  
 Structure Total: 8494 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE R-3305 TYPE 3 F/C).



REINFORCING PER ASTM A615 (GRADE 60).  
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.  
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.  
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Rim: 385.36' Rim to Invert: 3.2' Slack: 0.4" Sump: 36" Step Position:


| Position | Elev    | Angle | Ext. (cw) | Pipe     | Pipe OD | Connector | Hole | Horz Size | Up ( ) | Offset |
|----------|---------|-------|-----------|----------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | 382.16' | 75°   | 24.75"    | 12" HDPE | 14.5"   | Hole 18   | 18"  | 18.635"   | 34.75" | 4"     |
| Invert 2 |         |       |           |          |         |           |      |           |        |        |
| Invert 3 |         |       |           |          |         |           |      |           |        |        |
| Invert 4 |         |       |           |          |         |           |      |           |        |        |
| Invert 5 |         |       |           |          |         |           |      |           |        |        |
| Invert 6 |         |       |           |          |         |           |      |           |        |        |
| Invert 7 |         |       |           |          |         |           |      |           |        |        |
| Invert 8 |         |       |           |          |         |           |      |           |        |        |

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

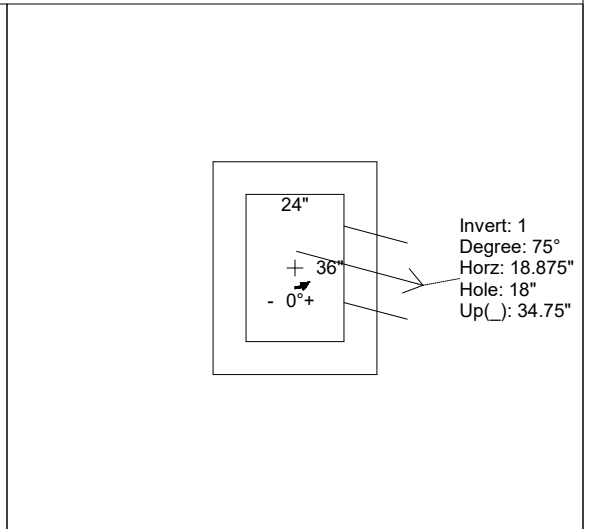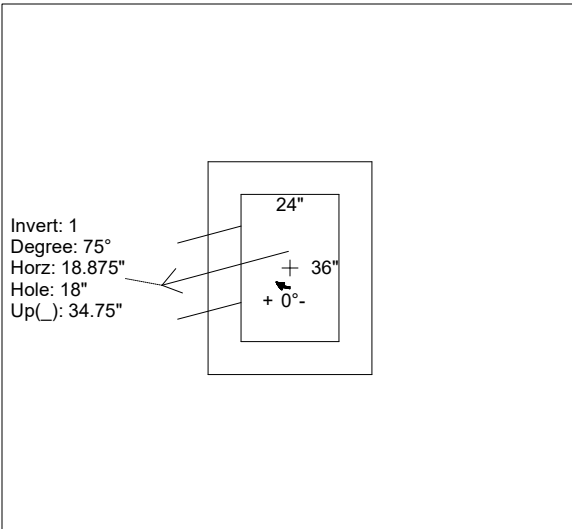

INSIDE WALL DIMENSIONS

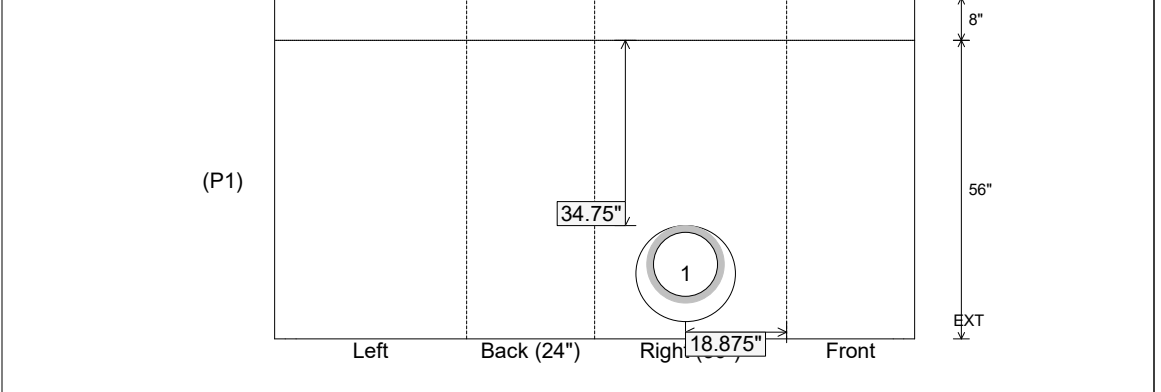

|                                  |                               |  |  |  |
|----------------------------------|-------------------------------|--|--|--|
| Coating (Int):<br>Coating (Ext): | Seam Up: Flat<br>Seam Dn: n/a | Wall Thickness: 8"<br>Floor Height: 8" | Height (Int): 56"<br>Height (Ext): 64" | Weight (Net): 6934 lb<br>Volume (Net): 1.77cu.yd |
|----------------------------------|-------------------------------|--|--|--|
